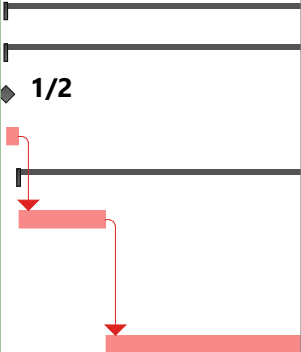




ID		Task Mode	Task Name	Duration	Start	Finish	February 2023										
							24	27	30	2	5	8	11	14	17	20	23
1			Destacamento Policial de Santana	119 days?	Wed 1/2/23	Tue 18/7/23											
2			Primer Nivel	82 days?	Wed 1/2/23	Fri 26/5/23											
3			inicio	0 days	Wed 1/2/23	Wed 1/2/23											
4			Movimiento de tierra	1 day?	Wed 1/2/23	Thu 2/2/23											
5			Hormigon Armado	37 days	Thu 2/2/23	Mon 27/3/23											
6			Hormigon Armado Zapatas	5 days	Thu 2/2/23	Thu 9/2/23											
7			Hormigon Armado Columnas	4 days	Tue 7/3/23	Mon 13/3/23											
8			Hormigon Armado Vigas y losa	10 days	Mon 13/3/23	Mon 27/3/23											
9			Muro de Bloques	18 days	Thu 9/2/23	Tue 7/3/23											
10			Terminacion de superficies	21 days	Mon 27/3/23	Tue 25/4/23											
11			Ventanas y Puertas	15 days	Tue 2/5/23	Tue 23/5/23											
12			Terminacion de Pisos y Paredes	5 days	Tue 25/4/23	Tue 2/5/23											
13			Instalaciones Electricas	58 days	Tue 7/3/23	Fri 26/5/23											
14			Canalizacion	5 days	Tue 7/3/23	Tue 14/3/23											
15			Alambrado	3 days	Tue 23/5/23	Fri 26/5/23											
16			S/C de Accesorios	2 days	Mon 15/5/23	Wed 17/5/23											
17			Instalaciones Sanitarias	21 days	Tue 7/3/23	Wed 5/4/23											
18			Acabados y pintura	8 days	Wed 3/5/23	Mon 15/5/23											
19			Miscelaneos	10 days	Tue 7/3/23	Tue 21/3/23											
20			Segundo Nivel	74 days	Tue 7/3/23	Mon 19/6/23											
21			Hormigon Armado	12 days	Fri 31/3/23	Tue 18/4/23											
22			Hormigon Armado Columnas	4 days	Fri 31/3/23	Thu 6/4/23											
23			Hormigon Armado Vigas y losa	8 days	Thu 6/4/23	Tue 18/4/23											


1/2

Project: Cronograma Santana a
Date: Mon 23/1/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	February 2023											
							24	27	30	2	5	8	11	14	17	20	23	
24			Muro de Bloques	18 days	Tue 7/3/23	Fri 31/3/23												
25			Terminacion de superficies	21 days	Tue 18/4/23	Wed 17/5/23												
26			Ventanas y Puertas	15 days	Wed 24/5/23	Wed 14/6/23												
27			Terminacion de Pisos y Paredes	5 days	Wed 17/5/23	Wed 24/5/23												
28			Instalaciones Electricas	56 days	Fri 31/3/23	Mon 19/6/23												
29			Canalizacion	5 days	Fri 31/3/23	Fri 7/4/23												
30			Alambrado	3 days	Wed 14/6/23	Mon 19/6/23												
31			S/C de Accesorios	2 days	Tue 6/6/23	Thu 8/6/23												
32			Instalaciones Sanitarias	21 days	Tue 7/3/23	Wed 5/4/23												
33			Acabados y pintura	7 days	Fri 26/5/23	Tue 6/6/23												
34			Exterior	30 days	Tue 6/6/23	Tue 18/7/23												
35			Miscelaneos Exteriore	30 days	Tue 6/6/23	Tue 18/7/23												
36			Fin del proyecto	0 days	Tue 18/7/23	Tue 18/7/23												

Project: Cronograma Santana a Date: Mon 23/1/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

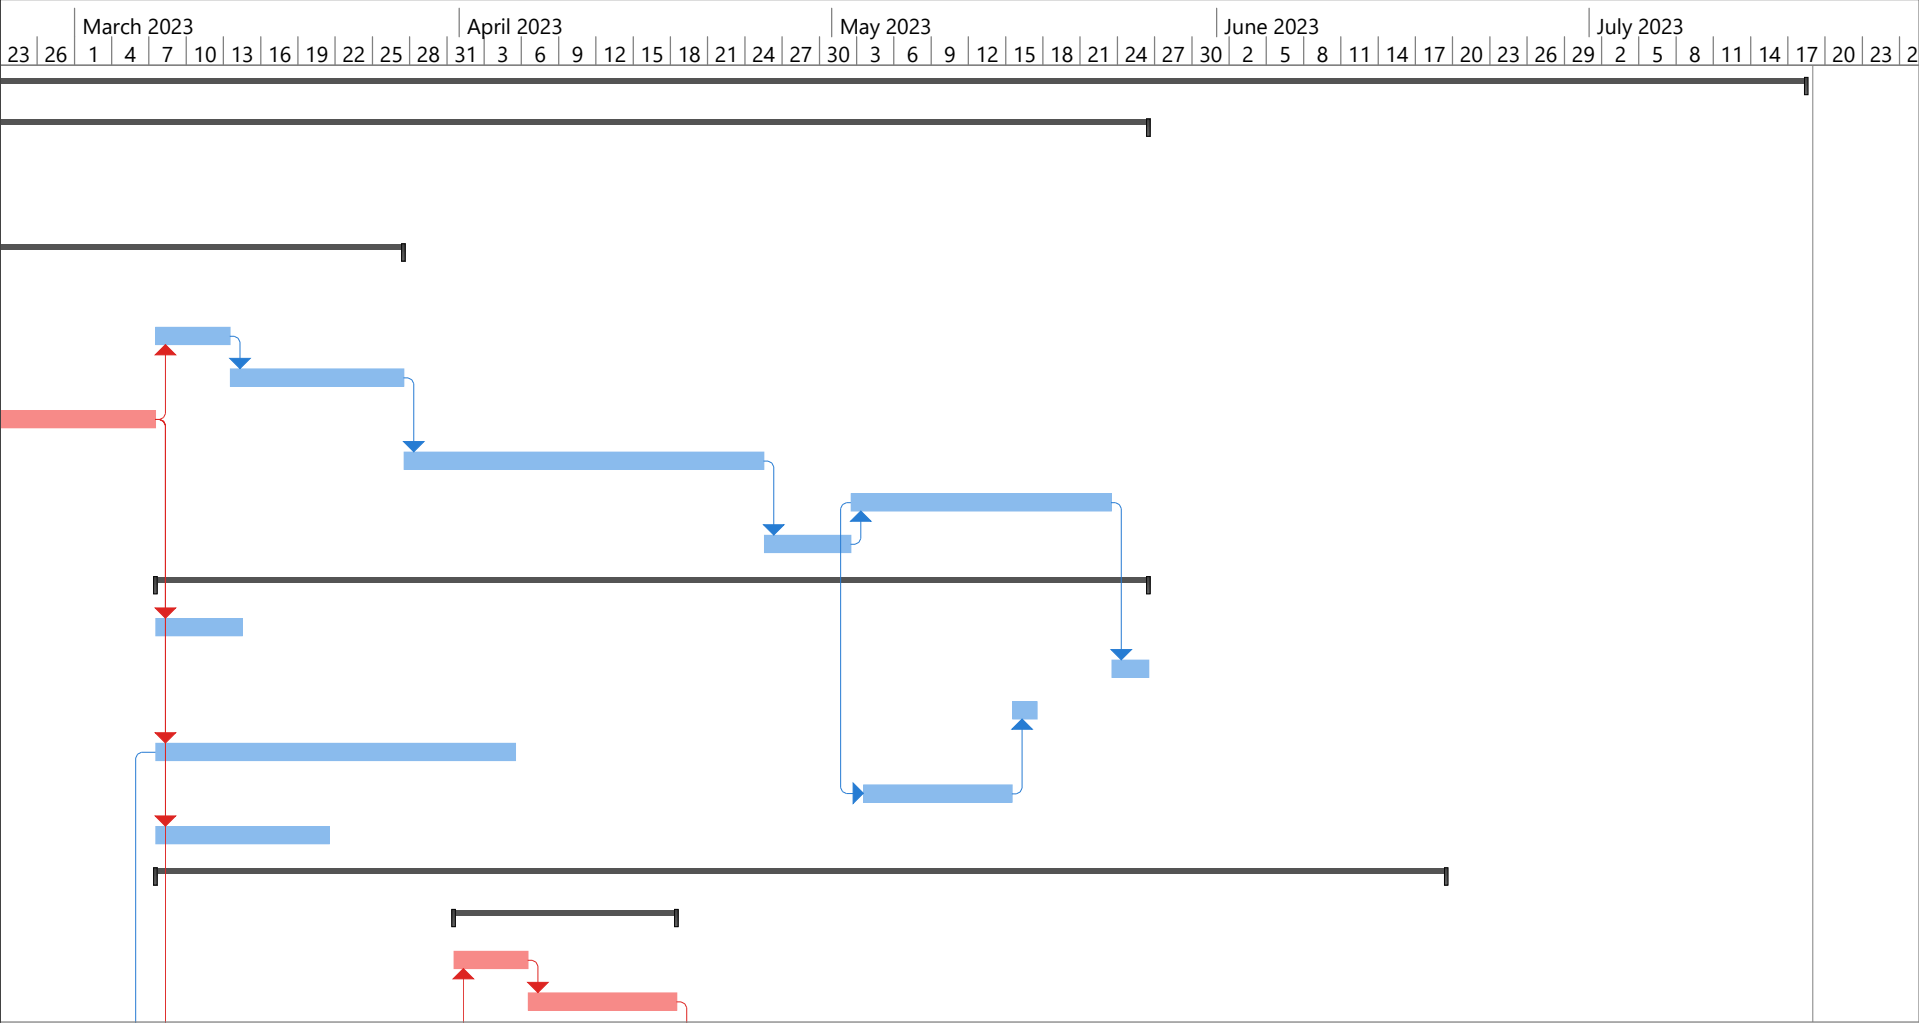

Project: Cronograma Santana a Date: Mon 23/1/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

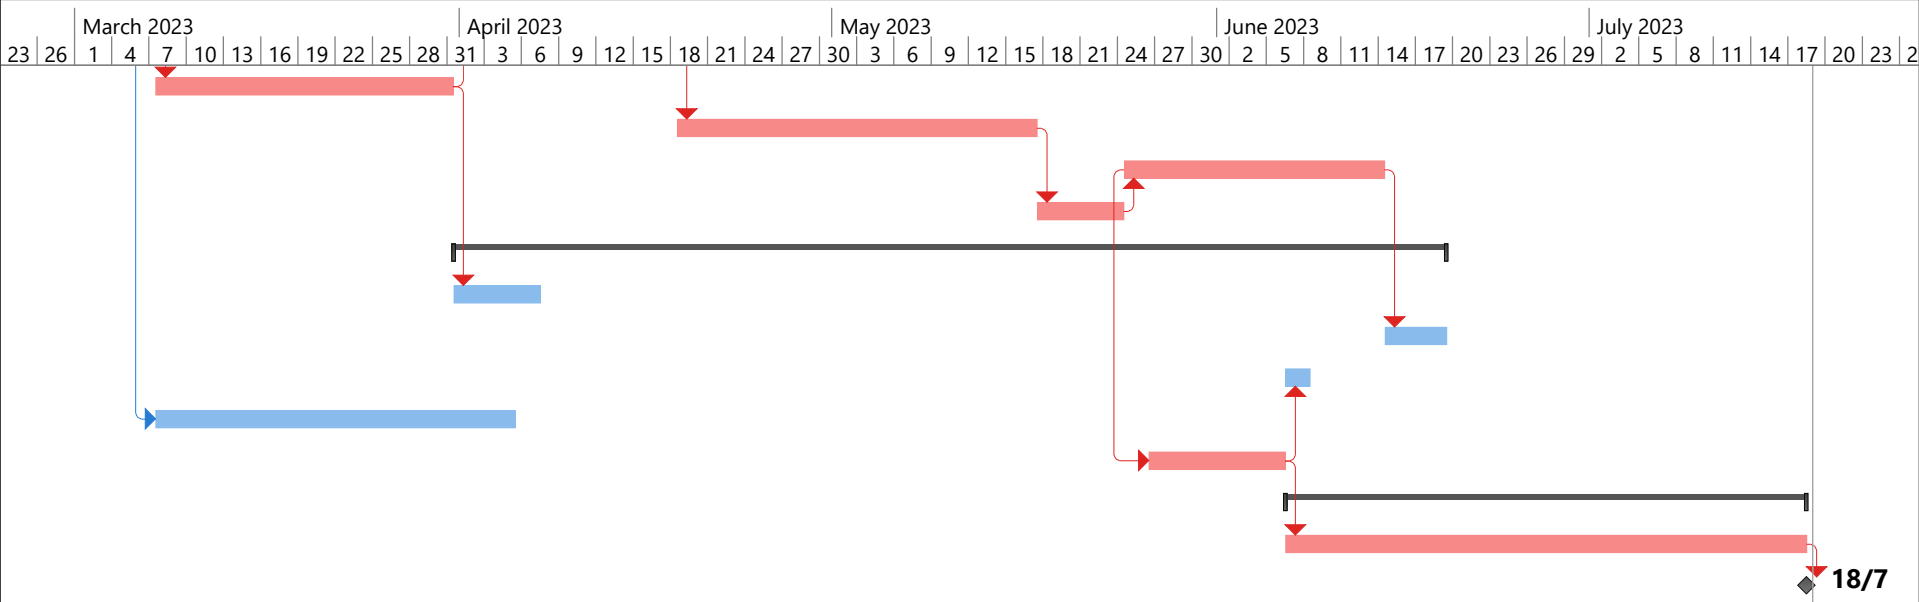

Project: Cronograma Santana a Date: Mon 23/1/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
