

Elaborado por
Ing. Jofiel Castillo

Task Name: Caseta bomba octena 1.50m x 1.70m x 2.00m
Duration: 3 days
Start: Mon 5/18/20
Finish: Wed 5/20/20
Progress: 29%

Task Name: Sum. E Instalación de Tlaco de 285 gls
Duration: 2 days
Start: Tue 5/19/20
Finish: Wed 5/20/20
Progress: 84%

Task Name: Filtrante de 10' Encamiz3 days
Duration: 3 days
Start: Thu 5/21/20
Finish: Mon 5/25/20
Progress: 79%

Task Name: Ventilación de 3" PVC
Duration: 1 day
Start: Mon 5/18/20
Finish: Mon 5/18/20
Progress: 80%

Task Name: Salida Drenaje Lavamanos (PVC)
Duration: 2 days
Start: Fri 5/22/20
Finish: Mon 5/25/20
Progress: 61%

Task Name: Salida Drenaje Inodoro 2 days
Duration: 2 days
Start: Fri 5/22/20
Finish: Mon 5/25/20
Progress: 82%

Task Name: Salida Drenaje ducha (PVC SCH-26 02")
Duration: 2 days
Start: Fri 4/17/20
Finish: Mon 4/20/20
Progress: 83%

Task Name: Base para Tlaco
Duration: 1 day
Start: Mon 5/18/20
Finish: Mon 5/18/20
Progress: 84%

Task Name: INSTALACIONES ELECTRICAS
Duration: 8 days
Start: Thu 5/21/20
Finish: Mon 6/1/20
Progress: 85%

Task Name: Salidas de luces cenitales3 days
Duration: 3 days
Start: Thu 5/21/20
Finish: Mon 5/25/20
Progress: 86%

Task Name: Salidas para bombocorrient3 days
Duration: 3 days
Start: Wed 5/27/20
Finish: Fri 5/29/20
Progress: 87%

Task Name: Salidas para bombocorrient3 days
Duration: 3 days
Start: Wed 5/27/20
Finish: Fri 5/29/20
Progress: 88%

Task Name: Salidas interruptores sim3 days
Duration: 3 days
Start: Wed 5/27/20
Finish: Fri 5/29/20
Progress: 89%

Task Name: Salidas para teléfonos 3 days
Duration: 3 days
Start: Wed 5/27/20
Finish: Fri 5/29/20
Progress: 90%

Task Name: Salidas para TV 3 days
Duration: 3 days
Start: Wed 5/27/20
Finish: Fri 5/29/20
Progress: 91%

Task Name: Salida para red de data y3 days
Duration: 3 days
Start: Wed 5/27/20
Finish: Fri 5/29/20
Progress: 92%

Task Name: Registro eléctrico 3 days
Duration: 3 days
Start: Thu 5/21/20
Finish: Mon 5/25/20
Progress: 93%

Task Name: Lámpara tipo secador en1 day
Duration: 1 day
Start: Mon 6/1/20
Finish: Mon 6/1/20
Progress: 94%

Task Name: Lámpara de techo en ext1 day
Duration: 1 day
Start: Tue 5/26/20
Finish: Tue 5/26/20
Progress: 95%

Task Name: Lámpara de pared en int1 day
Duration: 1 day
Start: Tue 5/26/20
Finish: Tue 5/26/20
Progress: 96%

Task Name: Lámpara de pared en exterior 20w
Duration: 1 day
Start: Tue 5/26/20
Finish: Tue 5/26/20
Progress: 97%

Task Name: Caja de Breakers 16 circuit3 days
Duration: 3 days
Start: Tue 5/26/20
Finish: Thu 5/28/20
Progress: 98%

Task Name: Acometida desde Transformador hasta aceros XDX de pared
Duration: 1 day
Start: Fri 5/29/20
Finish: Mon 6/1/20
Progress: 99%

Task Name: Suministro e instalación de aceros XDX de pared
Duration: 1 day
Start: Tue 5/26/20
Finish: Tue 5/26/20
Progress: 100%

Task Name: PINTURA 12 days
Duration: 12 days
Start: Tue 5/26/20
Finish: Wed 6/10/20
Progress: 102%

Task Name: Pintura Base Blanca 4 days
Duration: 4 days
Start: Mon 6/1/20
Finish: Thu 6/4/20
Progress: 103%

Task Name: Semigloss en muros interiores 1 day
Duration: 1 day
Start: Fri 6/5/20
Finish: Fri 6/5/20
Progress: 104%

Task Name: Acrilica en muros exteriores 4 days
Duration: 4 days
Start: Fri 6/5/20
Finish: Wed 6/10/20
Progress: 105%

Task Name: Economía en Techo 3 days
Duration: 3 days
Start: Tue 5/26/20
Finish: Thu 5/28/20
Progress: 106%

Task Name: Pintura mantenimiento en fierro caroles 4 days
Duration: 4 days
Start: Fri 6/5/20
Finish: Wed 6/10/20
Progress: 107%

Task Name: SEGUNDO NIVEL 22 days
Duration: 22 days
Start: Mon 5/18/20
Finish: Tue 6/16/20
Progress: 108%

Task Name: HORMIGON ARMADO EN 11 days
Duration: 11 days
Start: Mon 5/18/20
Finish: Mon 6/1/20
Progress: 109%

Task Name: Columnas de Anclaje 4 days
Duration: 4 days
Start: Mon 5/18/20
Finish: Thu 6/4/20
Progress: 110%

Task Name: Vigas O Tlaco 2.00m a 2.00m 4 days
Duration: 4 days
Start: Fri 5/22/20
Finish: Wed 5/27/20
Progress: 111%

Task Name: Cintas (0.15m x 0.20m) 1 day
Duration: 1 day
Start: Thu 5/28/20
Finish: Thu 5/28/20
Progress: 112%

Task Name: Losa de Techo (0.12m x 0.12m) 3 days
Duration: 3 days
Start: Thu 5/28/20
Finish: Mon 6/1/20
Progress: 113%

Task Name: MUROS DE BLOQUES 3 days
Duration: 3 days
Start: Tue 6/2/20
Finish: Thu 6/4/20
Progress: 114%

Task Name: Bloques Horm. 6" 036" 3 days
Duration: 3 days
Start: Tue 6/2/20
Finish: Thu 6/4/20
Progress: 115%

Task Name: Bloques Horm. 4" 036" 2 days
Duration: 2 days
Start: Tue 6/2/20
Finish: Wed 6/3/20
Progress: 116%

Task Name: Bloques Horm. 6" 036" 3 days
Duration: 3 days
Start: Tue 6/2/20
Finish: Thu 6/4/20
Progress: 117%

Task Name: Terminación de Techo 5 days
Duration: 5 days
Start: Tue 6/2/20
Finish: Mon 6/8/20
Progress: 118%

Task Name: Fino de techo plano 1 day
Duration: 1 day
Start: Wed 6/3/20
Finish: Wed 6/3/20
Progress: 119%

Task Name: Zabalita en techo 1 day
Duration: 1 day
Start: Thu 6/4/20
Finish: Thu 6/4/20
Progress: 120%

Task Name: Antepecho Terminado 1 day
Duration: 1 day
Start: Fri 6/5/20
Finish: Fri 6/5/20
Progress: 121%

Task Name: Impermeabilizante 2 days
Duration: 2 days
Start: Fri 6/5/20
Finish: Mon 6/8/20
Progress: 122%

Task Name: Manto Asfáltico Granular 2 days
Duration: 2 days
Start: Tue 6/2/20
Finish: Wed 6/3/20
Progress: 123%

Task Name: Paflete en Muros Interior 2 days
Duration: 2 days
Start: Fri 6/5/20
Finish: Mon 6/8/20
Progress: 124%

Task Name: Paflete en Muros Exterior 2 days
Duration: 2 days
Start: Fri 6/5/20
Finish: Mon 6/8/20
Progress: 125%

Task Name: Paflete en Losa de Techo 2 days
Duration: 2 days
Start: Tue 6/2/20
Finish: Wed 6/3/20
Progress: 126%

Task Name: Fregadero sobre superficie 2 days
Duration: 2 days
Start: Tue 6/2/20
Finish: Wed 6/3/20
Progress: 127%

Task Name: Cántica en general 2 days
Duration: 2 days
Start: Tue 6/2/20
Finish: Wed 6/3/20
Progress: 128%

Task Name: VENTANAS 2 days
Duration: 2 days
Start: Thu 6/11/20
Finish: Fri 6/12/20
Progress: 129%

Task Name: Ventanas Corredizas de 2 days
Duration: 2 days
Start: Thu 6/11/20
Finish: Fri 6/12/20
Progress: 130%

Task Name: PUERTAS 1 day
Duration: 1 day
Start: Thu 6/11/20
Finish: Thu 6/11/20
Progress: 131%

Task Name: Puerta PVC (0.60m x 1.50m) en Baños 1 day
Duration: 1 day
Start: Thu 6/11/20
Finish: Thu 6/11/20
Progress: 132%

Task Name: Puerta Polimetal (0.30m x 2.10m) en Baños 1 day
Duration: 1 day
Start: Thu 6/11/20
Finish: Thu 6/11/20
Progress: 133%

Task Name: TERMINACIÓN DE PISOS 4 days
Duration: 4 days
Start: Mon 6/8/20
Finish: Thu 6/11/20
Progress: 134%

Task Name: Piso en Porcelanato 2 days
Duration: 2 days
Start: Mon 6/8/20
Finish: Tue 6/9/20
Progress: 135%

Task Name: Zocalos de piso 2 days
Duration: 2 days
Start: Wed 6/10/20
Finish: Thu 6/11/20
Progress: 136%

Task Name: Importado 0.50m x 0.50m 2 days
Duration: 2 days
Start: Mon 6/8/20
Finish: Mon 6/8/20
Progress: 137%

Task Name: Cerámicas en Pared de b1 day
Duration: 1 day
Start: Mon 6/8/20
Finish: Mon 6/8/20
Progress: 138%

Task Name: Cerámicas en Pared de b1 day
Duration: 1 day
Start: Mon 6/8/20
Finish: Mon 6/8/20
Progress: 139%

Task Name: INSTALACIONES SANITARIAS 19 days
Duration: 19 days
Start: Mon 5/18/20
Finish: Thu 6/11/20
Progress: 140%

Task Name: Inodoros sanitarios 1 day
Duration: 1 day
Start: Wed 6/10/20
Finish: Wed 6/10/20
Progress: 141%


Task Name: Lavamanos Pedestal 1 day
Duration: 1 day
Start: Wed 6/10/20
Finish: Wed 6/10/20
Progress: 142%

Task Name: Original 1 day
Duration: 1 day
Start: Wed 6/10/20
Finish: Wed 6/10/20
Progress: 143%

Task Name: Ducha 1 day
Duration: 1 day
Start: Wed 6/10/20
Finish: Wed 6/10/20
Progress: 144%

Task Name: Mezcladora para lavamanos 1 day
Duration: 1 day
Start: Wed 6/10/20
Finish: Wed 6/10/20
Progress: 145%

Task Name: Set Accesorios para bañi1 day
Duration: 1 day
Start:

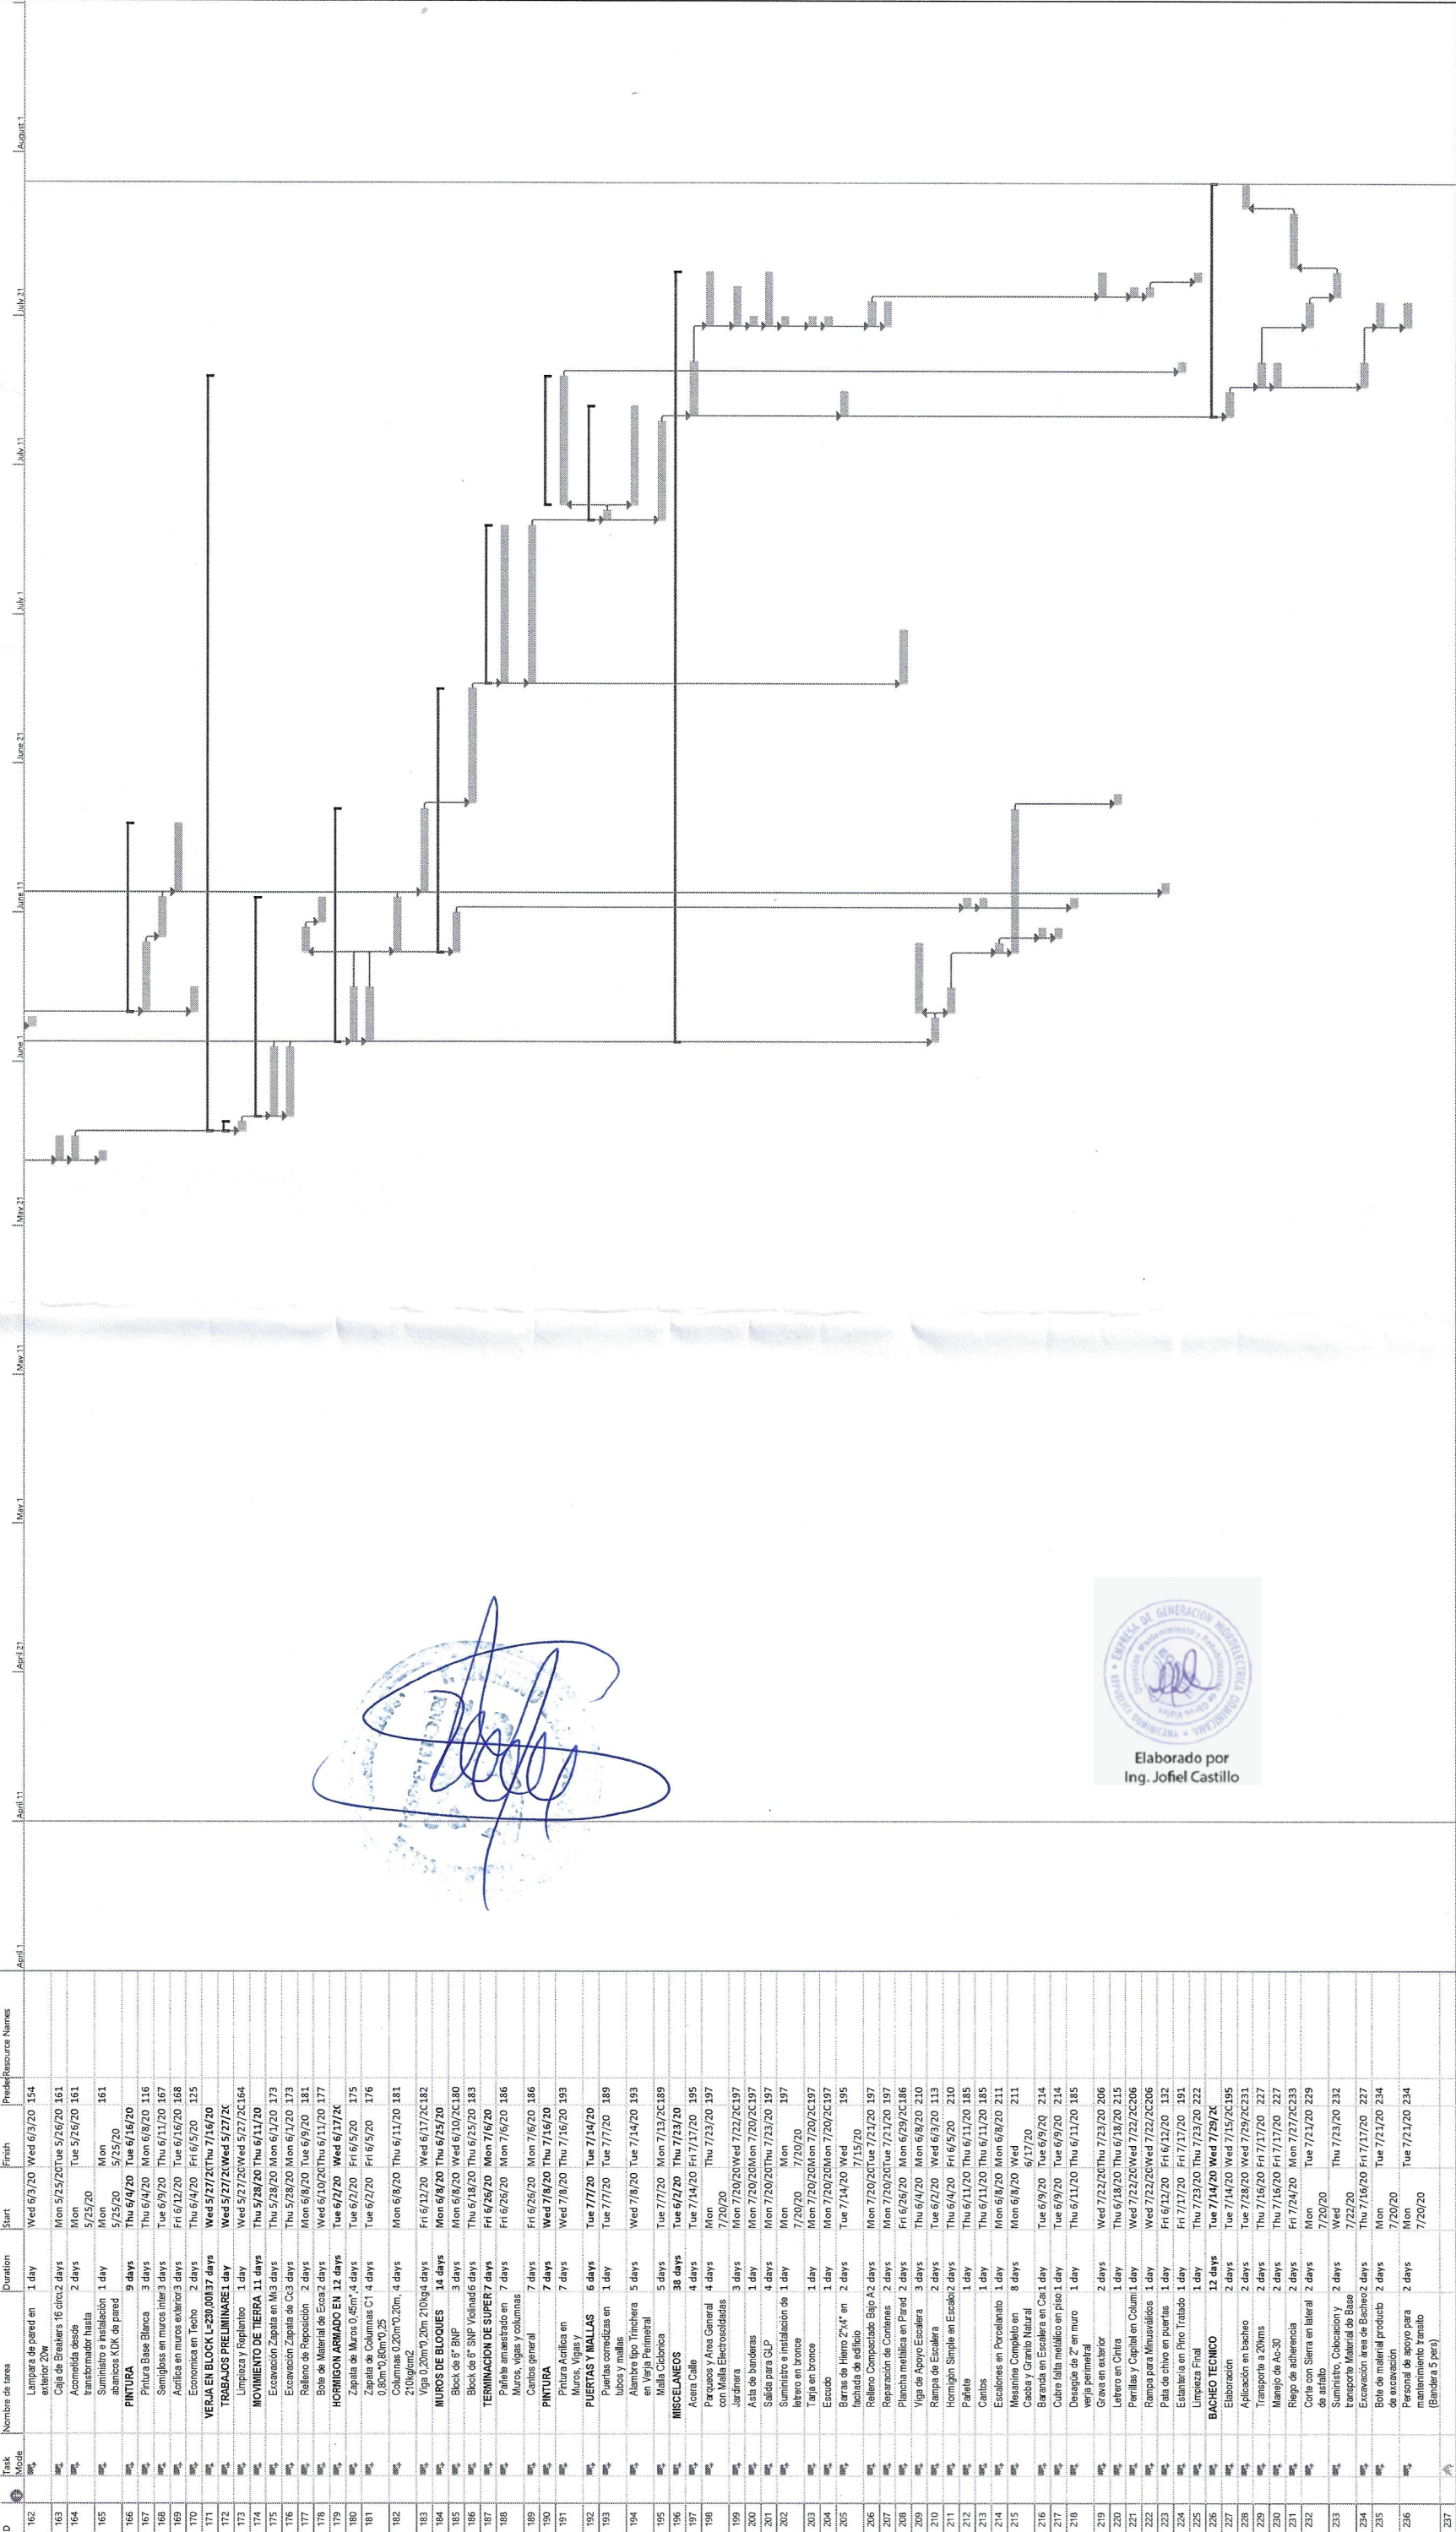




Elaborado por
Ing. Jofel Castillo
