

ID	Task/Mod	Duration	Start	Finish	Preced
1	IGLESIA SANTA LUCIA, MARTAS DE FARFAN	174.5 days	Thu 1/8/19	Wed 29/1/20	
2	IGLESIA Y AREAS ADMINISTRATIVAS	134 days	Thu 1/8/19	Wed 18/12/19	
3	PARTIDAS GENERALES	23 days	Thu 1/8/19	Sat 24/8/19	
4	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS	5 days	Thu 1/8/19	Tue 6/8/19	
5	DEMOLICIONES DE MUROS EN EL GRAN SALON	3 days	Tue 6/8/19	Fri 9/8/19	4
6	BOTE ESCOMBRO (VOLTEO DE 8 MB)	8 days	Fri 9/8/19	Sat 17/8/19	5
7	LIMPIEZA	5 days	Sat 17/8/19	Thu 22/8/19	6
8	REPLANTEO	2 days	Thu 22/8/19	Sat 24/8/19	7
9	MOVIMIENTO DE TIERRA	16 days	Sat 24/8/19	Tue 10/9/19	
10	EXCAVACION PARA MURO BLOCK DIVISORIO	4 days	Sat 24/8/19	Wed 28/8/19	8
11	RELLENO DE REPOSCION	3 days	Thu 29/8/19	Sat 31/8/19	10
12	BOTE DE MATERIAL INSERVIBLE	4 days	Sat 31/8/19	Thu 5/9/19	11
13	RELLENO COMPACTADO CALICHE	5 days	Thu 5/9/19	Tue 10/9/19	12
14	HORMIGON ARMADO EN:	10 days	Tue 10/9/19	Fri 20/9/19	
15	ZANATA DE MURO 6 DIVISORIO *	4 days	Tue 10/9/19	Sat 14/9/19	13
16	ZANATA DE COLUMNA C1	3 days	Sat 14/9/19	Tue 17/9/19	15
17	COLUMNAS PORTICO B.N.P.	3 days	Tue 17/9/19	Fri 20/9/19	16
18	HORMIGON ARMADO B.N.P.	7 days	Fri 20/9/19	Fri 27/9/19	
19	COLUMNAS PORTICO B.N.P.	4 days	Fri 20/9/19	Wed 25/9/19	17
20	VIGA DIFTEL (V0)	3 days	Wed 25/9/19	Fri 27/9/19	19
21	MUROS BLOQUES	48 days	Thu 1/8/19	Thu 19/9/19	
22	MUROS BLOQUES S/NP	1 day	Thu 1/8/19	Thu 1/8/19	
23	BLOQUES DE P3 3AT @ .80 S/NP	5 days	Sat 14/9/19	Thu 1/8/19	15
24	TERMINACION DE SUPERFICIE	24 days	Wed 25/9/19	Sat 19/10/19	
25	FRAGUACHE SOBRE HORMIGON	5 days	Wed 25/9/19	Mon 30/9/19	19
26	PANELES INTERIORES Y EXTERIORES EL 20%	8 days	Mon 30/9/19	Tue 8/10/19	25
27	CANTOS	4 days	Tue 8/10/19	Sat 12/10/19	26
28	CORNISAS EXT. DE CEMENTO EN TODO EL PERIMETRO	7 days	Sat 12/10/19	Sat 19/10/19	27
29	CORNISAS INTERIOR DE YESO TODO PERIMETRO	5 days	Sat 12/10/19	Thu 17/10/19	27
30	DIBUÑO DECORATIVO EN CORNISA ARCO	27 days	Thu 17/10/19	Thu 14/11/19	
31	EN PARTE FRONTAL DEL EDIFICIO	4 days	Thu 17/10/19	Tue 22/10/19	29
32	REVESTIMIENTO DE COLUMNAS EN MARMOL	5 days	Tue 22/10/19	Sat 26/10/19	31
33	PEDESTALES EN COLUMNAS	3 days	Sat 26/10/19	Wed 30/10/19	32
34	REVESTIMIENTO DE COLUMNAS EN PERILLA	3 days	Wed 30/10/19	Fri 1/11/19	33
35	GOTERO MAQUILADO	3 days	Sat 2/11/19	Tue 5/11/19	34
36	SUMINISTRO E INST. DE UN CRISTO EN BRONCE	5 days	Tue 5/11/19	Mon 11/11/19	35
37	TRABAJOS ARTISTICO EN EL PRENTE DEL TIEMPO	4 days	Mon 11/11/19	Thu 14/11/19	36
38	CONSTRUCCION Y TERMINACION DE TECHO:	10 days	Thu 14/11/19	Mon 25/11/19	
39	CONSTRUCCION CUPULA DEL TECHO	10 days	Thu 14/11/19	Mon 25/11/19	
40	EN TEJAS METALICA	6 days	Thu 14/11/19	Mon 25/11/19	37
41	PISO DE TECHO PLANO	4 days	Thu 14/11/19	Tue 19/11/19	37
42	TERMINACION DE TECHO EN DUREX	6 days	Tue 19/11/19	Mon 25/11/19	41
43	ZABILETAS	2 days	Tue 19/11/19	Wed 20/11/19	41
44	IMPRESIONES/ALICATES	2 days	Thu 21/11/19	Fri 22/11/19	43
45	TERMINACION DE PISO:	18 days	Thu 19/9/19	Tue 8/10/19	
46	DE CERAMICA ESPANOLA DE 1m FONDO Blanco	12 days	Thu 19/9/19	Wed 27/10/19	23
47	ZOCALO DE CERAMICA FONDO BLANCO	6 days	Wed 27/10/19	Tue 8/10/19	46
48	REVESTIMIENTO DE JARDINERAS EN LADRILLOS	5 days	Thu 19/9/19	Wed 25/9/19	23
49	LADRILLOS EN ENTRADA PUERTA PRINCIPAL	4 days	Wed 25/9/19	Sat 28/9/19	48
50	INSTALACIONES ELECTRICAS	22 days	Mon 25/11/19	Wed 18/12/19	
51	LUCES LAMPARA DECORATIVAS COLGANTES	5 days	Mon 25/11/19	Fri 29/11/19	42
52	LAMPARAS DECORATIVAS EN FRENTE DEL TEMP.	7 days	Sat 30/11/19	Sat 7/12/19	51
53	INTERRUPTORES DOBLES	4 days	Sat 7/12/19	Mon 9/12/19	52
54	INTERRUPTORES SIMPLE	4 days	Tue 10/12/19	Fri 13/12/19	53
55	TOMACORRIENTES	3 days	Fri 13/12/19	Tue 17/12/19	54
56	SUMINISTRO E INSTALACION DE LAMPARAS DE AERES ACONDICIONADOS DE 1800 BTU	3 days	Wed 27/11/19	Fri 29/11/19	58
57	PANEL DE DISTRIBUCION 12 CIRCUITOS	2 days	Mon 25/11/19	Wed 27/11/19	42
58	AMMO DE OMBIA	5 days	Mon 25/11/19	Mon 25/11/19	42

Elaborado por
Ing. Jofiel Castillo



ID	Task Title	Mod	Duration	Start	Finish	Preced
250	Rego de Impresión 0.6 g/s/m2 con Gavilla		4 days	Sat 11/1/20	Tue 16/1/20 24h	19
				4 Aug 19	11 Aug 19	16 Aug 19
				18 Aug 19	25 Aug 19	1 Sep 19
				8 Sep 19	15 Sep 19	22 Sep 19
				29 Sep 19	6 Oct 19	




Project: croco-Santa Lucia
Date: Thu 30/5/19

Task: ☐ Summary ☐ Inactive Milestone ☐ Duration only ☐ Start only ☐ External Milestone ☐ Manual Progress

Split: ☐ Inactive Summary ☐ Manual Summary ☐ Final only ☐ Duplicate


Milestone: ☐ Inactive Task ☐ Manual Task ☐ External Task ☐ Progress

Page 5

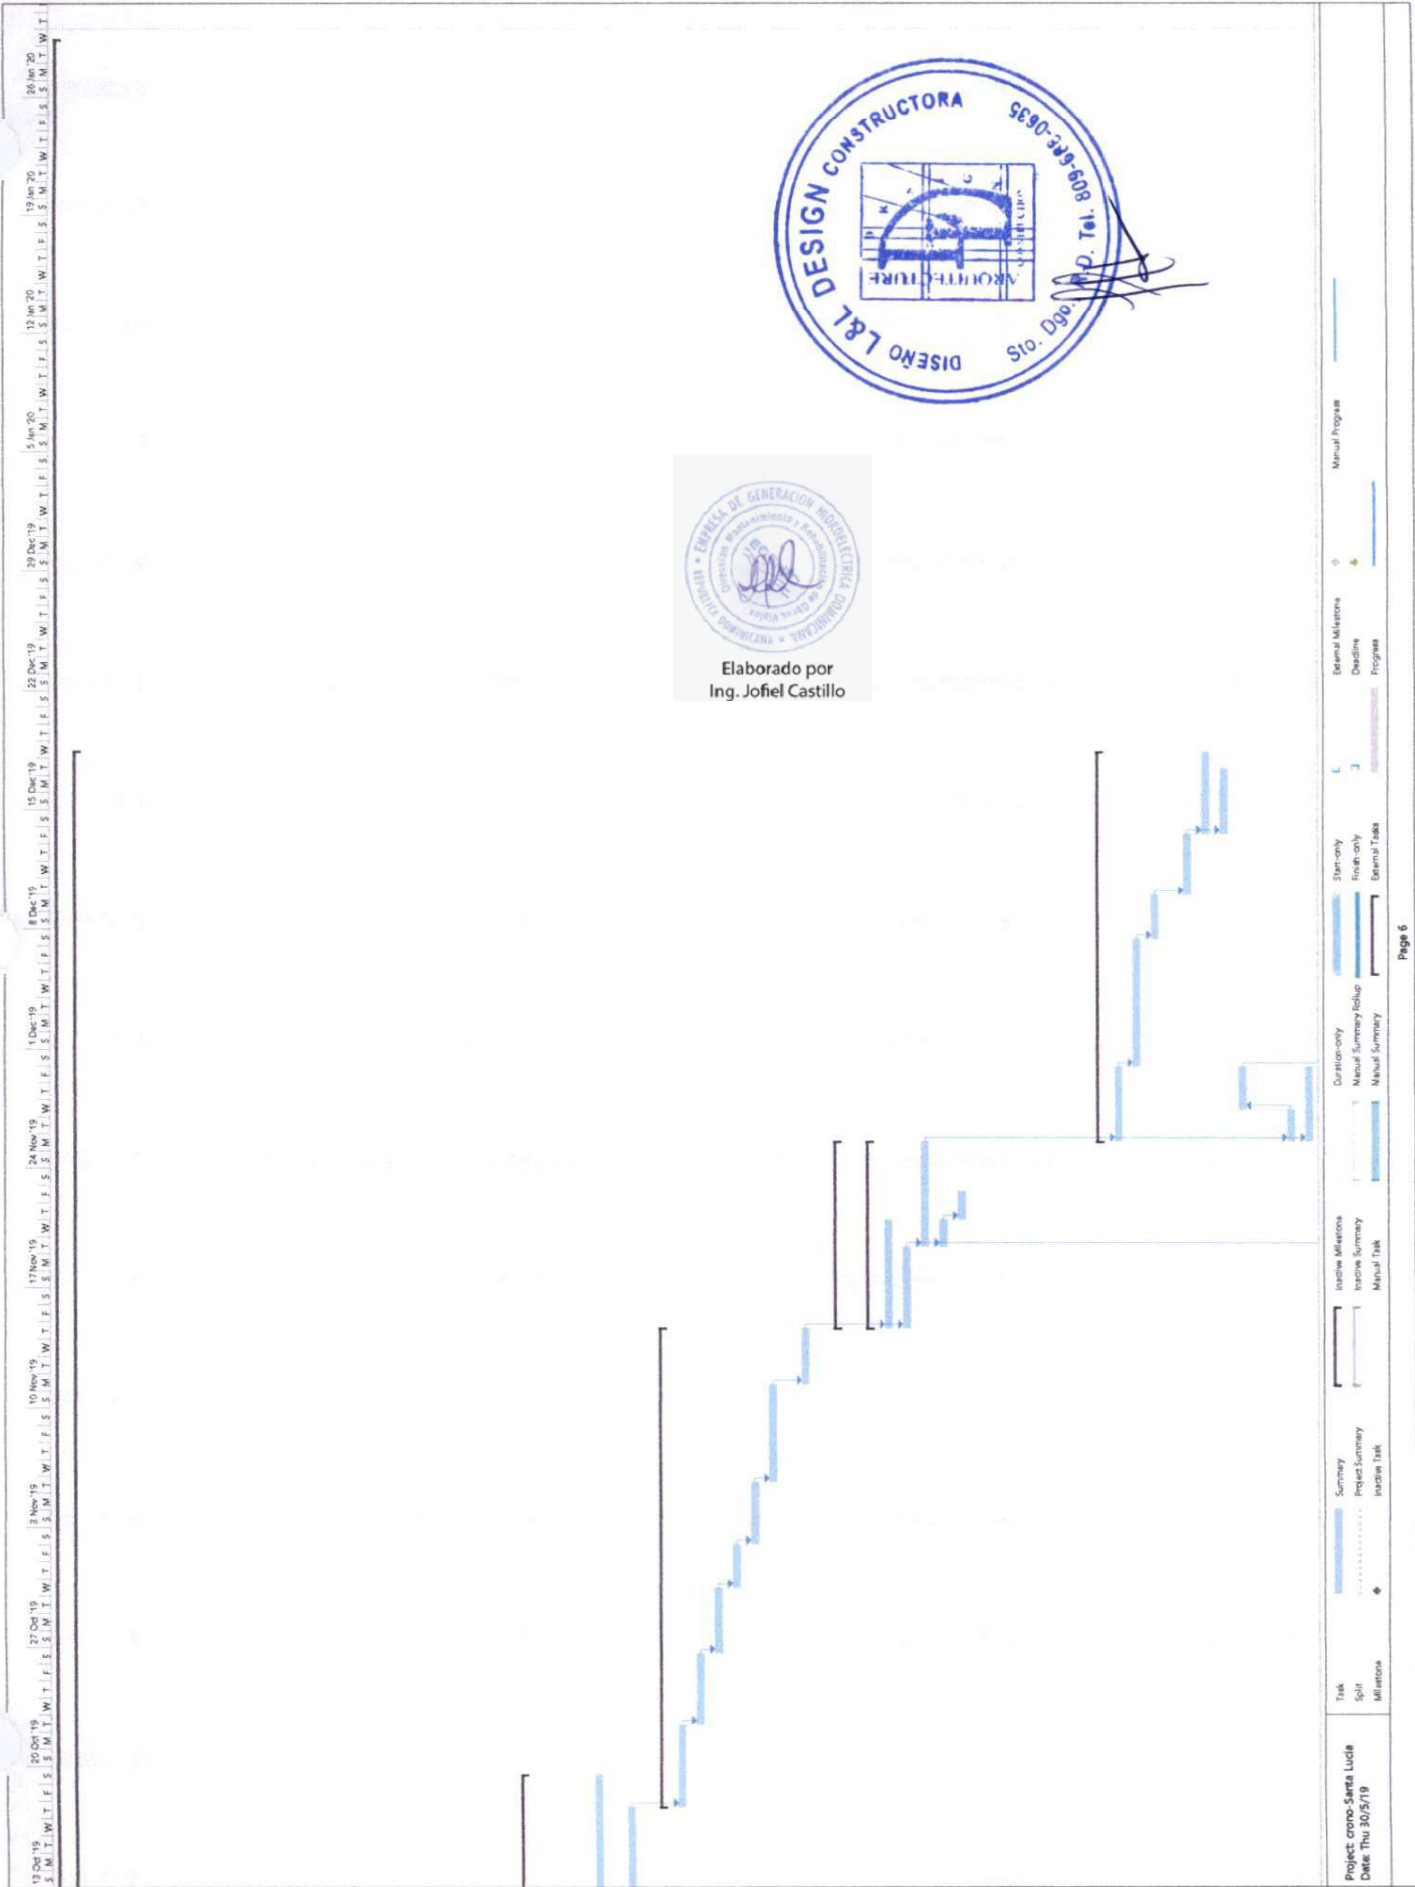


Elaborado por
Ing. Jofiel Castillo



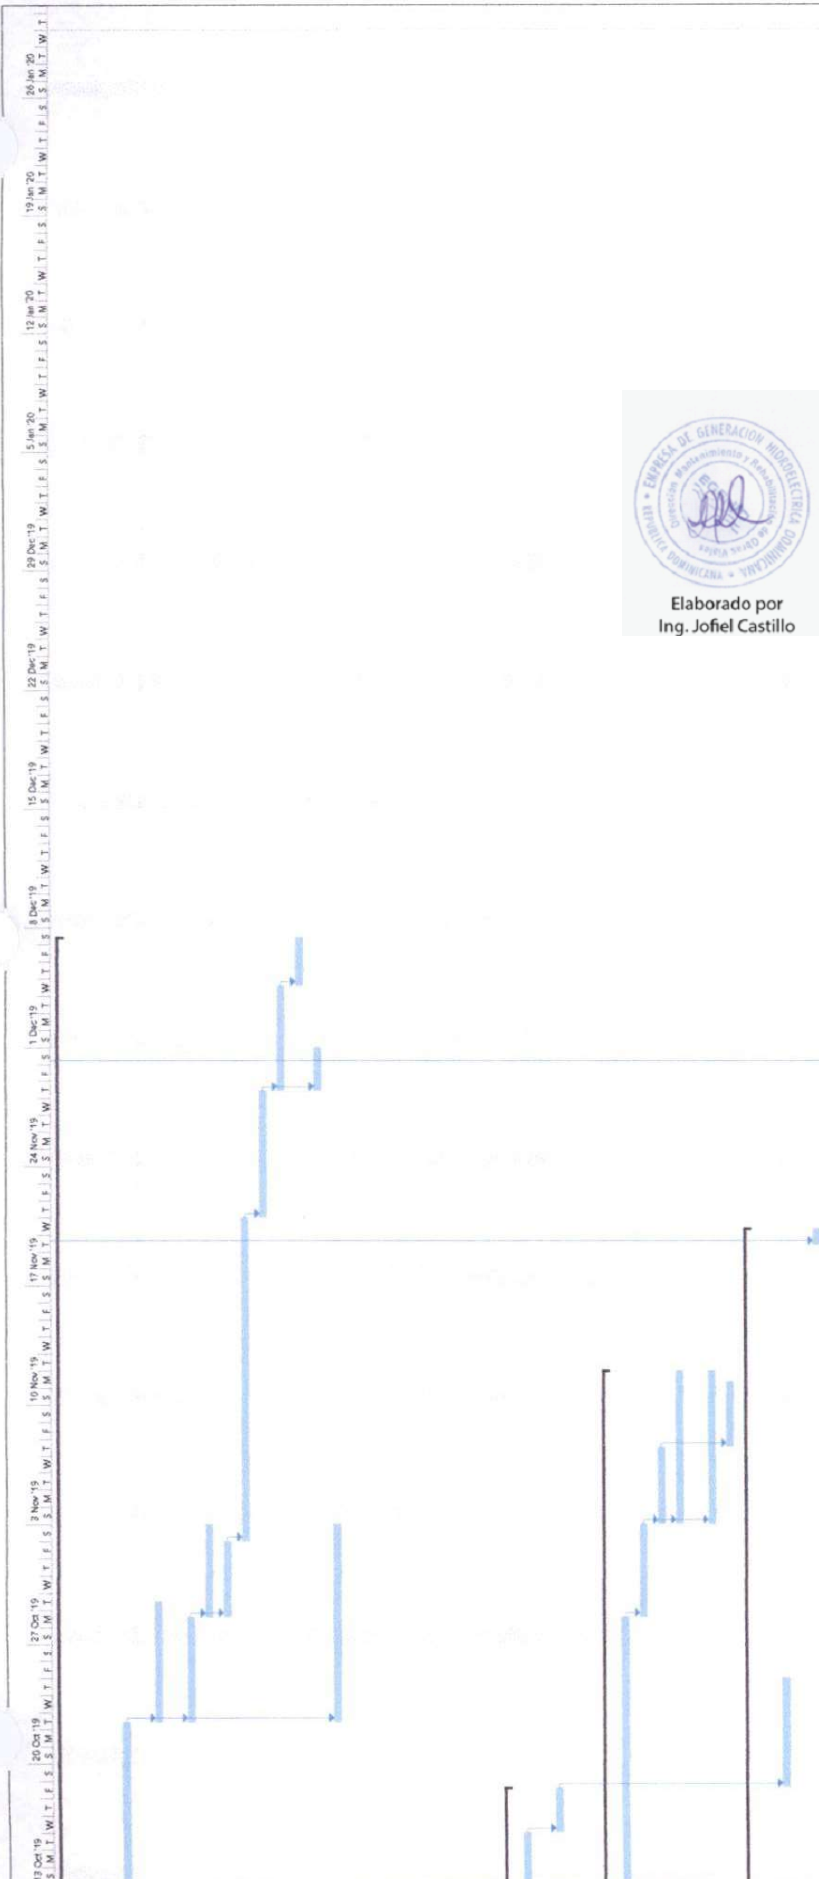

15 Oct 19 20 Oct 19 27 Oct 19 3 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dec 19 8 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

Elaborado por
Ing. Jofiel Castillo

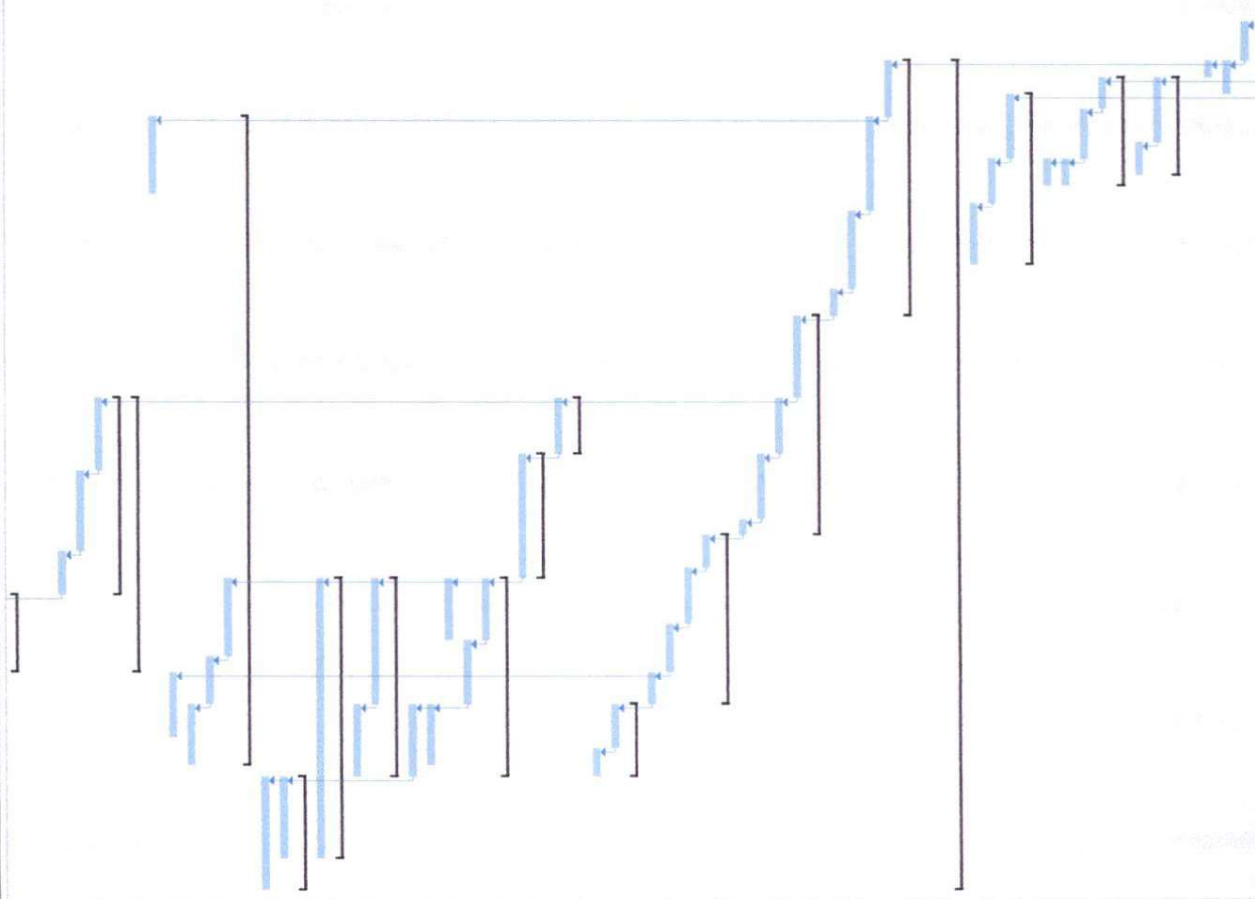

Project: cromo Santa Lucia
Date: Thu 30/5/19

- Task
- Split
- Milestone
- Summary
- Request Summary
- Insert Task
- Insert Milestone
- Insert Summary
- Manual Task
- Manual Milestone
- Manual Summary
- Start-only
- End-only
- External Task
- External Milestone
- Outline
- Project
- Manual Program

13 Oct 19 S M T T W T F S S 20 Oct 19 F S S M T T W T F S 27 Oct 19 F S S M T T W T F S 3 Nov 19 S S M T T W T F S 10 Nov 19 S M T T W T F S 17 Nov 19 F S S M T T W T F S 24 Nov 19 S S M T T W T F S 1 Dec 19 F S S M T T W T F S 8 Dec 19 F S S M T T W T F S 15 Dec 19 F S S M T T W T F S 22 Dec 19 F S S M T T W T F S 29 Dec 19 S M T T W T F S 5 Jan 20 S S M T T W T F S 12 Jan 20 F S S M T T W T F S 19 Jan 20 F S S M T T W T F S 26 Jan 20 S M T T W T F S



Elaborado por
Ing. Jofiel Castillo



Project: cagoo-Santa Lucia
 Date: Thu 30/5/19

Task

Summary

Inactive Milestone

Overlaid only

Start only

External Milestone

Manual Progress
