

ID	Task/Mod	Duration	Start	Finish	Preced
1	IGLESIA SANTA LUCIA, MARTAS DE FARFAN	174.5 days	Thu 1/8/19	Wed 29/1/20	
2	IGLESIA Y AREAS ADMINISTRATIVAS	134 days	Thu 1/8/19	Wed 18/12/19	
3	PARTIDAS GENERALES	23 days	Thu 1/8/19	Sat 24/8/19	
4	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS	5 days	Thu 1/8/19	Tue 6/8/19	
5	DEMOLICIONES DE MUROS EN EL GRAN SALON	3 days	Tue 6/8/19	Fri 9/8/19	4
6	BOTE ESCOMBRO (VOLTEO DE 8 MB)	8 days	Fri 9/8/19	Sat 17/8/19	5
7	LIMPIEZA	5 days	Sat 17/8/19	Thu 22/8/19	6
8	REPLANTEO	2 days	Thu 22/8/19	Sat 24/8/19	7
9	MOVIMIENTO DE TIERRA	16 days	Sat 24/8/19	Tue 10/9/19	
10	EXCAVACION PARA MURO BLOCK DIVISORIO	4 days	Sat 24/8/19	Wed 28/8/19	8
11	RELLENO DE REPOSICION	3 days	Thu 29/8/19	Sat 31/8/19	10
12	BOTE DE MATERIAL INSERVIBLE	4 days	Sat 31/8/19	Thu 5/9/19	11
13	RELLENO COMPACTADO CALICHE	5 days	Thu 5/9/19	Tue 10/9/19	12
14	HORMIGON ARMADO EN:	10 days	Tue 10/9/19	Fri 20/9/19	
15	ZANAYA DE MURO 6 DIVISORIO *	4 days	Tue 10/9/19	Sat 14/9/19	13
16	ZANAYA DE COLUMNA C1	3 days	Sat 14/9/19	Tue 17/9/19	15
17	COLUMNAS PORTICO B.N.P.	3 days	Tue 17/9/19	Fri 20/9/19	16
18	HORMIGON ARMADO B.N.P.	7 days	Fri 20/9/19	Fri 27/9/19	
19	COLUMNAS PORTICO B.N.P.	4 days	Fri 20/9/19	Wed 25/9/19	17
20	VIGA DAPTEL (V0)	3 days	Wed 25/9/19	Fri 27/9/19	19
21	MUROS BLOQUES	48 days	Thu 1/8/19	Thu 19/9/19	
22	MUROS BLOQUES S.NP	1 day	Thu 1/8/19	Thu 1/8/19	
23	BLOQUES DE P3 3AT @ .80 S.NP	5 days	Sat 14/9/19	Thu 1/8/19	15
24	TERMINACION DE SUPERFICIE	24 days	Wed 25/9/19	Sat 19/10/19	
25	FRAGUACHE SOBRE HORMIGON	5 days	Wed 25/9/19	Mon 30/9/19	19
26	PANELES INTERIORES Y EXTERIORES EL 20%	8 days	Mon 30/9/19	Tue 8/10/19	25
27	CANTOS	4 days	Tue 8/10/19	Sat 12/10/19	26
28	CORNISAS EXT. DE CEMENTO EN TODO EL PERIMETRO	7 days	Sat 12/10/19	Sat 19/10/19	27
29	CORNISAS INTERIOR DE YESO TODO PERIMETRO	5 days	Sat 12/10/19	Thu 17/10/19	27
30	DIBUÑO DECORATIVO EN CORNISA ARCO	27 days	Thu 17/10/19	Thu 14/11/19	
31	EN PARTE FRONTAL DEL EDIFICIO	4 days	Thu 17/10/19	Tue 22/10/19	29
32	REVESTIMIENTO DE COLUMNAS EN MARMOL	5 days	Tue 22/10/19	Sat 26/10/19	31
33	PEDESTALES EN COLUMNAS	3 days	Sat 26/10/19	Wed 30/10/19	32
34	REVESTIMIENTO DE COLUMNAS EN PERILLA	3 days	Wed 30/10/19	Fri 1/11/19	33
35	GOTERO MAQUILAGO	3 days	Sat 2/11/19	Tue 5/11/19	34
36	SUMINISTRO E INST. DE UN CRISTO EN BRONCE	5 days	Tue 5/11/19	Mon 11/11/19	35
37	TRABAJOS ARTISTICO EN EL PRENTE DEL TIEMPO	4 days	Mon 11/11/19	Thu 14/11/19	36
38	CONSTRUCCION Y TERMINACION DE DE TECHO:	10 days	Thu 14/11/19	Mon 25/11/19	
39	CONSTRUCCION CUPULA DEL TECHO	10 days	Thu 14/11/19	Mon 25/11/19	
40	EN TEGAS METALICA	6 days	Thu 14/11/19	Mon 25/11/19	37
41	PISO DE TECHO PLANO	4 days	Thu 14/11/19	Tue 19/11/19	37
42	TERMINACION DE DE TECHO EN DUKOK	6 days	Tue 19/11/19	Mon 25/11/19	41
43	ZABILETAS	2 days	Tue 19/11/19	Wed 20/11/19	41
44	IMPRESIONES/ALICATILES	2 days	Thu 21/11/19	Fri 22/11/19	43
45	TERMINACION DE PISO:	18 days	Thu 19/9/19	Tue 8/10/19	
46	DE CERAMICA ESPANOLA DE 1m FONDO Blanco	12 days	Thu 19/9/19	Wed 27/10/19	23
47	ZOCALO DE CERAMICA FONDO BLANCO	6 days	Wed 27/10/19	Tue 8/10/19	46
48	REVESTIMIENTO DE JARDINERAS EN LADRILLOS	5 days	Thu 19/9/19	Wed 25/9/19	23
49	LADRILLOS EN ENTRADA PUERTA PRINCIPAL	4 days	Wed 25/9/19	Sat 28/9/19	48
50	INSTALACIONES ELECTRICAS	22 days	Mon 25/11/19	Wed 18/12/19	
51	LUCES LAMPARA DECORATIVAS COLGANTES	5 days	Mon 25/11/19	Fri 29/11/19	42
52	LAMPARAS DECORATIVAS EN FREITE DEL TEMP.	7 days	Sat 30/11/19	Sat 7/12/19	51
53	INTERRUPTORES DOBLES	4 days	Tue 10/12/19	Fri 13/12/19	53
54	INTERRUPTORES SIMPLE	4 days	Fri 13/12/19	Wed 18/12/19	54
55	TOMACORRIENTES	3 days	Fri 13/12/19	Tue 17/12/19	54
56	SUMINISTRO E INSTALACION DE LAMPARAS DE AERES ACONDICIONADOS DE 1800 BTU	3 days	Wed 27/11/19	Fri 29/11/19	58
57	PANEL DE DISTRIBUCION 12 CIRCUITOS	2 days	Mon 25/11/19	Wed 27/11/19	42
58	AMMO DE OMBIA	5 days	Mon 25/11/19	Mon 25/11/19	42

Elaborado por
Ing. Jofiel Castillo



ID	Task Title	Mod	Duration	Start	Finish	Preld
60	PORTAJE Y ESTANTERIA TODO CACABA Y METALICAS		67 days	Sat 28/9/19	Sat 7/12/19	
61	PASAMAYOS BARANDAS EN MESANINE DEL CAMPAMARO DE 18 Y 148 PULO		12 days	Sat 28/9/19	Fri 11/10/19	49
62	PASAMAYOS DE 87 PULO PARA DIVOR EL ALTAR		10 days	Fri 11/10/19	Tue 22/10/19	61
63	SUMINISTRO E INSTAL DE PUERTAS NUEVAS EN CACABA		7 days	Tue 22/10/19	Tue 29/10/19	62
64	REPARACION PUERTAS PRINCIPALES TEMPLO		6 days	Tue 22/10/19	Mon 28/10/19	62
65	REPARACION DE PUERTAS		6 days	Mon 28/10/19	Sat 2/11/19	64
66	REPARACION DE BANCOS INCLUYE PINTURA		5 days	Mon 28/10/19	Fri 1/11/19	64
67	REPARACION DE UN JUEGO DE COMEDOR		18 days	Sat 2/11/19	Wed 20/11/19	66
68	REPARACION DE ARMARIOS GRANDES		7 days	Thu 21/11/19	Thu 28/11/19	67
69	REPARACION DE ESTANTES GRANDES		6 days	Thu 28/11/19	Wed 4/12/19	68
70	REPARACION DE BUTACAS		3 days	Wed 4/12/19	Sat 7/12/19	69
71	REPARACION DE BOYACAS		3 days	Tue 28/11/19	Sat 30/11/19	68
72	REPARACION DE PANELES TRAGALUZ		12 days	Tue 28/11/19	Sat 2/12/19	62
73	REPAR. VITRINA DE LA VIRGEN STA. LUCIA		4 days	Sat 28/9/19	Thu 3/10/19	49
74	REPAR. VITRINA DE LA VIRGEN ALTAGRACA		2 days	Thu 3/10/19	Fri 4/10/19	73
75	REPARACION VENTANILLAS DE ARRIBA EN EL TEMPLO		2 days	Sat 5/10/19	Mon 7/10/19	74
76	REPARACION ENTABILLADO CON CRISTAL		2 days	Mon 7/10/19	Wed 9/10/19	75
77	CONSTRUCCION GABINETES Y DEPENSA EN COCINA		5 days	Sat 28/9/19	Fri 4/10/19	49
78	SUMINISTRO E INSTAL DE PUERTAS METALICAS APARMEJADO		4 days	Sat 28/9/19	Thu 3/10/19	49
79	VENTANAS		6 days	Sat 12/10/19	Fri 18/10/19	
80	VENTANAS REFORZADAS CORREDIZAS DE ALUMINO Y VIDRIO EN TEMPLO		3 days	Sat 12/10/19	Tue 15/10/19	27
81	VENTANAS REFORZADAS CORREDIZAS DE ALUMINO Y VIDRIO EN AREAS ADMINISTRATIVAS		3 days	Tue 12/10/19	Fri 18/10/19	80
82	PINTURAS		29 days	Sat 12/10/19	Mon 11/11/19	
83	RENOCCION DE PINTURA EXISTENTE		15 days	Sat 12/10/19	Mon 28/10/19	127
84	MASILLADO Y RELLENO DE SUPERFICIE		6 days	Mon 28/10/19	Sat 2/11/19	83
85	ACRILICA ESPECIAL EN TECHO		4 days	Sat 2/11/19	Thu 7/11/19	84
86	ACRILICA ESPECIAL EN PAREDES EXTERIOR INTERIOR		8 days	Sat 2/11/19	Mon 11/11/19	84
87	UTILIZACION DE OONDOLA		8 days	Sat 2/11/19	Mon 11/11/19	84
88	MANTENIMIENTO EN PUERTAS		3 days	Thu 7/11/19	Mon 11/11/19	85
89	VARROS		50 days	Sat 28/9/19	Wed 30/11/19	
90	ACERA PERIMETRAL		4 days	Sat 28/9/19	Thu 3/10/19	49
91	PROTECCION DE VENTANAS Y PUERTAS HERRIO		6 days	Fri 18/10/19	Thu 24/10/19	81
92	CANALERA PARA DESAGUE DE TECHOEN PVC		1 day	Tue 19/11/19	Wed 20/11/19	1141
93	SIEMBRA DE GRAMAS Y FLORES		3 days	Thu 3/10/19	Sat 5/10/19	90
94	LIMPIEZA Y PINTURA CAMPAMARO		3 days	Sat 5/10/19	Wed 9/10/19	93
95	LIMPIEZA FINAL		2 days	Wed 9/10/19	Fri 11/10/19	94
96	CONSTRUCCION AREA DE BAÑO EXTERIOR		118 days	Tue 6/11/19	Fri 6/12/19	
97	PANTARRAS GENERALES		11 days	Tue 6/11/19	Sat 17/11/19	
98	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS Y MUROS		3 days	Tue 6/11/19	Fri 9/11/19	4
99	BOITE ESCOMBRO		4 days	Fri 9/11/19	Tue 13/11/19	98
100	LIMPIEZA		4 days	Tue 13/11/19	Sat 17/11/19	99
101	MOVIMIENTO DE TIERRA		9 days	Sat 17/11/19	Tue 27/11/19	
102	EXCAVACION PARA MURO BLOCK DIVORSO		2 days	Sat 17/11/19	Mon 19/11/19	100
103	RELLENO DE REPOSICION		2 days	Tue 20/11/19	Wed 21/11/19	102
104	BOITE DE MATERIAL INSEPARABLE		3 days	Wed 21/11/19	Sat 24/11/19	103
105	RELLENO COMPACTADO CALICHE		2 days	Sat 24/11/19	Tue 27/11/19	104
106	HORMION ARMADO EN:		4 days	Tue 27/11/19	Fri 30/11/19	
107	ZAPATA DE COLUMNA C1		2 days	Tue 27/11/19	Wed 28/11/19	105
108	COLUMNAS PORTICO EN P		2 days	Thu 29/11/19	Fri 30/11/19	107
109	HORMION ARMADO IMP EN:		9 days	Fri 30/11/19	Mon 9/12/19	
110	COLUMNAS PORTICO S.N.P		2 days	Mon 2/12/19	Wed 4/12/19	108
111	VIGA DUNTEL (V2)		2 days	Mon 2/12/19	Wed 4/12/19	110
112	VIGA DE CARGA		2 days	Mon 2/12/19	Wed 4/12/19	110
113	LOSAS Y VUELOS		5 days	Wed 4/12/19	Mon 9/12/19	112
114	MUROS BLOQUES		2 days	Tue 20/11/19	Wed 21/11/19	
115	BLOQUES DE F3 SFC @ 80 S/M		2 days	Tue 20/11/19	Wed 21/11/19	102
116	TERMINACION DE SUPERFICIE		7 days	Wed 21/11/19	Wed 28/11/19	
117	PRAQUICHE SOBRE HORMION		2 days	Wed 21/11/19	Fri 23/11/19	115

Elaborado por
Ing. Jofiel Castillo

9690-509-608 Tel. 015
DISEÑO L&L DESIGN CONSTRUCTORA
ARCHITECTURE

PROYECTO: PROYECTO SANTA LUCIA
FECHA: 30/05/19

Manual Program

External Milestone

Deadline

Progress

Start only

Final only

External Task

Custom only

Manual Summary Setup

Manual Summary

Inactive Milestone


Project Summary

Inactive Task

Task

Split

Milestone

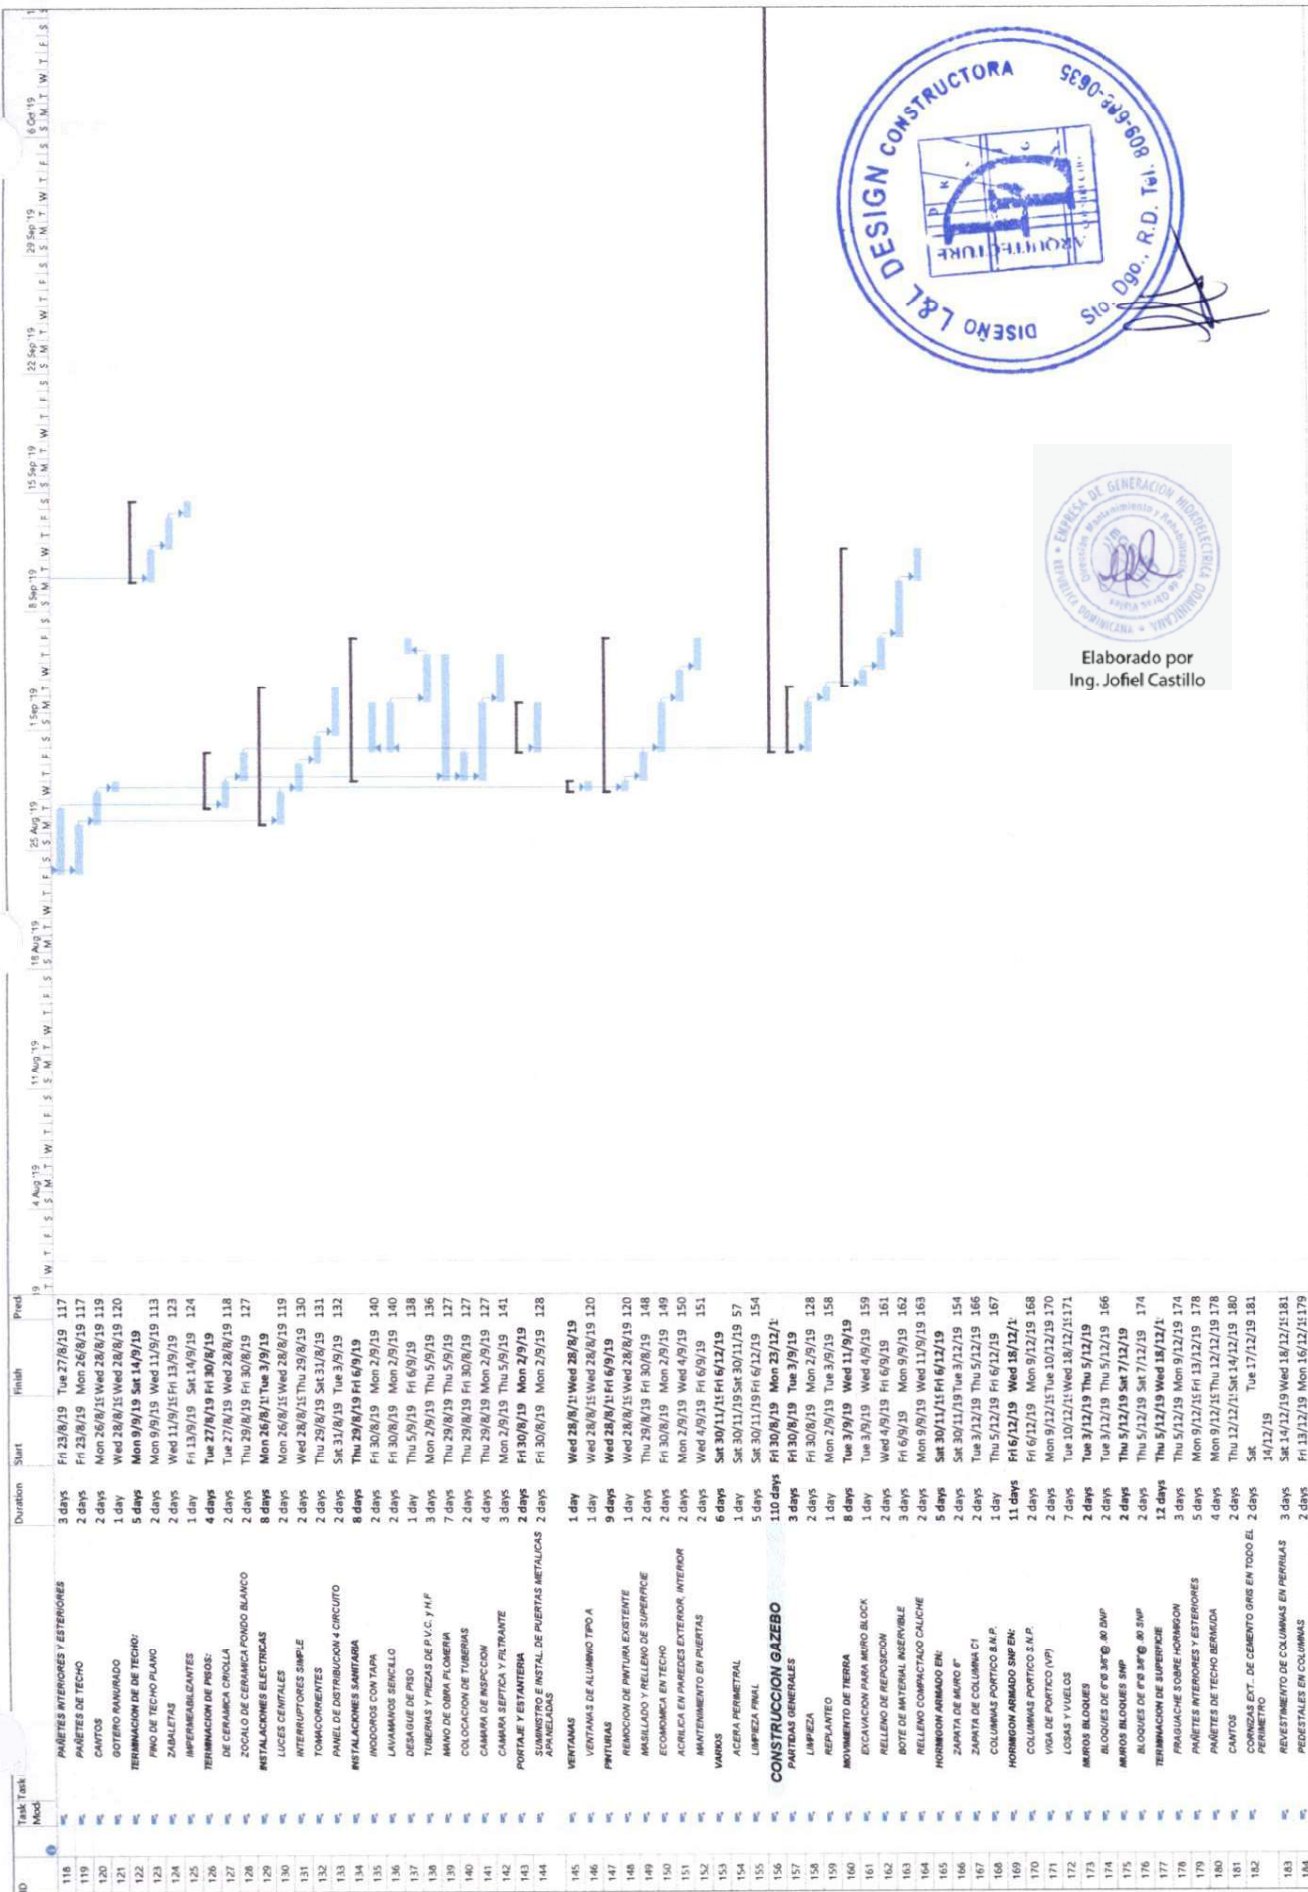

Elaborado por
Ing. Jofiel Castillo

ID	Task	Mod	Duration	Start	Finish	Preld
250	Rego de Impresión 0.6 g/s/m ² con Gavilla		4 days	Sat 11/1/20	Thu 16/1/20 24h	19
				4 Aug 19	11 Aug 19	16 Aug 19
				18 Aug 19	25 Aug 19	1 Sep 19
				8 Sep 19	15 Sep 19	22 Sep 19
				29 Sep 19	6 Oct 19	



Project: croco-Santa Lucia
Date: Thu 30/5/19


Task: ☐ Summary ☐ Inactive Milestone ☐ Duration only ☐ Start only ☐ External Milestone ☐ Manual Progress

Split: ☐ Inactive Summary ☐ Manual Summary ☐ Final only ☐ Duplicate

Milestone: ☐ Inactive Task ☐ Manual Task ☐ External Task ☐ Progress

Page 5

13 Oct 19 16 Oct 19 20 Oct 19 27 Oct 19 3 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dec 19 8 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

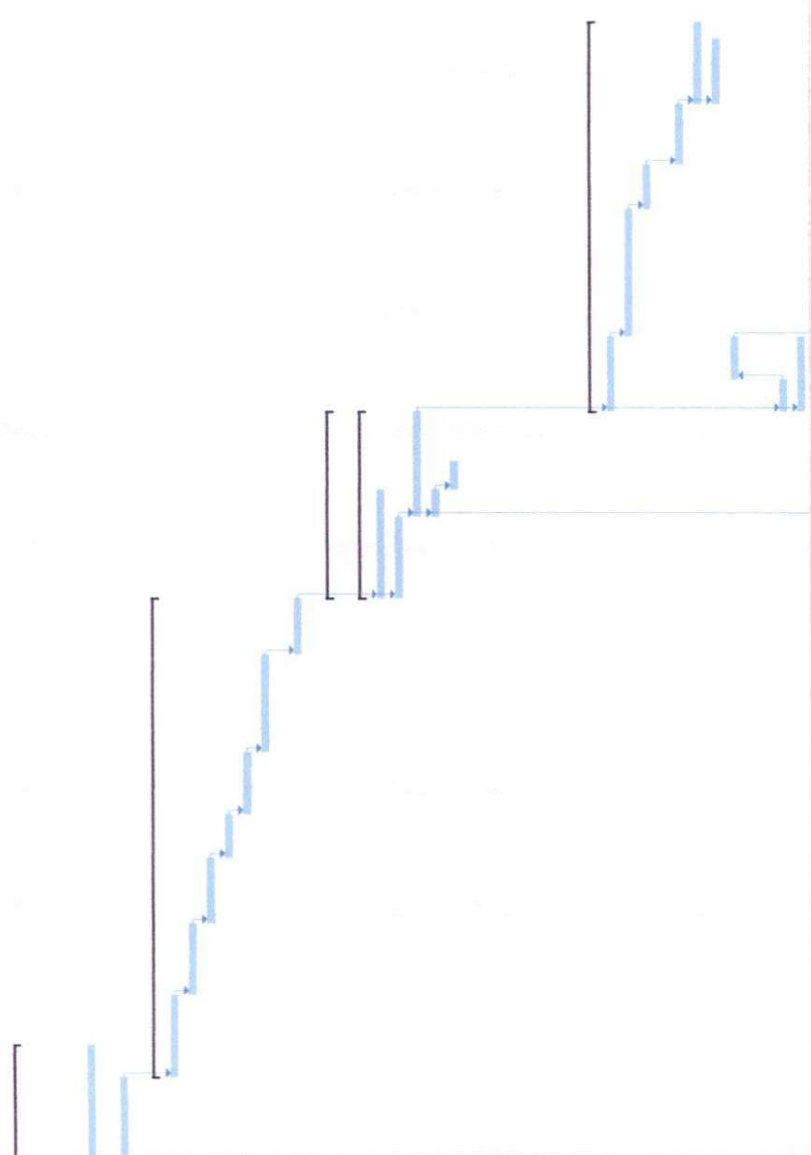

Elaborado por
Ing. Jofiel Castillo






Elaborado por
Ing. Jofiel Castillo



15 Oct 19 20 Oct 19 27 Oct 19 3 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dec 19 8 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

Elaborado por
Ing. Jofiel Castillo

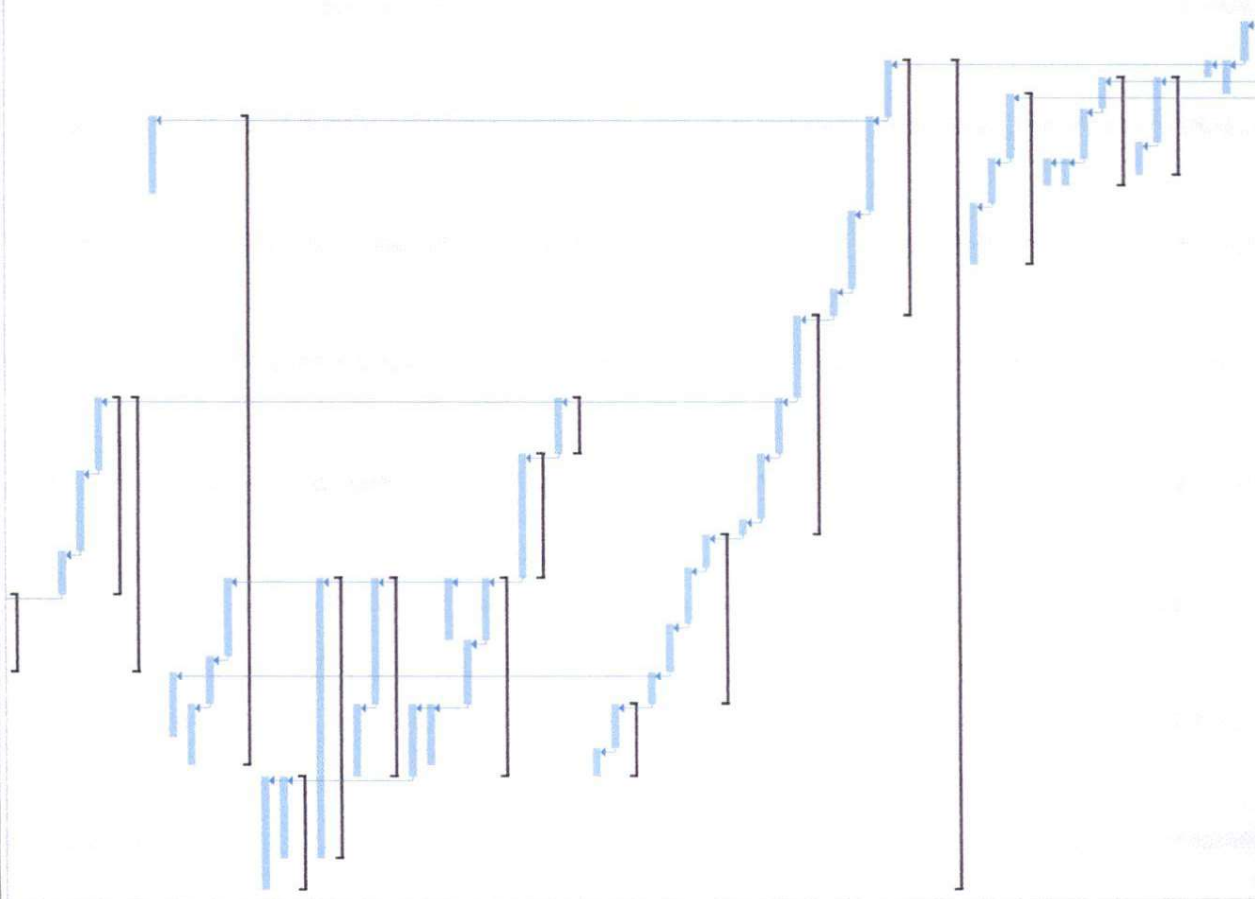

Project: cromo Santa Lucia
Date: Thu 30/5/19

Task
Split
Milestone
Summary
Request Summary
Insert Task
Insert Milestone
Insert Summary
Manual Task
Question only
Manual Summary Setup
Manual Summary
Start only
End only
External Task
External Milestone
Deadline
Project
Manual Program

13 Oct 19 S M T T W T F S S 20 Oct 19 F S S M T T W T F S 27 Oct 19 F S S M T T W T F S 3 Nov 19 S S M T T W T F S 10 Nov 19 S M T W T F S 17 Nov 19 F S S M T T W T F S 24 Nov 19 S S M T T W T F S 1 Dec 19 F S S M T T W T F S 8 Dec 19 S M T T W T F S 15 Dec 19 F S S M T T W T F S 22 Dec 19 F S S M T T W T F S 29 Dec 19 S M T T W T F S 5 Jan 20 S S M T T W T F S 12 Jan 20 F S S M T T W T F S 19 Jan 20 S M T T W T F S 26 Jan 20 S S M T T W T F S



Elaborado por
Ing. Jofiel Castillo



Project: cagoo-Santa Lucia
 Date: Thu 30/5/19

Task
 Split
 Milestone

Summary
 Project Summary
 Inactive Task

Inactive Milestone
 Inactive Summary
 Manual Task

Over-on-only
 Manual Summary Rollup
 Manual Summary

Start-only
 Finish-only
 External Task

External Milestone
 Deadline
 Progress

Manual Progress
