




Elaborado por  
Ing. Johel Castillo

ID	Task Mode	Task Name	Duration	Start	Finish
1	★	Reparacion de centro medico	18 days	Mon 16/11/20	Wed 09/12/20
2	★	TERMINACION DE TECHO	5 days	Mon 16/11/20	Fri 20/11/20
3	★	fino de techo plano	3 days	Mon 16/11/20	Wed 18/11/20
4	★	impermeabilizante manto asfaltico granular	2 days	Thu 19/11/20	Fri 20/11/20
5	★				
6	★	PORTAJE	5 days	Fri 27/11/20	Thu 03/12/20
7	★	puertas principaes en pino tratado	1 day?	Mon 30/11/20	Mon 30/11/20
8	★	puertas apaneladas ever door blanca	1 day?	Tue 01/12/20	Tue 01/12/20
9	★	ventanas corrediza de cristal p65	1 day?	Wed 02/12/20	Wed 02/12/20
10	★	puerta en closet en pino tratado con division	1 day?	Thu 03/12/20	Thu 03/12/20
11	★	gabinete en piso de pino tratado	2 days	Fri 27/11/20	Mon 30/11/20
12	★	gabinete de pared de pino tratado	2 days	Fri 27/11/20	Mon 30/11/20
13	★	meseta de granito natural	2 days	Mon 30/11/20	Tue 01/12/20

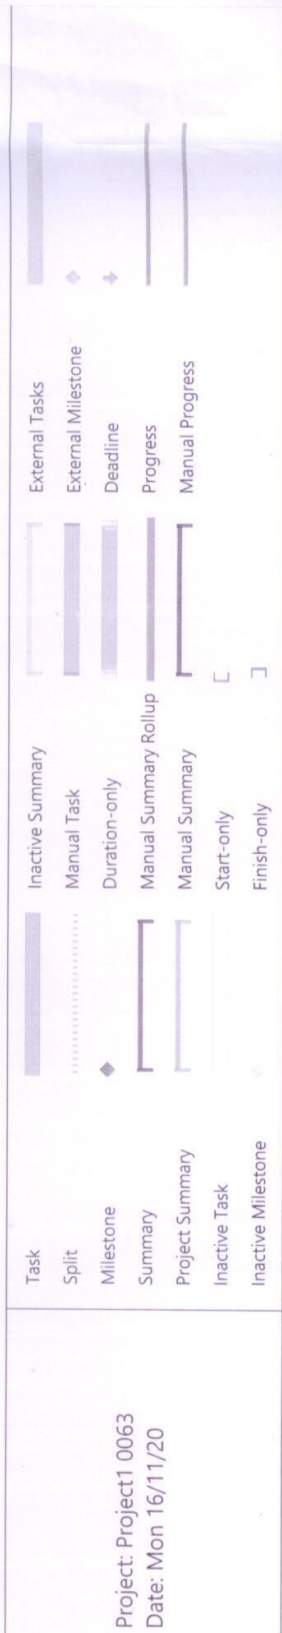

Project: Project1 0063  
Date: Mon 16/11/20

- Task
- Split
- Milestone
- Summary
- Project Summary
- Inactive Task
- Inactive Milestone
- Inactive Summary
- Manual Task
- Duration-only
- Manual Summary Rollup
- Manual Summary
- Start-only
- Finish-only
- External Tasks
- External Milestone
- Deadline
- Progress
- Manual Progress

ID	Task Mode	Task Name	Duration	Start	Finish
14	★	mueble en meseta pino tratado	1 day?	Tue 01/12/20	Tue 01/12/20
15	★	<b>PINTURA</b>	<b>5 days</b>	<b>Mon 23/11/20</b>	<b>Fri 27/11/20</b>
16	★	pintura en techo	3 days	Mon 23/11/20	Wed 25/11/20
17	★	pintura interior	4 days	Tue 24/11/20	Fri 27/11/20
18	★	semiglos muros, vigas y columnas	3 days	Wed 25/11/20	Fri 27/11/20
19	★	'pintura exterior acrílica muros, vigas y columnas	3 days	Wed 25/11/20	Fri 27/11/20
20	★	<b>INSTALACIONES SANITARIAS</b>	<b>6 days</b>	<b>Wed 02/12/20</b>	<b>Wed 09/12/20</b>
21	★	inodoro azteca	1 day?	Wed 02/12/20	Wed 02/12/20
22	★	blanco c/tapa sum,	1 day?	Wed 02/12/20	Wed 02/12/20
23	★	lavamanos blanco	1 day?	Wed 02/12/20	Wed 02/12/20
24	★	inc. mezcladora	1 day?	Wed 02/12/20	Wed 02/12/20
25	★	fregadero dos bocas teka	1 day?	Wed 02/12/20	Wed 02/12/20
26	★	acometida agua potable	1 day?	Mon 07/12/20	Mon 07/12/20
	★	suministro e instalacion de tinaco 265gls	2 days	Thu 03/12/20	Fri 04/12/20



Elaborado por  
Ing. Jofiel Castillo




Project: Project1 0063  
Date: Mon 16/11/20

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	



Elaborado por  
Ing. Jofiel Castillo

ID	Task Mode	Task Name	Duration	Start	Finish
27	★	sum. Y col. Bomba de 1/2 hp pedrolo botiquin	1 day?	Tue 08/12/20	Tue 08/12/20
28	★	accesorios	1 day?	Tue 08/12/20	Tue 08/12/20
29	★	tuberias y piezas especiales	1 day?	Wed 09/12/20	Wed 09/12/20
31	★	mano de obra plomero			
32	★				
33	★	<b>INSTALACIONES ELECTRICAS</b>	<b>3 days</b>	<b>Mon 23/11/20</b>	<b>Wed 25/11/20</b>
34	★	interruptores sencill	2 days	Mon 23/11/20	Tue 24/11/20
35	★	interruptores dobles	1 day?	Mon 23/11/20	Mon 23/11/20
36	★	globo	2 days	Mon 23/11/20	Tue 24/11/20
37	★	tomacorriente 10	3 days	Mon 23/11/20	Wed 25/11/20
38	★	lampara exterior tipo secador	1 day?	Mon 23/11/20	Mon 23/11/20
39	★	tuberias y piezas especiales	1 day?	Mon 23/11/20	Mon 23/11/20
40	★	paneles de distribucion 4 a 8	2 days	Tue 24/11/20	Wed 25/11/20
41	★				
42	★	<b>PISO CERAMICA</b>	<b>6 days</b>	<b>Thu 26/11/20</b>	<b>Thu 03/12/20</b>
43	★	piso de porcelanato 0.5*0.5 importada	5 days	Thu 26/11/20	Wed 02/12/20



Project: Project1 0063  
Date: Mon 16/11/20

ID	Task Mode	Task Name	Duration	Start	Finish	15 Nov '20	22 Nov '20	29 Nov '20	06 Dec '20
						S S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S
44	★	ceramica en pared de baños	3 days	Fri 27/11/20	Tue 01/12/20			█	
45	★	ceramica en pared de cocina	2 days	Mon 30/11/20	Tue 01/12/20			█	
46	★	zocalos	3 days	Tue 01/12/20	Thu 03/12/20				█



Project: Project1 0063 Date: Mon 16/11/20	<ul style="list-style-type: none"> <li>Task</li> <li>Split</li> <li>Milestone</li> <li>Summary</li> <li>Project Summary</li> <li>Inactive Task</li> <li>Inactive Milestone</li> </ul>	<ul style="list-style-type: none"> <li>Inactive Summary</li> <li>Manual Task</li> <li>Duration-only</li> <li>Manual Summary Rollup</li> <li>Manual Summary</li> <li>Start-only</li> <li>Finish-only</li> </ul>	<ul style="list-style-type: none"> <li>External Tasks</li> <li>External Milestone</li> <li>Deadline</li> <li>Progress</li> <li>Manual Progress</li> </ul>
--	---	--	---
