

ID	Task (Mod.)	Duration	Start	Finish	Preced
60	PORTAJE Y ESTANTERIA TODO CAJONIA Y METALICAS	67 days	Sat 28/9/19	Sat 7/12/19	
61	PASAMANOS BARRAJAS EN MESA/ME DE CAMPANARIO DE 150 Y 140 PULO	12 days	Sat 28/9/19	Fri 11/10/19	49
62	PASAMANOS DE 87 PULO PARA DIVIDIR EL ALTAR	10 days	Fri 11/10/19	Tue 22/10/19	61
63	SUMINISTRO E INSTAL DE PUERTAS NUEVAS EN CAJONIA	7 days	Tue 22/10/19	Tue 29/10/19	62
64	REPARACION PUERTAS PRINCIPALES TIEMPO	6 days	Tue 22/10/19	Mon 28/10/19	162
65	REPARACION DE PUERTAS	6 days	Mon 28/10/19	Sat 2/11/19	64
66	REPARACION PUERTAS DE BABEN	5 days	Mon 28/10/19	Fri 1/11/19	64
67	REPARACION DE BANCOS INCLUYE PINTURA	18 days	Sat 2/11/19	Wed 20/11/19	166
68	REPARACION DE UN JUEGO DE COMEDOR	7 days	Thu 21/11/19	Thu 28/11/19	67
69	REPARACION DE ARMARIOS GRANDES	6 days	Thu 28/11/19	Wed 4/12/19	68
70	REPARACION DE ESTANTES GRANDES	3 days	Wed 4/12/19	Sat 7/12/19	69
71	REPARACION DE BOUTAS	3 days	Thu 28/11/19	Sat 30/11/19	68
72	REPARACION DE PANELES TRAGALUZ	12 days	Tue 22/10/19	Sat 2/11/19	62
73	REPARA VITRINA DE LA VIBRETA STA LUCIA	4 days	Sat 28/9/19	Thu 3/10/19	49
74	REPARAR VITRINA DE LA VIBRETA ALTA GRACA	2 days	Thu 3/10/19	Fri 4/10/19	73
75	REPARACION VENTANILLAS DE ARRIBA EN EL TIEMPO	2 days	Sat 5/10/19	Mon 7/10/19	74
76	REPARACION ENTABLADO CON CRISTAL	2 days	Mon 7/10/19	Wed 9/10/19	75
77	CONSTRUCCION GABINETES Y DEFENSA EN COCINA	5 days	Sat 28/9/19	Fri 4/10/19	49
78	SUMINISTRO E INSTAL DE PUERTAS METALICAS ADMINISTRACION	4 days	Sat 28/9/19	Thu 3/10/19	49
79	VENTANAS	6 days	Sat 12/10/19	Fri 18/10/19	
80	VENTANAS REFORZADAS CORREDIZAS DE ALUMINO Y VIDRIO EN TIEMPO	3 days	Sat 12/10/19	Tue 15/10/19	27
81	VENTANAS REFORZADAS CORREDIZAS DE ALUMINO Y VIDRIO EN AREAS ADMINISTRATIVAS	3 days	Tue 15/10/19	Fri 18/10/19	80
82	PINTURAS	29 days	Sat 12/10/19	Mon 11/11/19	
83	REMOCCION DE PINTURA EXISTENTE	15 days	Sat 12/10/19	Mon 28/10/19	27
84	MASILLADO Y RELLENO DE SUPERFICIE	6 days	Mon 28/10/19	Sat 2/11/19	83
85	ACRILICA ESPECIAL EN TECHO	4 days	Sat 2/11/19	Thu 7/11/19	84
86	ACRILICA ESPECIAL EN PAREDES EXTERIOR INTERIOR	8 days	Sat 2/11/19	Mon 11/11/19	84
87	UTILIZACION DE BONDOLA	8 days	Sat 2/11/19	Mon 11/11/19	84
88	MANTENIMIENTO EN PUERTAS	3 days	Thu 7/11/19	Mon 11/11/19	85
89	VARIOS	50 days	Sat 28/9/19	Wed 20/11/19	
90	ACERA PERIMETRAL	4 days	Sat 28/9/19	Thu 3/10/19	49
91	PROTECCION DE VENTANAS Y PUERTAS HIERRO	6 days	Fri 18/10/19	Thu 24/10/19	81
92	CANALERA PARA DESGUE DE TECHOS PVC	1 day	Tue 19/11/19	Wed 20/11/19	41
93	SIEMBRA DE GRAMOS Y FLORES	3 days	Thu 3/10/19	Sat 5/10/19	90
94	LIMPIEZA Y PINTURA CAMPANARIO	3 days	Sat 5/10/19	Wed 9/10/19	93
95	LIMPIEZA FINAL	2 days	Wed 9/10/19	Fri 11/10/19	94
96	CONSTRUCCION AREA DE BAÑO EXTERIOR	118 days	Tue 6/8/19	Fri 6/12/19	
97	PANTALLAS GENERALES	11 days	Tue 6/8/19	Sat 17/8/19	
98	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS Y MUROS	3 days	Tue 6/8/19	Fri 9/8/19	4
99	BOITE ESCOMBRO	4 days	Fri 9/8/19	Tue 13/8/19	98
100	LIMPIEZA	4 days	Tue 13/8/19	Sat 17/8/19	99
101	MOVIMIENTO DE TIERRA	9 days	Sat 17/8/19	Tue 27/8/19	
102	EXCAVACION PARA BLOQUE DIVISORIO	2 days	Sat 17/8/19	Mon 19/8/19	100
103	RELLENO DE POSICION	2 days	Tue 20/8/19	Wed 21/8/19	102
104	BOITE DE MATERIAL INSENVIBLE	3 days	Wed 21/8/19	Sat 24/8/19	103
105	RELLENO COMPACTADO CALICHE	2 days	Sat 24/8/19	Tue 27/8/19	104
106	HORNICON ARMADO EN:	4 days	Tue 27/8/19	Fri 30/8/19	
107	ZAPATA DE COLUMNA C1	2 days	Tue 27/8/19	Wed 28/8/19	105
108	COLUMNAS PORTICO S.N.P	2 days	Thu 29/8/19	Fri 30/8/19	107
109	HORNICON ARMADO S.N.P	9 days	Fri 30/8/19	Mon 9/9/19	
110	COLUMNAS PORTICO S.N.P	2 days	Mon 2/9/19	Mon 2/9/19	108
111	VISA DINTEL (01)	2 days	Mon 2/9/19	Wed 4/9/19	110
112	VIGA DE CARGA	2 days	Mon 2/9/19	Wed 4/9/19	110
113	LOSAS Y VUELOS	5 days	Wed 4/9/19	Mon 9/9/19	112
114	MUROS BLOQUES	2 days	Tue 20/8/19	Wed 21/8/19	102
115	BLOQUES DE FIBRA DE CARBON	2 days	Tue 20/8/19	Wed 21/8/19	102
116	TERMINACION DE SUPERFICIE	7 days	Wed 21/8/19	Wed 28/8/19	
117	PRAQUACHE SOBRE HORNICON	2 days	Wed 21/8/19	Fri 23/8/19	115



ID	Task/Task Mod	Duration	Start	Finish	Preced
118	PAÑETES INTERIORES Y ESTERONERES	3 days	Fri 23/8/19	Tue 27/8/19	117
119	PAÑETES DE TECHO	2 days	Fri 23/8/19	Mon 26/8/19	117
120	CANTOS	2 days	Mon 26/8/19	Wed 28/8/19	119
121	GOTERO RANURADO	1 day	Wed 28/8/19	Wed 28/8/19	120
122	TERMINACION DE TECHO:	5 days	Mon 9/9/19	Sat 14/9/19	
123	PIÑO DE TECHO PLANO	2 days	Mon 9/9/19	Wed 11/9/19	113
124	ZABALETAS	2 days	Wed 11/9/19	Fri 13/9/19	123
125	IMPERMEABILIZANTES	1 day	Fri 13/9/19	Sat 14/9/19	124
126	TERMINACION DE PISO:	4 days	Tue 27/8/19	Fri 30/8/19	
127	DE CERRAMICA CROSLA	2 days	Tue 27/8/19	Wed 28/8/19	118
128	ZOCALO DE CERRAMICA PONGO BLANCO	2 days	Thu 29/8/19	Fri 30/8/19	127
129	INSTALACIONES ELECTRICAS	8 days	Mon 26/8/19	Tue 3/9/19	
130	LUCES CENTIALES	2 days	Mon 26/8/19	Wed 28/8/19	119
131	INTERRUPTORES SIMPLE	2 days	Wed 28/8/19	Thu 29/8/19	130
132	TOMACORRIENTES	2 days	Thu 29/8/19	Sat 31/8/19	131
133	PANEL DE DISTRIBUCION 4 CIRCUITO	2 days	Sat 31/8/19	Tue 3/9/19	132
134	INSTALACIONES SANITARIA	8 days	Thu 29/8/19	Fri 6/9/19	
135	INDICADORES CON TAPA	2 days	Fri 30/8/19	Mon 2/9/19	140
136	LAVAMANOS SENCILLO	2 days	Fri 30/8/19	Mon 2/9/19	140
137	DESAGUE DE PISO	1 day	Thu 5/9/19	Fri 6/9/19	138
138	TUBERIAS Y PIEZAS DE P.V.C. Y H.F	3 days	Mon 2/9/19	Thu 5/9/19	136
139	MAIWO DE OBRAS PLOMERIA	7 days	Thu 29/8/19	Thu 5/9/19	127
140	COLOCACION DE TUBERIAS	2 days	Thu 29/8/19	Fri 30/8/19	127
141	CAMARA DE INSPECCION	4 days	Mon 2/9/19	Mon 2/9/19	127
142	CAMARA SEPTICA Y REFRANTE	3 days	Fri 30/8/19	Thu 5/9/19	141
143	PORTALE Y ESTANTERIA	2 days	Fri 30/8/19	Mon 2/9/19	
144	SUMINISTRO E INSTALACION DE PUERTAS METALICAS	2 days	Fri 30/8/19	Mon 2/9/19	128
145	VENTANAS	1 day	Wed 28/8/19	Wed 28/8/19	
146	VENTANAS DE ALUMINIO TIPO A	1 day	Wed 28/8/19	Wed 28/8/19	120
147	PINTURAS	9 days	Wed 28/8/19	Fri 6/9/19	
148	RENOVACION DE PINTURA EXISTENTE	1 day	Wed 28/8/19	Wed 28/8/19	120
149	ASELILLADO Y RELLENO DE SUPERFICIE	2 days	Thu 29/8/19	Fri 30/8/19	148
150	ECONOMICA EN TECHO	2 days	Fri 30/8/19	Mon 2/9/19	149
151	ACRILICA EN PAREDES EXTERIOR, INTERIOR	2 days	Mon 2/9/19	Wed 4/9/19	150
152	MANTENIMIENTO EN PUERTAS	2 days	Wed 4/9/19	Fri 6/9/19	151
153	VARIOS	6 days	Sat 30/11/19	Fri 6/12/19	
154	ACERA PERIMETRAL	1 day	Sat 30/11/19	Sat 30/11/19	57
155	LIMPIEZA FINAL	5 days	Sat 30/11/19	Fri 6/12/19	154
156	110 days	Fri 30/8/19	Mon 23/12/19		
157	3 days	Fri 30/8/19	Tue 3/9/19		
158	2 days	Fri 30/8/19	Mon 2/9/19	128	
159	1 day	Mon 2/9/19	Tue 3/9/19	158	
160	8 days	Tue 3/9/19	Wed 11/9/19		
161	1 day	Tue 3/9/19	Wed 4/9/19	159	
162	2 days	Wed 4/9/19	Fri 6/9/19	161	
163	3 days	Fri 6/9/19	Mon 9/9/19	162	
164	2 days	Mon 9/9/19	Wed 11/9/19	163	
165	5 days	Sat 30/11/19	Fri 6/12/19		
166	2 days	Sat 30/11/19	Tue 3/12/19	154	
167	2 days	Tue 3/12/19	Thu 5/12/19	166	
168	1 day	Thu 5/12/19	Fri 6/12/19	167	
169	11 days	Fri 6/12/19	Wed 18/12/19		
170	2 days	Fri 6/12/19	Mon 9/12/19	168	
171	2 days	Mon 9/12/19	Tue 10/12/19	170	
172	7 days	Tue 10/12/19	Wed 18/12/19	171	
173	2 days	Tue 3/12/19	Thu 5/12/19	166	
174	2 days	Tue 3/12/19	Thu 5/12/19	166	
175	2 days	Thu 5/12/19	Sat 7/12/19	174	
176	12 days	Thu 5/12/19	Wed 18/12/19		
177	3 days	Thu 5/12/19	Mon 9/12/19	174	
178	5 days	Mon 9/12/19	Fri 13/12/19	178	
179	4 days	Mon 9/12/19	Thu 12/12/19	178	
180	2 days	Thu 12/12/19	Sat 14/12/19	180	
181	2 days	Sat 14/12/19	Tue 17/12/19	181	
182	3 days	Sat 14/12/19	Wed 18/12/19	181	
183	2 days	Fri 13/12/19	Mon 16/12/19	181	
184					



Projecto: **Proyecto Santa Lucia**
 Date: **Thu 30/5/19**

Task: Summary Inactive Task Inactive Milestone Inactive Summary

Split: Manual Summary Manual Summary

Milestone: Inactive Milestone Inactive Summary

External Milestone: External Milestone

Deadline: Deadline

Progress: Progress

Manual Task: Manual Task

Str-only: Str-only

Inv-only: Inv-only

External Task: External Task

Manual Program: Manual Program

ID	Task Title	Mod	Duration	Start	Finish	Predecessors
250	Rego de Impresión 0.6 g/s/m ² con Gavilla		4 days	Sat 11/1/20	Thu 16/1/20 24h	19



Project: crono-Sana Lucia
Date: Thu 30/5/19

Task: Spine
Milestone: Milestone

Summary: [Progress bar]

Request Summary: [Progress bar]

Initial Task: [Progress bar]

Initial Milestone: [Progress bar]

Initial Summary: [Progress bar]

Manual Task: [Progress bar]

Duration only: [Progress bar]

Manual Summary (Setup): [Progress bar]

Manual Summary: [Progress bar]

Final only: [Progress bar]

External Task: [Progress bar]

External Milestone: [Progress bar]

External Task: [Progress bar]

Manual Progress: [Progress bar]

Page 5

13 Dic 19 20 Dic 19 27 Dic 19 3 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dic 19 8 Dic 19 15 Dic 19 22 Dic 19 29 Dic 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20



Project: **proo-Santa Luda**
 Date: **Thu 30/5/19**

Task: Task Split Milestone

Summary: Summary Project Summary inactive Task

Interval Milestone: Interval Milestone Interval Summary Manual Task

Duration-only: Duration-only Manual Summary Manual Summary

Start-only: Start-only Finish only Interval Task

External Milestone: External Milestone Deadline Program


Manual Program: Manual Program



ELABORADO POR: ING. JOFEL CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS



18 Oct 19 | 20 Oct 19 | 27 Oct 19 | 3 Nov 19 | 10 Nov 19 | 17 Nov 19 | 24 Nov 19 | 1 Dec 19 | 8 Dec 19 | 15 Dec 19 | 22 Dec 19 | 29 Dec 19 | 5 Jan 20 | 12 Jan 20 | 19 Jan 20 | 26 Jan 20

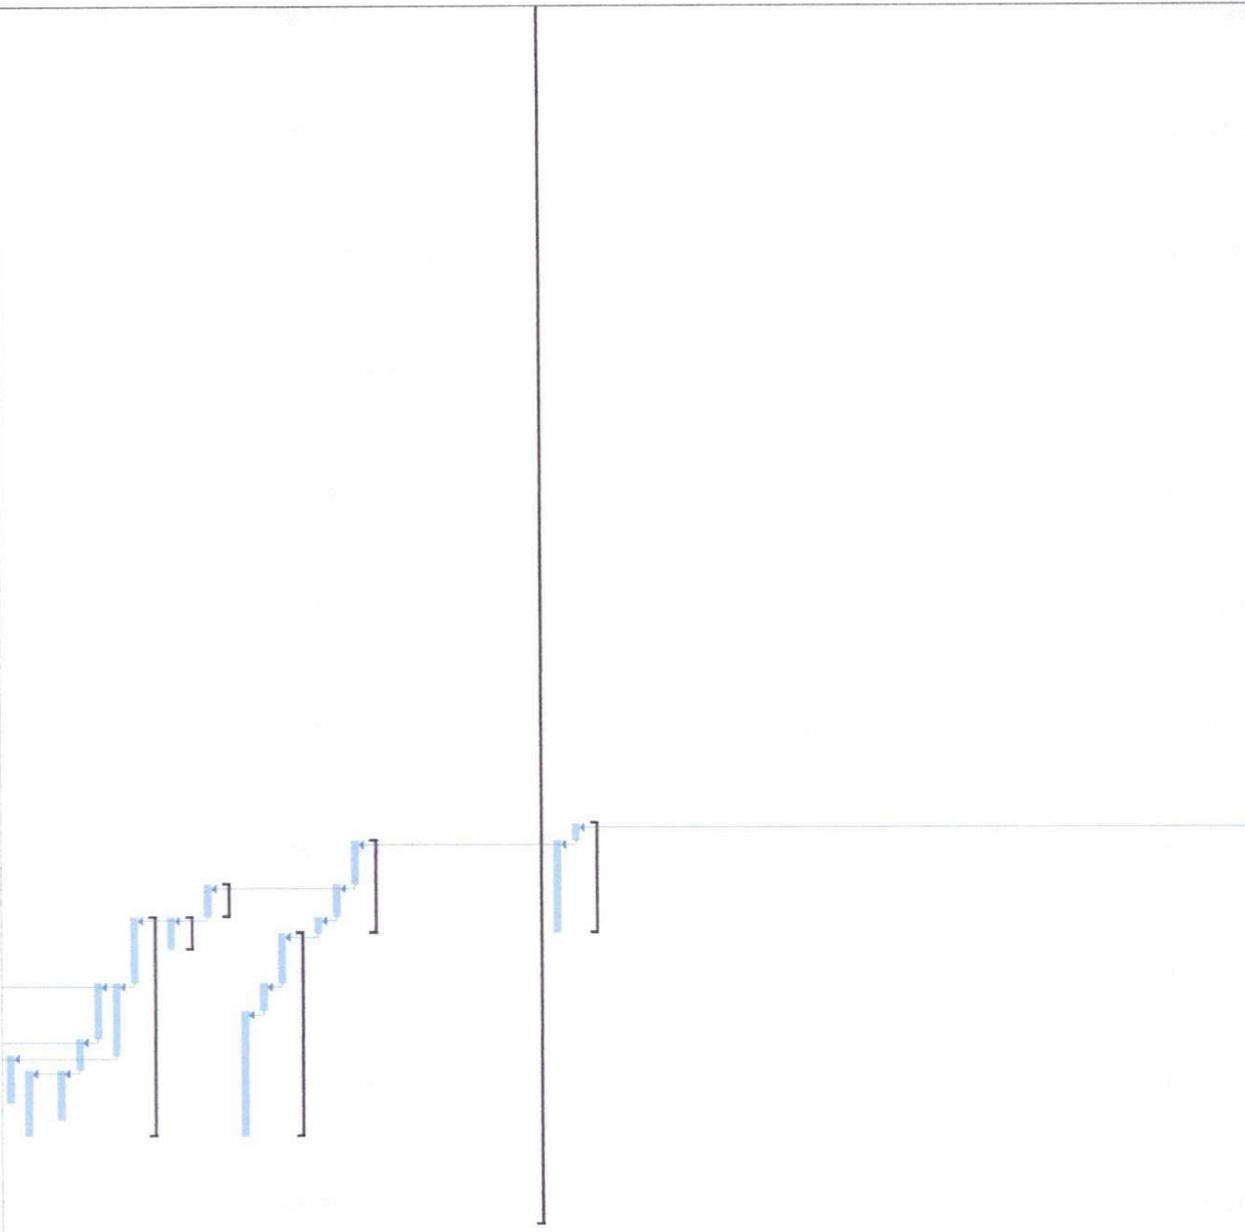

Project: **Corona Santa Lucia**
 Date: **Thu 30/5/19**

Task Milestone Summary Project Summary System Milestone Duration Only Start Only Finish Only External Milestone Manual Program


Page 8



ELABORADO POR: ING. JOFEL CASTILLO
 ENCARGADO DE CONTROL DE PROYECTOS



15 Oct 19 20 Oct 19 27 Oct 19 31 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dec 19 8 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

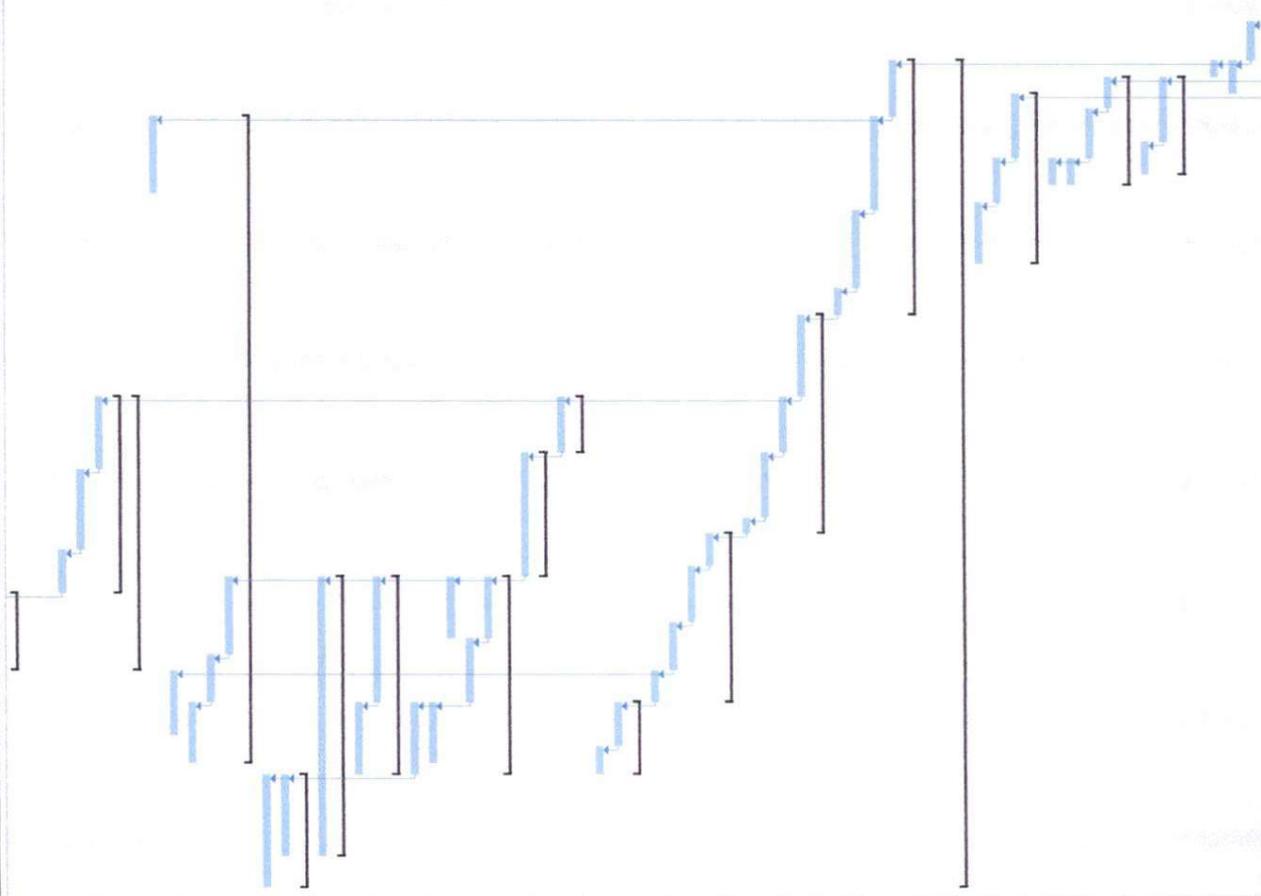

ELABORADO POR: ING. JOFEL CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS



Project: crono Santa Lucia
Date: Thu 30/9/19

- Task
- Sign
- Milestone
- Summary
- Request Summary
- Initial Task
- Initial Milestone
- Initial Summary
- Manual Task
- Overrun-only
- Manual Summary (blue)
- Manual Summary
- Start-only
- End-only
- External Task
- External Milestone
- Deadline
- Project
- Manual Program

13 Oct 19 | 19 Oct 19 | 20 Oct 19 | 27 Oct 19 | 3 Nov 19 | 10 Nov 19 | 17 Nov 19 | 24 Nov 19 | 1 Dec 19 | 8 Dec 19 | 15 Dec 19 | 22 Dec 19 | 29 Dec 19 | 5 Jan 20 | 12 Jan 20 | 19 Jan 20 | 26 Jan 20



ELABORADO POR ING. JOSE CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS

Project: **casas Santa Lucia**
Date: **Thu 30/5/19**

Task: **Summary** | **Project Summary** | **header task**

Task: **Split** | **Milestone**

Task: **Active Milestone** | **Inactive Milestone** | **Manual Task**

Task: **Duration only** | **Manual Summary Rollup** | **Manual Summary**

Task: **Start only** | **Finish only** | **External Task**

Task: **External Milestone** | **Deadline** | **Progress**

Task: **Manual Progress**
