


ID	Task (Mod.)	Duration	Start	Finish	Preced
60	PORTAJE Y ESTANTERIA TODO CAJONIA Y METALICAS	67 days	Sat 28/9/19	Sat 7/12/19	
61	PASAMANOS BARRAJAS EN MESA/ME DELE CAMPANARIO DE 150 Y 140 PULO	12 days	Sat 28/9/19	Fri 11/10/19	49
62	PASAMANOS DE 87 PULO PARA DIVIDIR EL ALTAR	10 days	Fri 11/10/19	Tue 22/10/19	61
63	SUMINISTRO E INSTAL DE PUERTAS NUEVAS EN CAJONIA	7 days	Tue 22/10/19	Tue 29/10/19	62
64	REPARACION PUERTAS PRINCIPALES TIEMPO	6 days	Tue 22/10/19	Mon 28/10/19	62
65	REPARACION DE PUERTAS	6 days	Mon 28/10/19	Sat 2/11/19	64
66	REPARACION PUERTAS DE BABEN	5 days	Mon 28/10/19	Fri 1/11/19	64
67	REPARACION DE BANCOS INCLUYE PINTURA	18 days	Sat 2/11/19	Wed 20/11/19	66
68	REPARACION DE UN JUEGO DE COMEDOR	7 days	Thu 21/11/19	Thu 28/11/19	67
69	REPARACION DE ARMARIOS GRANDES	6 days	Thu 28/11/19	Wed 4/12/19	68
70	REPARACION DE ESTANTES GRANDES	3 days	Wed 4/12/19	Sat 7/12/19	69
71	REPARACION DE BOUTAS	3 days	Thu 28/11/19	Sat 30/11/19	68
72	REPARACION DE PANELES TRAGALUZ	12 days	Tue 22/10/19	Sat 2/11/19	62
73	REPARA VITRINA DE LA VIBRETA STA LUCIA	4 days	Sat 28/9/19	Thu 3/10/19	49
74	REPARA VITRINA DE LA VIBRETA ALTA GRACA	2 days	Thu 3/10/19	Fri 4/10/19	73
75	REPARACION VENTANILLAS DE ARRIBA EN EL TIEMPO	2 days	Sat 5/10/19	Mon 7/10/19	74
76	REPARACION ENTABLADO CON CRISTAL	2 days	Mon 7/10/19	Wed 9/10/19	75
77	CONSTRUCCION GABINETES Y DEFENSA EN COCINA	5 days	Sat 28/9/19	Fri 4/10/19	49
78	SUMINISTRO E INSTAL DE PUERTAS METALICAS ADMINISTRACION	4 days	Sat 28/9/19	Thu 3/10/19	49
79	VENTANAS	6 days	Sat 12/10/19	Fri 18/10/19	
80	VENTANAS REFORZADAS CORREDIZAS DE ALUMINO Y VIDRIO EN TIEMPO	3 days	Sat 12/10/19	Tue 15/10/19	27
81	VENTANAS REFORZADAS CORREDIZAS DE ALUMINO Y VIDRIO EN AREAS ADMINISTRATIVAS	3 days	Tue 15/10/19	Fri 18/10/19	80
82	PINTURAS	29 days	Sat 12/10/19	Mon 11/11/19	
83	REMOCCION DE PINTURA EXISTENTE	15 days	Sat 12/10/19	Mon 28/10/19	27
84	MASILLADO Y RELLENO DE SUPERFICIE	6 days	Mon 28/10/19	Sat 2/11/19	83
85	ACRILICA ESPECIAL EN TECHO	4 days	Sat 2/11/19	Thu 7/11/19	84
86	ACRILICA ESPECIAL EN PAREDES EXTERIOR INTERIOR	8 days	Sat 2/11/19	Mon 11/11/19	84
87	UTILIZACION DE BONDOLA	8 days	Sat 2/11/19	Mon 11/11/19	84
88	MANTENIMIENTO EN PUERTAS	3 days	Thu 7/11/19	Mon 11/11/19	85
89	VARIOS	50 days	Sat 28/9/19	Wed 20/11/19	
90	ACERA PERIMETRAL	4 days	Sat 28/9/19	Thu 3/10/19	49
91	PROTECCION DE VENTANAS Y PUERTAS HIERRO	6 days	Fri 18/10/19	Thu 24/10/19	81
92	CANALERA PARA DESAGUE DE TECHOS EN PVC	1 day	Tue 19/11/19	Wed 20/11/19	41
93	SIEMBRA DE GRAMAS Y FLORES	3 days	Thu 3/10/19	Sat 5/10/19	90
94	LIMPIEZA Y PINTURA CAMPANARIO	3 days	Sat 5/10/19	Wed 9/10/19	93
95	LIMPIEZA FINAL	2 days	Wed 9/10/19	Fri 11/10/19	94
96	CONSTRUCCION AREA DE BAÑO EXTERIOR	118 days	Tue 6/8/19	Fri 6/12/19	
97	PANTALLAS GENERALES	11 days	Tue 6/8/19	Sat 17/8/19	
98	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS Y MUROS	3 days	Tue 6/8/19	Fri 9/8/19	4
99	BOITE ESCOMBRO	4 days	Fri 9/8/19	Tue 13/8/19	98
100	LIMPIEZA	4 days	Tue 13/8/19	Sat 17/8/19	99
101	MOVIMIENTO DE TIERRA	9 days	Sat 17/8/19	Tue 27/8/19	
102	EXCAVACION PARA BARRIO BLOCK DIVISORIO	2 days	Sat 17/8/19	Mon 19/8/19	100
103	RELLENO DE POSICION	2 days	Tue 20/8/19	Wed 21/8/19	102
104	BOITE DE MATERIAL INSENVIBLE	3 days	Wed 21/8/19	Sat 24/8/19	103
105	RELLENO COMPACTADO CALICHE	2 days	Sat 24/8/19	Tue 27/8/19	104
106	HORNO ARMADO EN:	4 days	Tue 27/8/19	Fri 30/8/19	
107	ZAPATA DE COLUMNA C1	2 days	Tue 27/8/19	Wed 28/8/19	105
108	COLUMNAS PORTICO S.N.P	2 days	Thu 29/8/19	Fri 30/8/19	107
109	HORNO ARMADO S.M.P	9 days	Fri 30/8/19	Mon 9/9/19	
110	COLUMNAS PORTICO S.N.P	2 days	Mon 2/9/19	Mon 2/9/19	108
111	VISA DINTEL (01)	2 days	Mon 2/9/19	Wed 4/9/19	110
112	VIGA DE CARGA	2 days	Mon 2/9/19	Wed 4/9/19	110
113	LOSAS Y VUELOS	5 days	Wed 4/9/19	Mon 9/9/19	112
114	MUROS BLOQUES	2 days	Tue 20/8/19	Wed 21/8/19	102
115	BLOQUES DE FIBRA DE CARBON	2 days	Tue 20/8/19	Wed 21/8/19	102
116	TERMINACION DE SUPERFICIE	7 days	Wed 21/8/19	Wed 28/8/19	
117	PRAQUACHE SOBRE HORNOBON	2 days	Wed 21/8/19	Fri 23/8/19	115



LABORADO POR ING. JOSE CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS

ID	Task Title	Mod	Duration	Start	Finish	Predecessors
200	Rego de Impresión 0.6 g/s/m ² con Genilla		4 days	Sat 11/1/20	Tue 16/1/20 24h	



Project: crono-Sana Lucia
Date: Thu 30/5/19

Task: Spine
Milestone: Milestone

Summary: [Progress bar]

Request Summary: [Progress bar]

Initial Task: [Progress bar]

Initial Milestone: [Progress bar]

Initial Summary: [Progress bar]

Manual Task: [Progress bar]

Duration only: [Progress bar]

Manual Summary (dup): [Progress bar]

Manual Summary: [Progress bar]

Start only: [Progress bar]

Final only: [Progress bar]

External Task: [Progress bar]


External Milestone: [Progress bar]

External Task: [Progress bar]

Manual Progress: [Progress bar]

Page 5

13 Dic 19 20 Dic 19 27 Dic 19 3 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dic 19 8 Dic 19 15 Dic 19 22 Dic 19 29 Dic 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

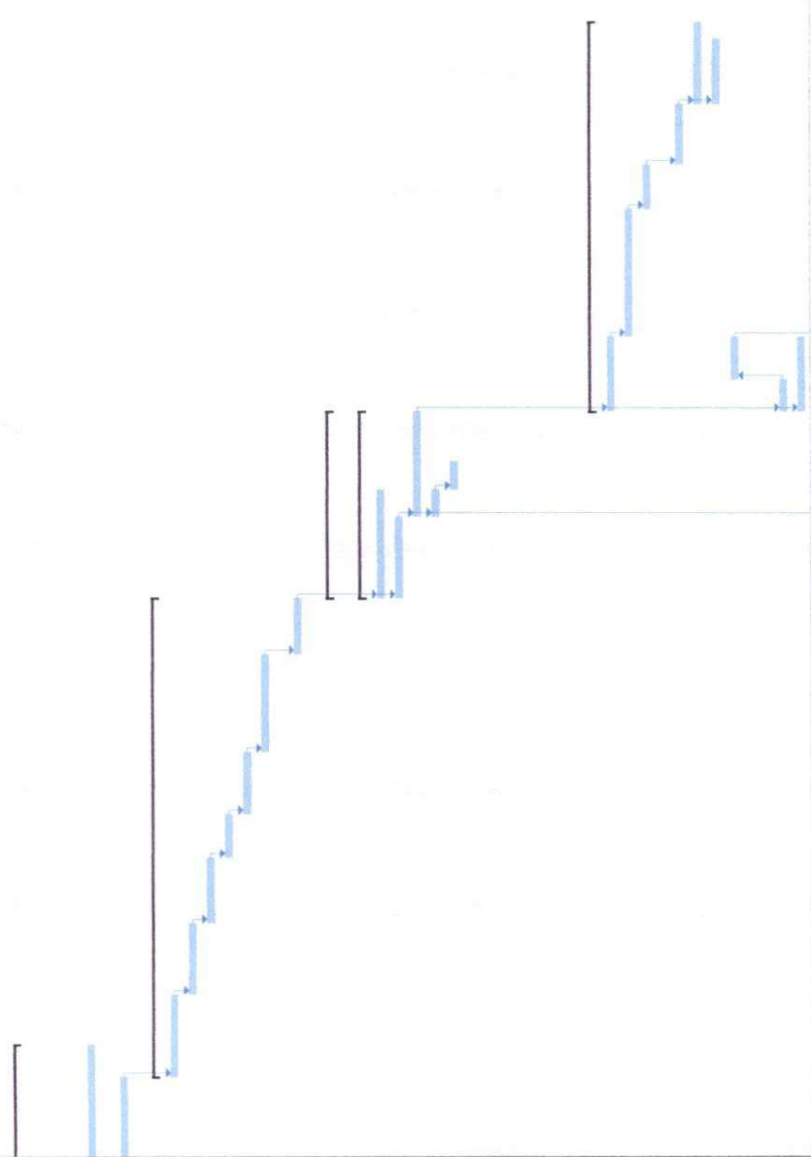

Project: **proo-Santa Luda**
 Date: **Thu 30/5/19**

Task: Task Split Milestone

Summary: Summary Project Summary inactive Task

Interval Milestone: Interval Milestone Interval Summary Manual Task


Duration-only: Duration-only Manual Summary Manual Summary

Start-only: Start-only Finish only Interval Task

External Milestone: External Milestone Deadline Program

Manual Program: Manual Program

19 Oct 19 20 Oct 19 27 Oct 19 29 Oct 19 30 Nov 19 01 Nov 19 06 Nov 19 07 Nov 19 13 Nov 19 20 Nov 19 26 Nov 19 01 Dec 19 08 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 05 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

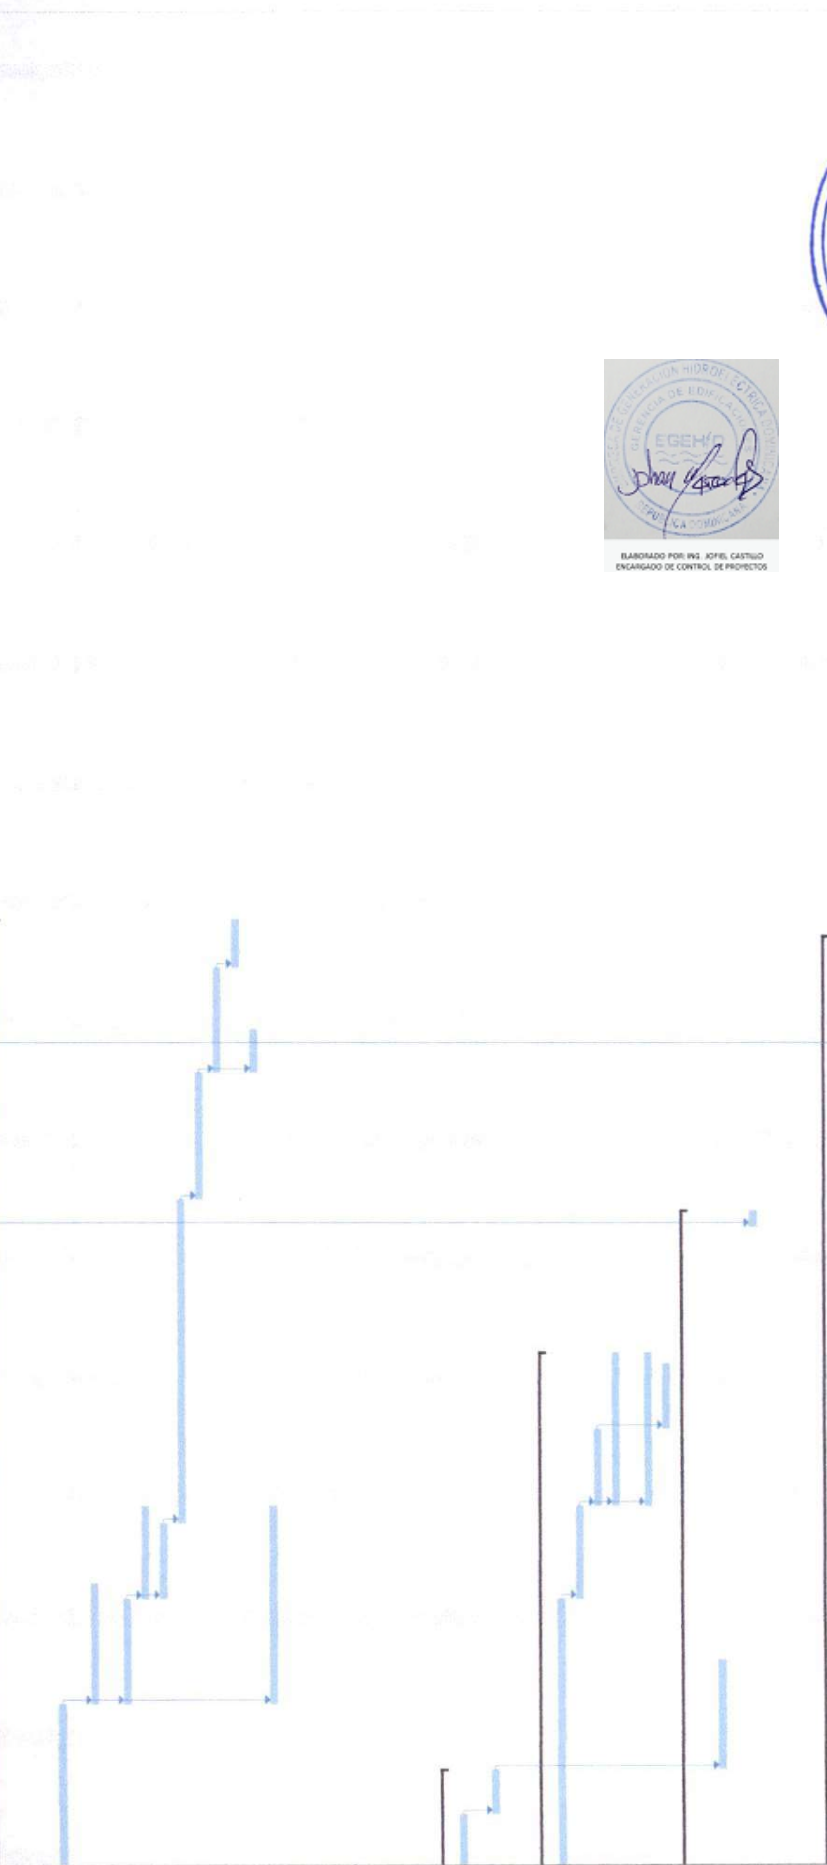


ELABORADO POR: ING. JOFEL CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS



Project: **crono-Santa Lucia**
Date: **Thu 30/5/19**

- Task: []
- Split: []
- Milestone: []
- Summary: []
- Project Summary: []
- Inactive Task: []
- Inactive Milestone: []
- Inactive Summary: []
- Inactive Manual Task: []
- Duration-only: []
- Manual Summary Setup: []
- Manual Summary: []
- Start-only: []
- Finish-only: []
- Estimate Task: []
- Estimate Milestone: []
- Estimate Milestone Deadline: []
- Estimate Milestone Progress: []
- Manual Progress: []

18 Oct 19 | 20 Oct 19 | 27 Oct 19 | 3 Nov 19 | 10 Nov 19 | 17 Nov 19 | 24 Nov 19 | 1 Dec 19 | 8 Dec 19 | 15 Dec 19 | 22 Dec 19 | 29 Dec 19 | 5 Jan 20 | 12 Jan 20 | 19 Jan 20 | 26 Jan 20

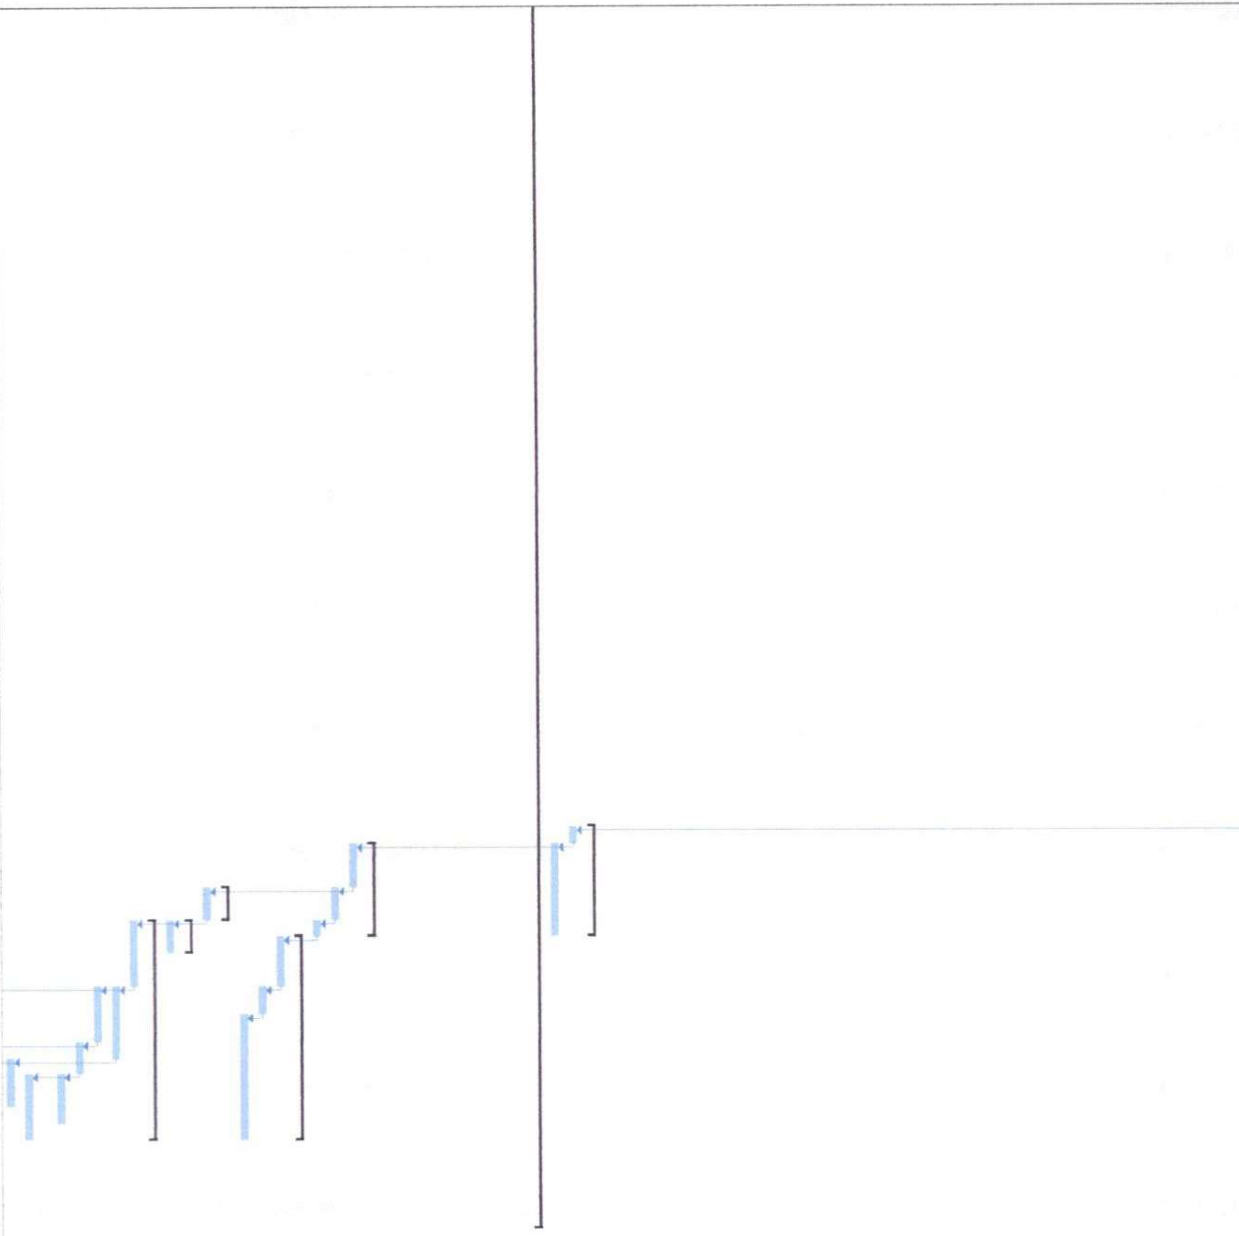

Project: **Corona Santa Lucia**
 Date: **Thu 30/5/19**


Task Milestone Summary Project Summary System Milestone Duration Only Start Only Finish Only External Milestone Manual Program

Page 8

ELABORADO POR: ING. JOFEL CASTILLO
 ENCARGADO DE CONTROL DE PROYECTOS



15 Oct 19 | 20 Oct 19 | 27 Oct 19 | 3 Nov 19 | 10 Nov 19 | 17 Nov 19 | 24 Nov 19 | 1 Dec 19 | 8 Dec 19 | 15 Dec 19 | 22 Dec 19 | 29 Dec 19 | 5 Jan 20 | 12 Jan 20 | 19 Jan 20 | 26 Jan 20

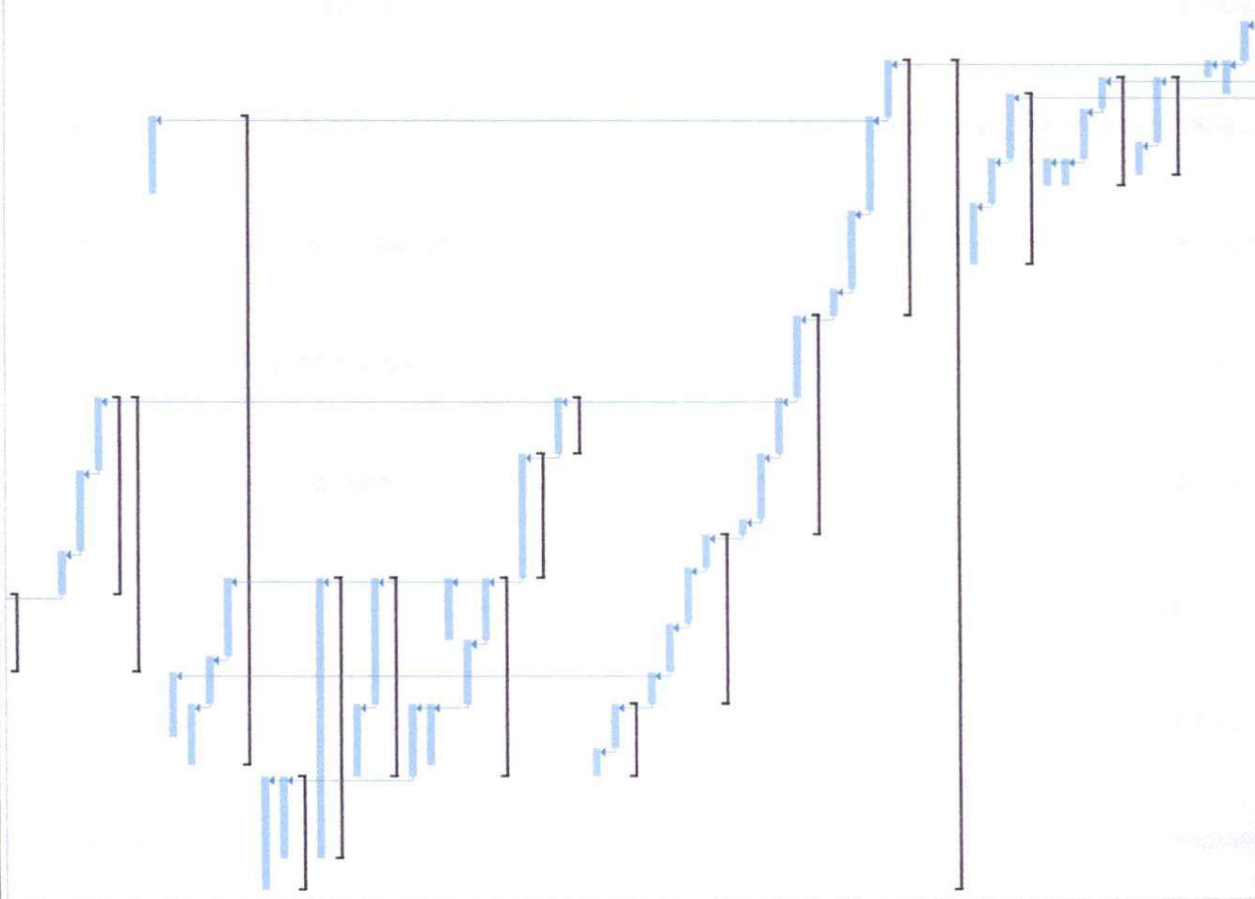

ELABORADO POR: ING. JOFEL CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS



Project: crono Santa Lucia
Date: Thu 30/9/19

Task: []
Summary: []
Inchka Milestone: []
Question-only: []
Sketch-only: []
External Milestone: []
Manual Program: []

13 Oct 19 | 19 Oct 19 | 20 Oct 19 | 27 Oct 19 | 3 Nov 19 | 10 Nov 19 | 17 Nov 19 | 24 Nov 19 | 1 Dec 19 | 8 Dec 19 | 15 Dec 19 | 22 Dec 19 | 29 Dec 19 | 5 Jan 20 | 12 Jan 20 | 19 Jan 20 | 26 Jan 20



ELABORADO POR ING. JOSE CASTILLO
ENCARGADO DE CONTROL DE PROYECTOS

Project: **casas Santa Lucia**
Date: **Thu 30/5/19**

Task: Task Summary Inactive Milestone Milestone

Split: Split Manual Summary Rollup Manual Summary

Inactive Milestone: Inactive Milestone Inactive Summary Manual Task

Summary: Summary Project Summary Inactive Task

Duration only: Duration only Manual Summary Rollup Manual Summary

Start only: Start only Finish only External Tasks

External Milestone: External Milestone Deadline Progress

Manual Progress: Manual Progress
