



 Elaborado por
 Ing. Jofiel Castillo



ID	Task (Mod.)	Duration	Start	Finish	Preced
60	PORTAJE Y ESTANTERIA TODO CAJERA Y METALICAS	67 days	Sat 28/9/19	Sat 7/12/19	
61	PASAMANOS BARRAJAS EN MESA/ME DELE CAMPANARIO DE 150 Y 140 PULO	12 days	Sat 28/9/19	Fri 11/10/19	49
62	PASAMANOS DE 87 PULO PARA DIVIDIR EL ALTAR	10 days	Fri 11/10/19	Tue 22/10/19	61
63	SUMINISTRO E INSTAL. DE PUERTAS NUEVAS EN CAJERA	7 days	Tue 22/10/19	Tue 29/10/19	62
64	REPARACION PUERTAS PRINCIPALES TIEMPO	6 days	Tue 22/10/19	Mon 28/10/19	162
65	REPARACION DE PUERTAS	6 days	Mon 28/10/19	Sat 2/11/19	64
66	REPARACION PUERTAS DE BABEN	5 days	Mon 28/10/19	Fri 1/11/19	64
67	REPARACION DE BANCOS INCLUYE PINTURA	18 days	Sat 2/11/19	Wed 20/11/19	166
68	REPARACION DE UN JUEGO DE COMEDOR	7 days	Thu 21/11/19	Thu 28/11/19	67
69	REPARACION DE ARMARIOS GRANDES	6 days	Thu 28/11/19	Wed 4/12/19	68
70	REPARACION DE ESTANTES GRANDES	3 days	Wed 4/12/19	Sat 7/12/19	69
71	REPARACION DE BOUTAS	3 days	Thu 28/11/19	Sat 30/11/19	68
72	REPARACION DE PANELES TRAGALUZ	12 days	Tue 22/10/19	Sat 2/11/19	62
73	REPAR. VITRINA DE LA VIBRETA ALTA LUCIA	4 days	Sat 28/9/19	Thu 3/10/19	49
74	REPAR. VITRINA DE LA VIBRETA ALTA LUCIA	2 days	Thu 3/10/19	Fri 4/10/19	73
75	REPARACION VENTANILLAS DE ARRIBA EN EL TIEMPO	2 days	Sat 5/10/19	Mon 7/10/19	74
76	REPARACION ENTABLADO CON CRISTAL	2 days	Mon 7/10/19	Wed 9/10/19	75
77	CONSTRUCCION GABINETES Y DEFENSA EN COCINA	5 days	Sat 28/9/19	Fri 4/10/19	49
78	SUMINISTRO E INSTAL. DE PUERTAS METALICAS	4 days	Sat 28/9/19	Thu 3/10/19	49
79	VENTANAS	6 days	Sat 12/10/19	Fri 18/10/19	
80	VENTANAS REFORZADAS CORROZIDAS DE ALUMINO Y VIDRIO EN TIEMPO	3 days	Sat 12/10/19	Tue 15/10/19	27
81	VENTANAS REFORZADAS CORROZIDAS DE ALUMINO Y VIDRIO EN AREAS ADMINISTRATIVAS	3 days	Tue 12/10/19	Fri 18/10/19	80
82	PINTURAS	29 days	Sat 12/10/19	Mon 11/11/19	
83	REMOCCION DE PINTURA EXISTENTE	15 days	Sat 12/10/19	Mon 28/10/19	27
84	MASILLADO Y RELLENO DE SUPERFICIE	6 days	Mon 28/10/19	Sat 2/11/19	83
85	ACRILICA ESPECIAL EN TECHO	4 days	Sat 2/11/19	Thu 7/11/19	84
86	ACRILICA ESPECIAL EN PAREDES EXTERIOR, INTERIOR	8 days	Sat 2/11/19	Mon 11/11/19	84
87	UTILIZACION DE BONDOLA	8 days	Sat 2/11/19	Mon 11/11/19	84
88	MANTENIMIENTO EN PUERTAS	3 days	Thu 7/11/19	Mon 11/11/19	85
89	VARDS	50 days	Sat 28/9/19	Wed 20/11/19	
90	ACERA PERIMETRAL	4 days	Sat 28/9/19	Thu 3/10/19	49
91	PROTECCION DE VENTANAS Y PUERTAS HIERRO	6 days	Fri 18/10/19	Thu 24/10/19	81
92	CANALERA PARA DESAGUE DE TECHOS EN PVC	1 day	Tue 19/11/19	Wed 20/11/19	41
93	SIEMBRA DE GRAMAS Y FLORES	3 days	Thu 3/10/19	Sat 5/10/19	90
94	LIMPIEZA Y PINTURA CAMPANARIO	3 days	Sat 5/10/19	Wed 9/10/19	93
95	LIMPIEZA FINAL	2 days	Wed 9/10/19	Fri 11/10/19	94
96	CONSTRUCCION AREA DE BAÑO EXTERIOR	118 days	Tue 6/8/19	Fri 6/12/19	
97	PANTALLAS GENERALES	11 days	Tue 6/8/19	Sat 17/8/19	
98	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS Y MUROS	3 days	Tue 6/8/19	Fri 9/8/19	4
99	BOITE ESCOMBRO	4 days	Fri 9/8/19	Tue 13/8/19	98
100	LIMPIEZA	4 days	Tue 13/8/19	Sat 17/8/19	99
101	MOVIMIENTO DE TIERRA	9 days	Sat 17/8/19	Tue 27/8/19	
102	EXCAVACION PARA BLOQUE DIVISORIO	2 days	Sat 17/8/19	Mon 19/8/19	100
103	RELLENO DE REPOSICION	2 days	Tue 20/8/19	Wed 21/8/19	102
104	BOITE DE MATERIAL INSENVIBLE	3 days	Wed 21/8/19	Sat 24/8/19	103
105	RELLENO COMPACTADO CALICHE	2 days	Sat 24/8/19	Tue 27/8/19	104
106	HORMONADO ARMADO EN:	4 days	Tue 27/8/19	Fri 30/8/19	
107	ZAPATA DE COLUMNA C1	2 days	Tue 27/8/19	Wed 28/8/19	105
108	COLUMNAS PORTICO S.N.P	2 days	Thu 29/8/19	Fri 30/8/19	107
109	HORMONADO ARMADO S.M.P:	9 days	Fri 30/8/19	Mon 9/9/19	
110	COLUMNAS PORTICO S.N.P	2 days	Mon 2/9/19	Mon 2/9/19	108
111	VISA DINTEL (00)	2 days	Mon 2/9/19	Wed 4/9/19	110
112	VIGA DE CARGA	2 days	Mon 2/9/19	Wed 4/9/19	110
113	LOSAS Y VUELOS	5 days	Wed 4/9/19	Mon 9/9/19	112
114	MUROS BLOQUES	2 days	Tue 20/8/19	Wed 21/8/19	102
115	BLOQUES DE FIBRA DE CARBON	2 days	Tue 20/8/19	Wed 21/8/19	102
116	TERMINACION DE SUPERFICIE	7 days	Wed 21/8/19	Wed 28/8/19	
117	PRAQUACHE SOBRE HORMONADO	2 days	Wed 21/8/19	Fri 23/8/19	115

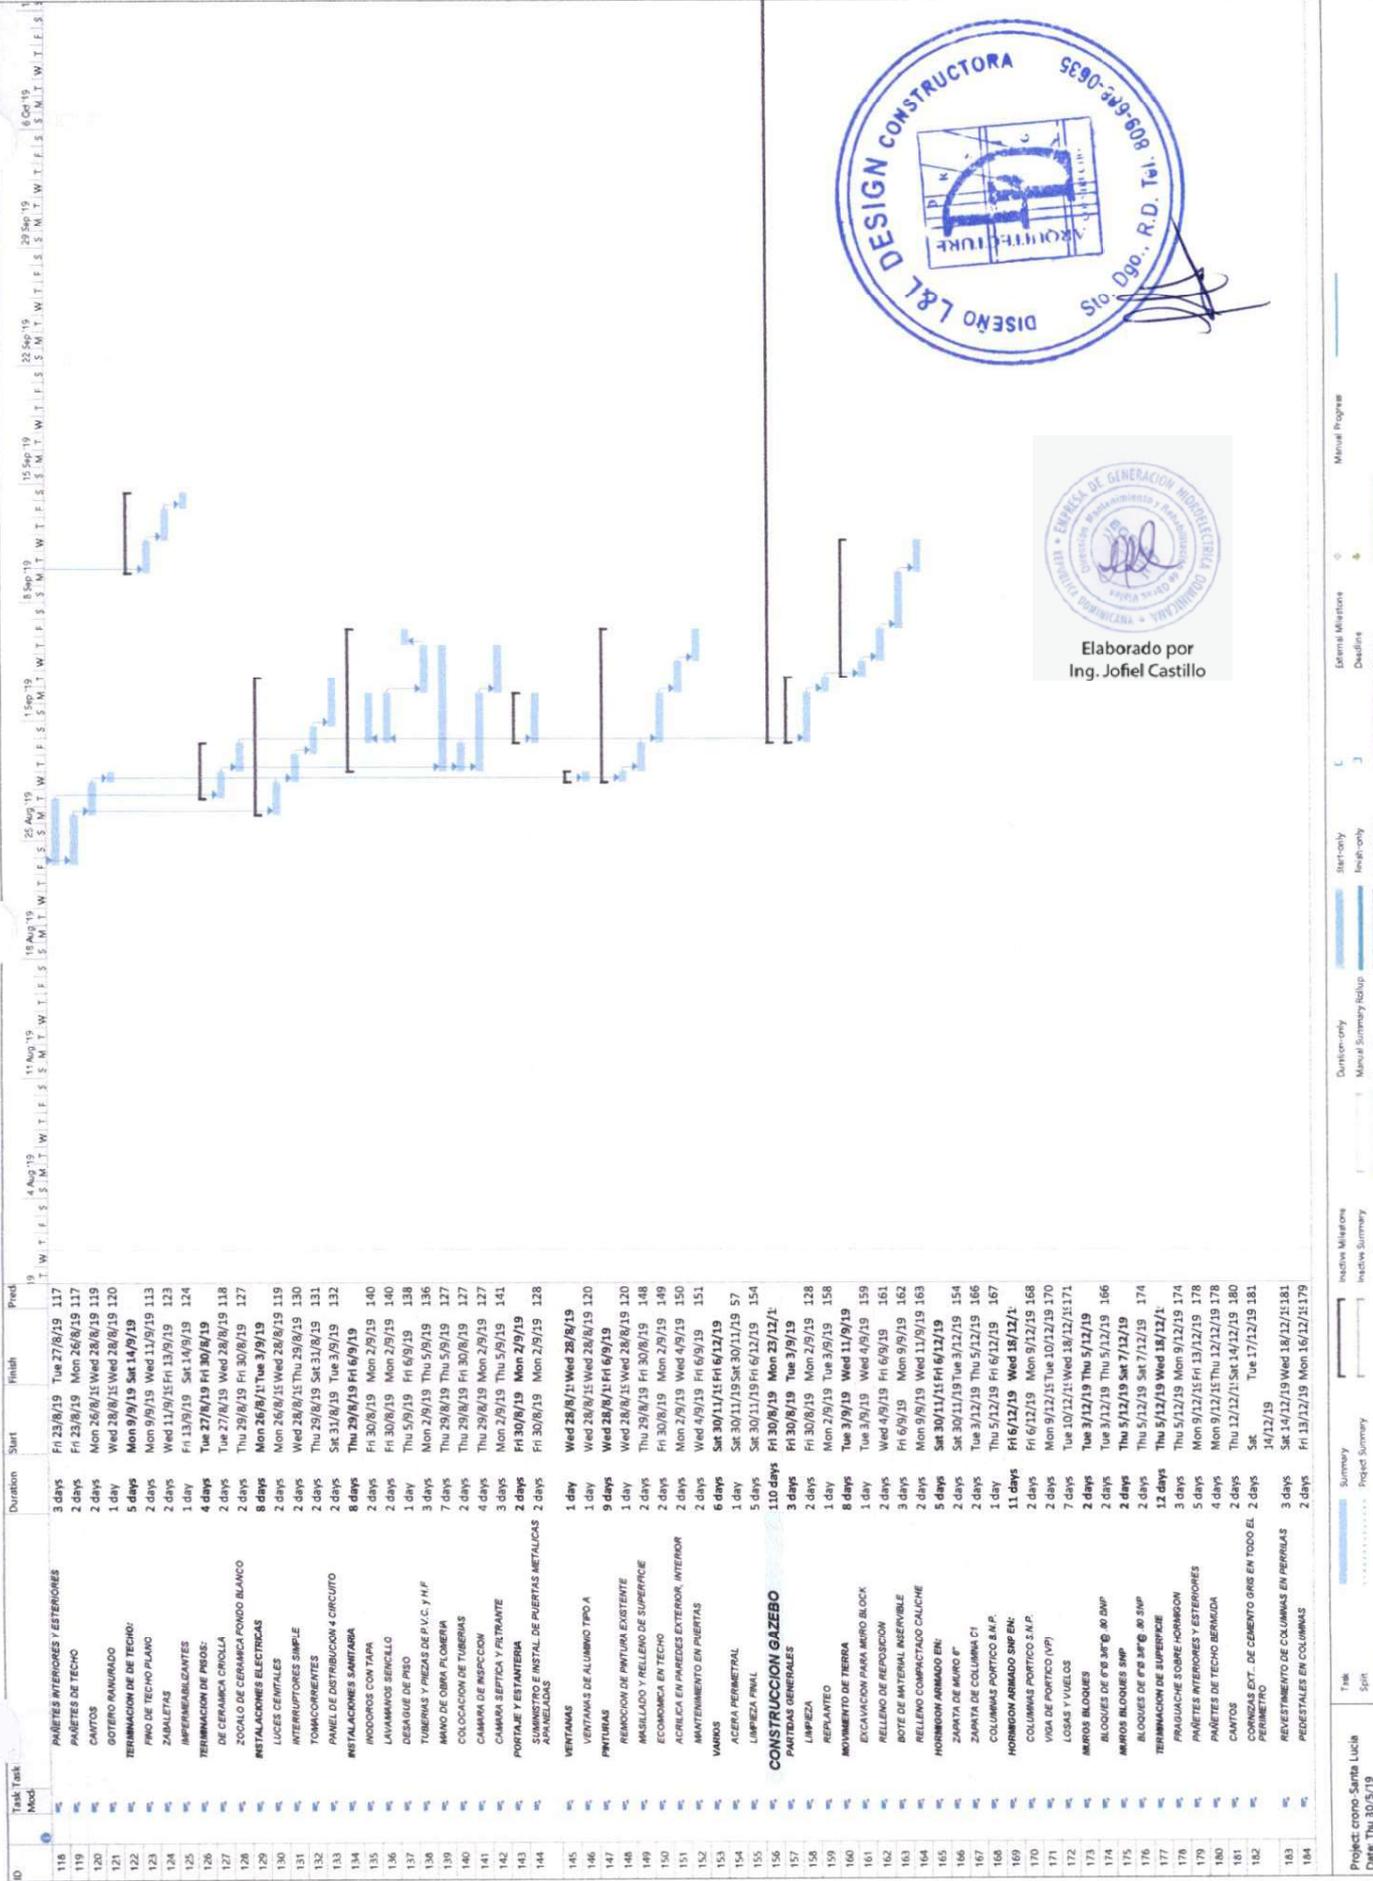

Elaborado por
Ing. Jofiel Castillo

ID	Task/Task Mod	Duration	Start	Finish	Preced
118	PAÑETES INTERIORES Y ESTERNORES	3 days	Fri 23/8/19	Tue 27/8/19	117
119	PAÑETES DE TECHO	2 days	Fri 23/8/19	Mon 26/8/19	117
120	CANTOS	2 days	Mon 26/8/19	Wed 28/8/19	119
121	GOTERO RANURADO	1 day	Wed 28/8/19	Wed 28/8/19	120
122	TERMINACION DE TECHO:	5 days	Mon 9/9/19	Sat 14/9/19	
123	PIPO DE TECHO PLANO	2 days	Mon 9/9/19	Wed 11/9/19	113
124	ZABALETAS	2 days	Wed 11/9/19	Fri 13/9/19	123
125	IMPERMEABILIZANTES	1 day	Fri 13/9/19	Sat 14/9/19	124
126	TERMINACION DE PISO:	4 days	Tue 27/8/19	Fri 30/8/19	
127	DE CERRAMICA CROSLA	2 days	Tue 27/8/19	Wed 28/8/19	118
128	ZOCALO DE CERRAMICA PONGO BLANCO	2 days	Thu 29/8/19	Fri 30/8/19	127
129	INSTALACIONES ELECTRICAS	8 days	Mon 26/8/19	Tue 3/9/19	
130	LUCES CENTIALES	2 days	Mon 26/8/19	Wed 28/8/19	119
131	INTERRUPTORES SIMPLE	2 days	Wed 28/8/19	Thu 29/8/19	130
132	TOMACORRIENTES	2 days	Thu 29/8/19	Sat 31/8/19	131
133	PANEL DE DISTRIBUCION 4 CIRCUITO	2 days	Sat 31/8/19	Tue 3/9/19	132
134	INSTALACIONES SANITARIA	8 days	Fri 30/8/19	Fri 6/9/19	
135	INDOOROS CON TAPA	2 days	Fri 30/8/19	Mon 2/9/19	140
136	LAVAMANOS SENCILLO	2 days	Fri 30/8/19	Mon 2/9/19	140
137	DESAGUE DE PISO	1 day	Thu 5/9/19	Fri 6/9/19	138
138	TUBERIAS Y PIEZAS DE P.V.C. Y H.F	3 days	Mon 2/9/19	Thu 5/9/19	136
139	MAVO DE OBRAS PLOMERIA	7 days	Thu 29/8/19	Thu 5/9/19	127
140	COLOCACION DE TUBERIAS	2 days	Thu 29/8/19	Fri 30/8/19	127
141	CAMARA DE INSPECCION	4 days	Mon 2/9/19	Mon 2/9/19	127
142	CAMARA SEPTICA Y REFRANTE	3 days	Fri 30/8/19	Thu 5/9/19	141
143	PORTALE Y ESTANTERIA	2 days	Fri 30/8/19	Mon 2/9/19	
144	SUMINISTRO E INSTAL. DE PUERTAS METALICAS	2 days	Fri 30/8/19	Mon 2/9/19	128
145	APUNELADAS	1 day	Wed 28/8/19	Wed 28/8/19	
146	VENTANAS DE ALUMINIO TIPO A	1 day	Wed 28/8/19	Wed 28/8/19	120
147	PINTURAS	9 days	Wed 28/8/19	Fri 6/9/19	
148	RENOCION DE PINTURA EXISTENTE	1 day	Wed 28/8/19	Wed 28/8/19	120
149	ASELILLADO Y RELLENO DE SUPERFICIE	2 days	Thu 29/8/19	Fri 30/8/19	148
150	ECONOMICA EN TECHO	2 days	Fri 30/8/19	Mon 2/9/19	149
151	ACHILICA EN PAREDES EXTERIOR, INTERIOR	2 days	Mon 2/9/19	Wed 4/9/19	150
152	MANTENIMIENTO EN PUERTAS	2 days	Wed 4/9/19	Fri 6/9/19	151
153	VARIOS	6 days	Sat 30/11/19	Fri 6/12/19	
154	ACERA PERIMETRAL	1 day	Sat 30/11/19	Sat 30/11/19	57
155	LIMPIEZA FINAL	5 days	Sat 30/11/19	Fri 6/12/19	154
156	CONSTRUCCION GAZEBO	110 days	Fri 30/8/19	Mon 23/12/19	
157	PANTIDAS GENERALES	3 days	Fri 30/8/19	Tue 3/9/19	
158	LIMPIEZA	2 days	Fri 30/8/19	Mon 2/9/19	128
159	REPLANTIO	1 day	Mon 2/9/19	Tue 3/9/19	158
160	MOVIMIENTO DE TIERRA	8 days	Tue 3/9/19	Wed 11/9/19	
161	ELEVACION PARA MURO BLOK	1 day	Tue 3/9/19	Wed 4/9/19	159
162	RELLENO DE REPOSICION	2 days	Wed 4/9/19	Fri 6/9/19	161
163	ROTE DE MATERIAL INSERVIBLE	3 days	Fri 6/9/19	Mon 9/9/19	162
164	RELLENO COMPACTADO CALICHE	2 days	Mon 9/9/19	Wed 11/9/19	163
165	HORMIGON ARMADO EN:	5 days	Sat 30/11/19	Tue 3/12/19	
166	ZARPA DE MURO "	2 days	Sat 30/11/19	Tue 3/12/19	154
167	ZARPA DE COLUMNA CI	2 days	Tue 3/12/19	Thu 5/12/19	166
168	COLUMNAS PORTICO B.A.P.	1 day	Thu 5/12/19	Fri 6/12/19	167
169	HORMIGON ARMADO SMP EN:	11 days	Fri 6/12/19	Wed 18/12/19	
170	COLUMNA PORTICO S.A.P.	2 days	Fri 6/12/19	Mon 9/12/19	168
171	VIGA DE PORTICO (VP)	2 days	Mon 9/12/19	Tue 10/12/19	170
172	LOSAS Y VUELOS	7 days	Tue 10/12/19	Wed 18/12/19	171
173	MUROS BLOQUES	2 days	Tue 3/12/19	Thu 5/12/19	166
174	BLOQUES DE P'8 30" @ 80 DMP	2 days	Tue 3/12/19	Thu 5/12/19	166
175	MUROS BLOQUES SMP	2 days	Thu 5/12/19	Sat 7/12/19	174
176	BLOQUES DE P'8 30" @ 80 SMP	2 days	Thu 5/12/19	Sat 7/12/19	174
177	TERMINACION DE SUPERFICIE	12 days	Thu 5/12/19	Wed 18/12/19	
178	FRAGUACHE SOBRE HORMIGON	3 days	Thu 5/12/19	Mon 9/12/19	174
179	PAÑETES INTERIORES Y ESTERNORES	5 days	Mon 9/12/19	Fri 13/12/19	178
180	PAÑETES DE TECHO BERRIDA	4 days	Mon 9/12/19	Thu 12/12/19	178
181	CANTOS	2 days	Thu 12/12/19	Sat 14/12/19	180
182	CONIZAS EXT. DE CEMENTO GRS EN TODO EL PERIMETRO	2 days	Sat 14/12/19	Tue 17/12/19	181
183	REVESTIMIENTO DE COLUMNAS EN PERRILAS	3 days	Sat 14/12/19	Wed 18/12/19	181
184	PREESTABLES EN COLUMNAS	2 days	Fri 13/12/19	Mon 16/12/19	178

ID	Task Title	Duration	Start	Finish	Predecessors
200	Rego de Impresión 0.6 g/s/m ² con Gavilla	4 days	Sat 11/1/20	Thu 16/1/20 24h	19



Task	Summary	Request Summary	Initial Task	Initial Milestone	Initial Summary	Manual Task	Duration only	Manual Summary (dup)	Manual Summary	Start only	Final only	External Task	External Milestone	Qualifies	Progress	Manual Progress
Task	Summary	Request Summary	Initial Task	Initial Milestone	Initial Summary	Manual Task	Duration only	Manual Summary (dup)	Manual Summary	Start only	Final only	External Task	External Milestone	Qualifies	Progress	Manual Progress

Project: crono-Sana Lucia
Date: Thu 30/5/19

13 Dic 19 20 Dic 19 27 Dic 19 3 Dic 19 10 Dic 19 17 Dic 19 24 Dic 19 31 Dic 19 7 Ene 20 14 Ene 20 21 Ene 20 28 Ene 20 4 Feb 20 11 Feb 20 18 Feb 20 25 Feb 20 3 Mar 20



Elaborado por
Ing. Jofiel Castillo



Project: **proo-Santa Luda**
Date: **Thu 30/5/19**

Task: Task Split Milestone

Summary: Summary Project Summary Inactive Task

Issue Milestone: Issue Milestone Issue Summary Manual Task

Duration-only: Duration-only Manual Summary Manual Summary

Start-only: Start-only Finish only Eventual Task

Eventual Milestone: Eventual Milestone Deadline Program

Manual Program: Manual Program

19 Oct 19 20 Oct 19 27 Oct 19 29 Oct 19 30 Oct 19 31 Oct 19 01 Nov 19 02 Nov 19 03 Nov 19 04 Nov 19 05 Nov 19 06 Nov 19 07 Nov 19 08 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 05 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20




Elaborado por
Ing. Jofiel Castillo



Project: **crono-Santa Lucia**
Date: **Thu 30/5/19**

Task	Summary	Inactive Milestone	Duration-only	Start-only	Manual Progress
Split	Project Summary	Inactive Summary	Manual Summary Setup	Finish-only	
Milestone	Inactive Task	Manual Task	Manual Summary	Estimate Task	Deadline

15 Oct 19 16 Oct 19 17 Oct 19 18 Oct 19 19 Oct 19 20 Oct 19 21 Oct 19 22 Oct 19 23 Oct 19 24 Oct 19 25 Oct 19 26 Oct 19 27 Oct 19 28 Oct 19 29 Oct 19 30 Oct 19 31 Oct 19 1 Nov 19 2 Nov 19 3 Nov 19 4 Nov 19 5 Nov 19 6 Nov 19 7 Nov 19 8 Nov 19 9 Nov 19 10 Nov 19 11 Nov 19 12 Nov 19 13 Nov 19 14 Nov 19 15 Nov 19 16 Nov 19 17 Nov 19 18 Nov 19 19 Nov 19 20 Nov 19 21 Nov 19 22 Nov 19 23 Nov 19 24 Nov 19 25 Nov 19 26 Nov 19 27 Nov 19 28 Nov 19 29 Nov 19 30 Nov 19 1 Dec 19 2 Dec 19 3 Dec 19 4 Dec 19 5 Dec 19 6 Dec 19 7 Dec 19 8 Dec 19 9 Dec 19 10 Dec 19 11 Dec 19 12 Dec 19 13 Dec 19 14 Dec 19 15 Dec 19 16 Dec 19 17 Dec 19 18 Dec 19 19 Dec 19 20 Dec 19 21 Dec 19 22 Dec 19 23 Dec 19 24 Dec 19 25 Dec 19 26 Dec 19 27 Dec 19 28 Dec 19 29 Dec 19 30 Dec 19 31 Dec 19 1 Jan 20 2 Jan 20 3 Jan 20 4 Jan 20 5 Jan 20 6 Jan 20 7 Jan 20 8 Jan 20 9 Jan 20 10 Jan 20 11 Jan 20 12 Jan 20 13 Jan 20 14 Jan 20 15 Jan 20 16 Jan 20 17 Jan 20 18 Jan 20 19 Jan 20 20 Jan 20 21 Jan 20 22 Jan 20 23 Jan 20 24 Jan 20 25 Jan 20 26 Jan 20 27 Jan 20 28 Jan 20 29 Jan 20 30 Jan 20 31 Jan 20

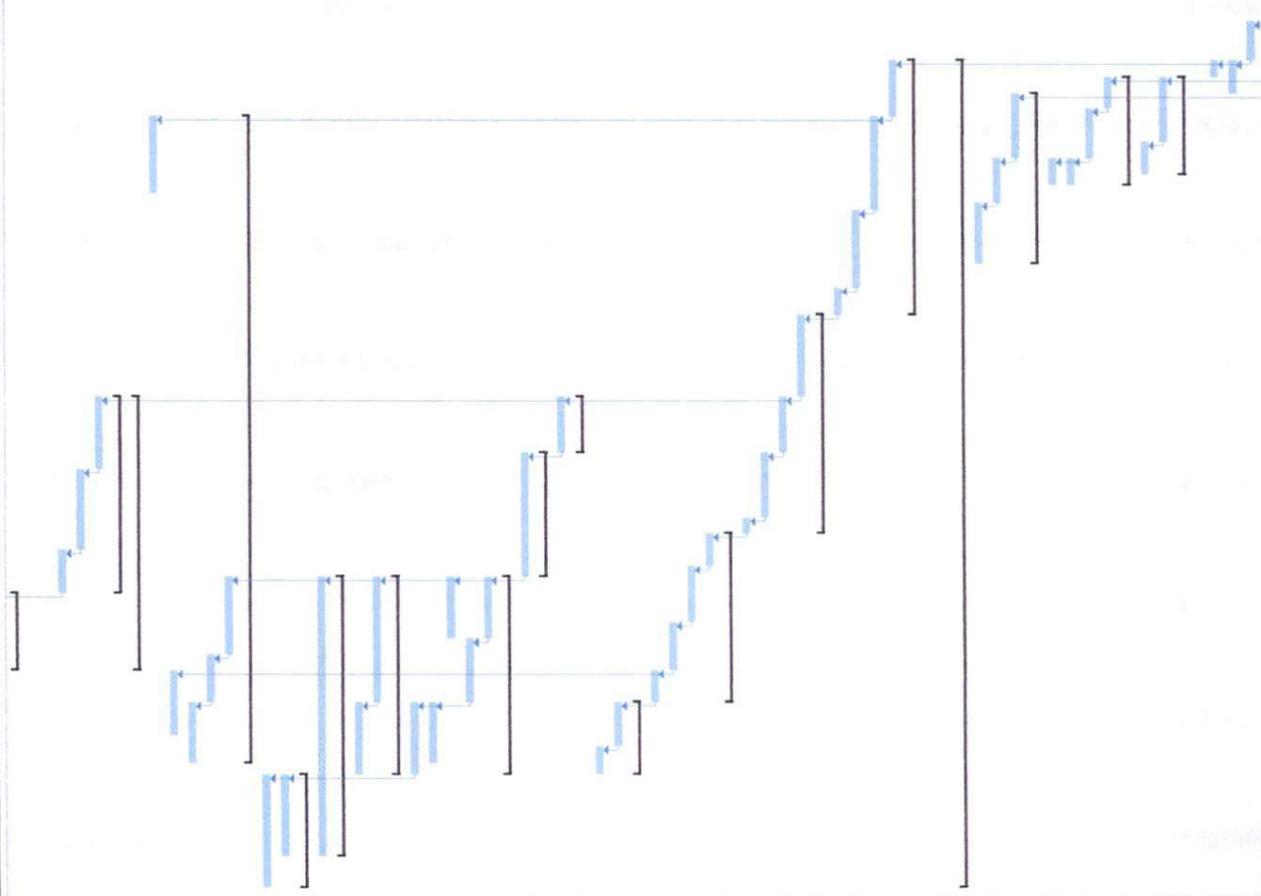

Elaborado por
Ing. Jofiel Castillo



Project: crono Santa Lucia
Order: THU 30/5/19

Task
Sign
Milestone
Summary
Fixed Summary
Inchka Task
Inchka Milestone
Inchka Summary
Manual Task
Question-only
Manual Summary (edit)
Manual Summary
Sketch-only
Inchka-only
External Task
External Milestone
Deadline
Project
Manual Program

