


ID	Tarea	Nombre de tarea	Duration	Start	Finish	Predecessor Names
1	CUARTEL POLICIAL	78 days	Mon 4/13/20	Wed 7/29/20		
2	PRIMER NIVEL	43 days	Mon 4/13/20	Wed 6/10/20		
3	PARTIDAS GENERALES	4 days	Mon 4/13/20	Thu 4/15/20		
4	Limpieza y Replanteo	2 days	Mon 4/13/20	Tue 4/14/20		
5	Induye charrechia	2 days	Wed 4/15/20	Thu 4/16/20		
6	Caseta de Materiales	2 days	Wed 4/15/20	Thu 4/16/20		
7	MOVIMIENTO DE TIERRA 15 days	15 days	Fri 4/17/20	Thu 5/7/20		
8	Demolicion de	2 days	Fri 4/17/20	Mon 4/20/20		
9	Estructuras de Hormigon	3 days	Tue 4/21/20	Thu 4/23/20		
10	Excavacion en Material C2	2 days	Fri 4/24/20	Mon 4/27/20		
11	Excavacion Zanja de Mz	2 days	Tue 4/28/20	Wed 4/29/20		
12	Excavacion C1	2 days	Tue 4/28/20	Wed 4/29/20		
13	Replanteo de Responsion	1 day	Wed 5/6/20	Wed 5/6/20		
14	Replanteo Competicion en 1 day	1 day	Thu 5/7/20	Thu 5/7/20		
15	Replanteo de Responsion	1 day	Thu 4/30/20	Thu 4/30/20		
16	HORMIGON ARMADO EK. 32 days	32 days	Mon 4/13/20	Tue 5/25/20		
17	Zapatas para Muros de	4 days	Thu 4/30/20	Tue 5/12/20		
18	Columnas para Muros de	4 days	Thu 4/30/20	Tue 5/12/20		
19	Columnas para Columnas	4 days	Thu 4/30/20	Tue 5/12/20		
20	Columnas de Amarras	4 days	Wed 5/6/20	Mon 5/11/20		
21	Columnas Circulares de 14 days	14 days	Wed 5/6/20	Mon 5/11/20		
22	Columnas de Amarras	4 days	Tue 5/12/20	Fri 5/15/20		
23	Vigas de Amarras	4 days	Wed 5/6/20	Mon 5/11/20		
24	Vigas de Amarras	4 days	Wed 5/6/20	Mon 5/11/20		
25	Viga 0.10x2.0	4 days	Wed 5/6/20	Mon 5/11/20		
26	Dientes 0.15m x 0.20m	1 day	Wed 5/6/20	Wed 5/6/20		
27	Dintel Puerta Frontal	1 day	Wed 5/6/20	Wed 5/6/20		
28	Relanzos Plancha 14'30x2'3	2 days	Tue 5/12/20	Wed 5/13/20		
29	Losa de Techo enl-14m, 4 days	4 days	Tue 5/12/20	Fri 5/15/20		
30	Muros de Bloques	1 day	Mon 4/13/20	Mon 4/13/20		
31	Buques Hom. 6' 01/2' 2 days	2 days	Mon 5/18/20	Tue 5/19/20		
32	Buques Hom. 6' 01/2' 7 days	7 days	Mon 5/18/20	Tue 5/25/20		
33	Buques Hom. 4' 01/2' 2 days	2 days	Mon 5/18/20	Tue 5/19/20		
34	Buques Hom. 4' 01/2' 4 days	4 days	Mon 5/18/20	Thu 5/21/20		
35	TERMINACION DE SUPER 7 days	7 days	Mon 5/18/20	Tue 5/25/20		
36	Paralelo en Muros Exteriores	5 days	Wed 5/20/20	Thu 5/24/20		
37	Paralelo en Muros Exteriores	5 days	Wed 5/20/20	Thu 5/24/20		
38	Foguetas sobre superficie	3 days	Wed 5/20/20	Fri 5/22/20		
39	Cortes en general	3 days	Fri 5/22/20	Tue 5/25/20		
40	Estrías o alio relieve	2 days	Fri 5/22/20	Mon 5/25/20		
41	VENIVANAS	6 days	Wed 5/27/20	Wed 6/3/20		
42	Ventanas Cortadas de 4 days	4 days	Wed 5/27/20	Mon 6/1/20		
43	Aluminio y Cristal	2 days	Tue 6/2/20	Wed 6/3/20		
44	PUERTAS	5 days	Wed 5/27/20	Wed 6/3/20		
45	Puerta en Aluminio y Cristal	1 day	Wed 5/27/20	Wed 5/27/20		
46	Puerta Polimetal 0.80m	1 day	Wed 5/27/20	Wed 5/27/20		
47	Puerta de Hierro 0.80x2.1	1 day	Wed 5/27/20	Wed 5/27/20		
48	Ripias de Hierro en acropolis	2 days	Mon 6/1/20	Mon 6/1/20		
49	Gabinete de Pied en 1 day	1 day	Wed 5/27/20	Wed 5/27/20		
50	Tubo de Galva Natural	1 day	Tue 6/2/20	Tue 6/2/20		
51	TERMINACION DE PISOS 7 days	7 days	Tue 5/26/20	Wed 6/3/20		
52	Piso en Pisos	3 days	Wed 5/27/20	Fri 5/29/20		
53	Zoclos de piso	3 days	Mon 6/1/20	Wed 6/3/20		
54	Acera (Vehículo en 3 days	3 days	Tue 5/26/20	Thu 5/28/20		
55	Acera (Vehículo en 3 days	3 days	Tue 5/26/20	Thu 5/28/20		
56	REVESTIMIENTO EN PARIQ 2 days	2 days	Wed 5/27/20	Thu 5/28/20		
57	Ceramica fropadas	2 days	Wed 5/27/20	Thu 5/28/20		
58	Instalaciones sanitarias	1 day	Wed 5/27/20	Wed 5/27/20		
59	Instalaciones sanitarias	1 day	Wed 5/27/20	Wed 5/27/20		
60	Instalaciones sanitarias	1 day	Wed 5/27/20	Wed 5/27/20		
61	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
62	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
63	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
64	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
65	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
66	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
67	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
68	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
69	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
70	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
71	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
72	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
73	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
74	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
75	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		
76	Instalaciones sanitarias	1 day	Tue 5/26/20	Tue 5/26/20		



Elaborado por
Ing. Jofiel Castillo

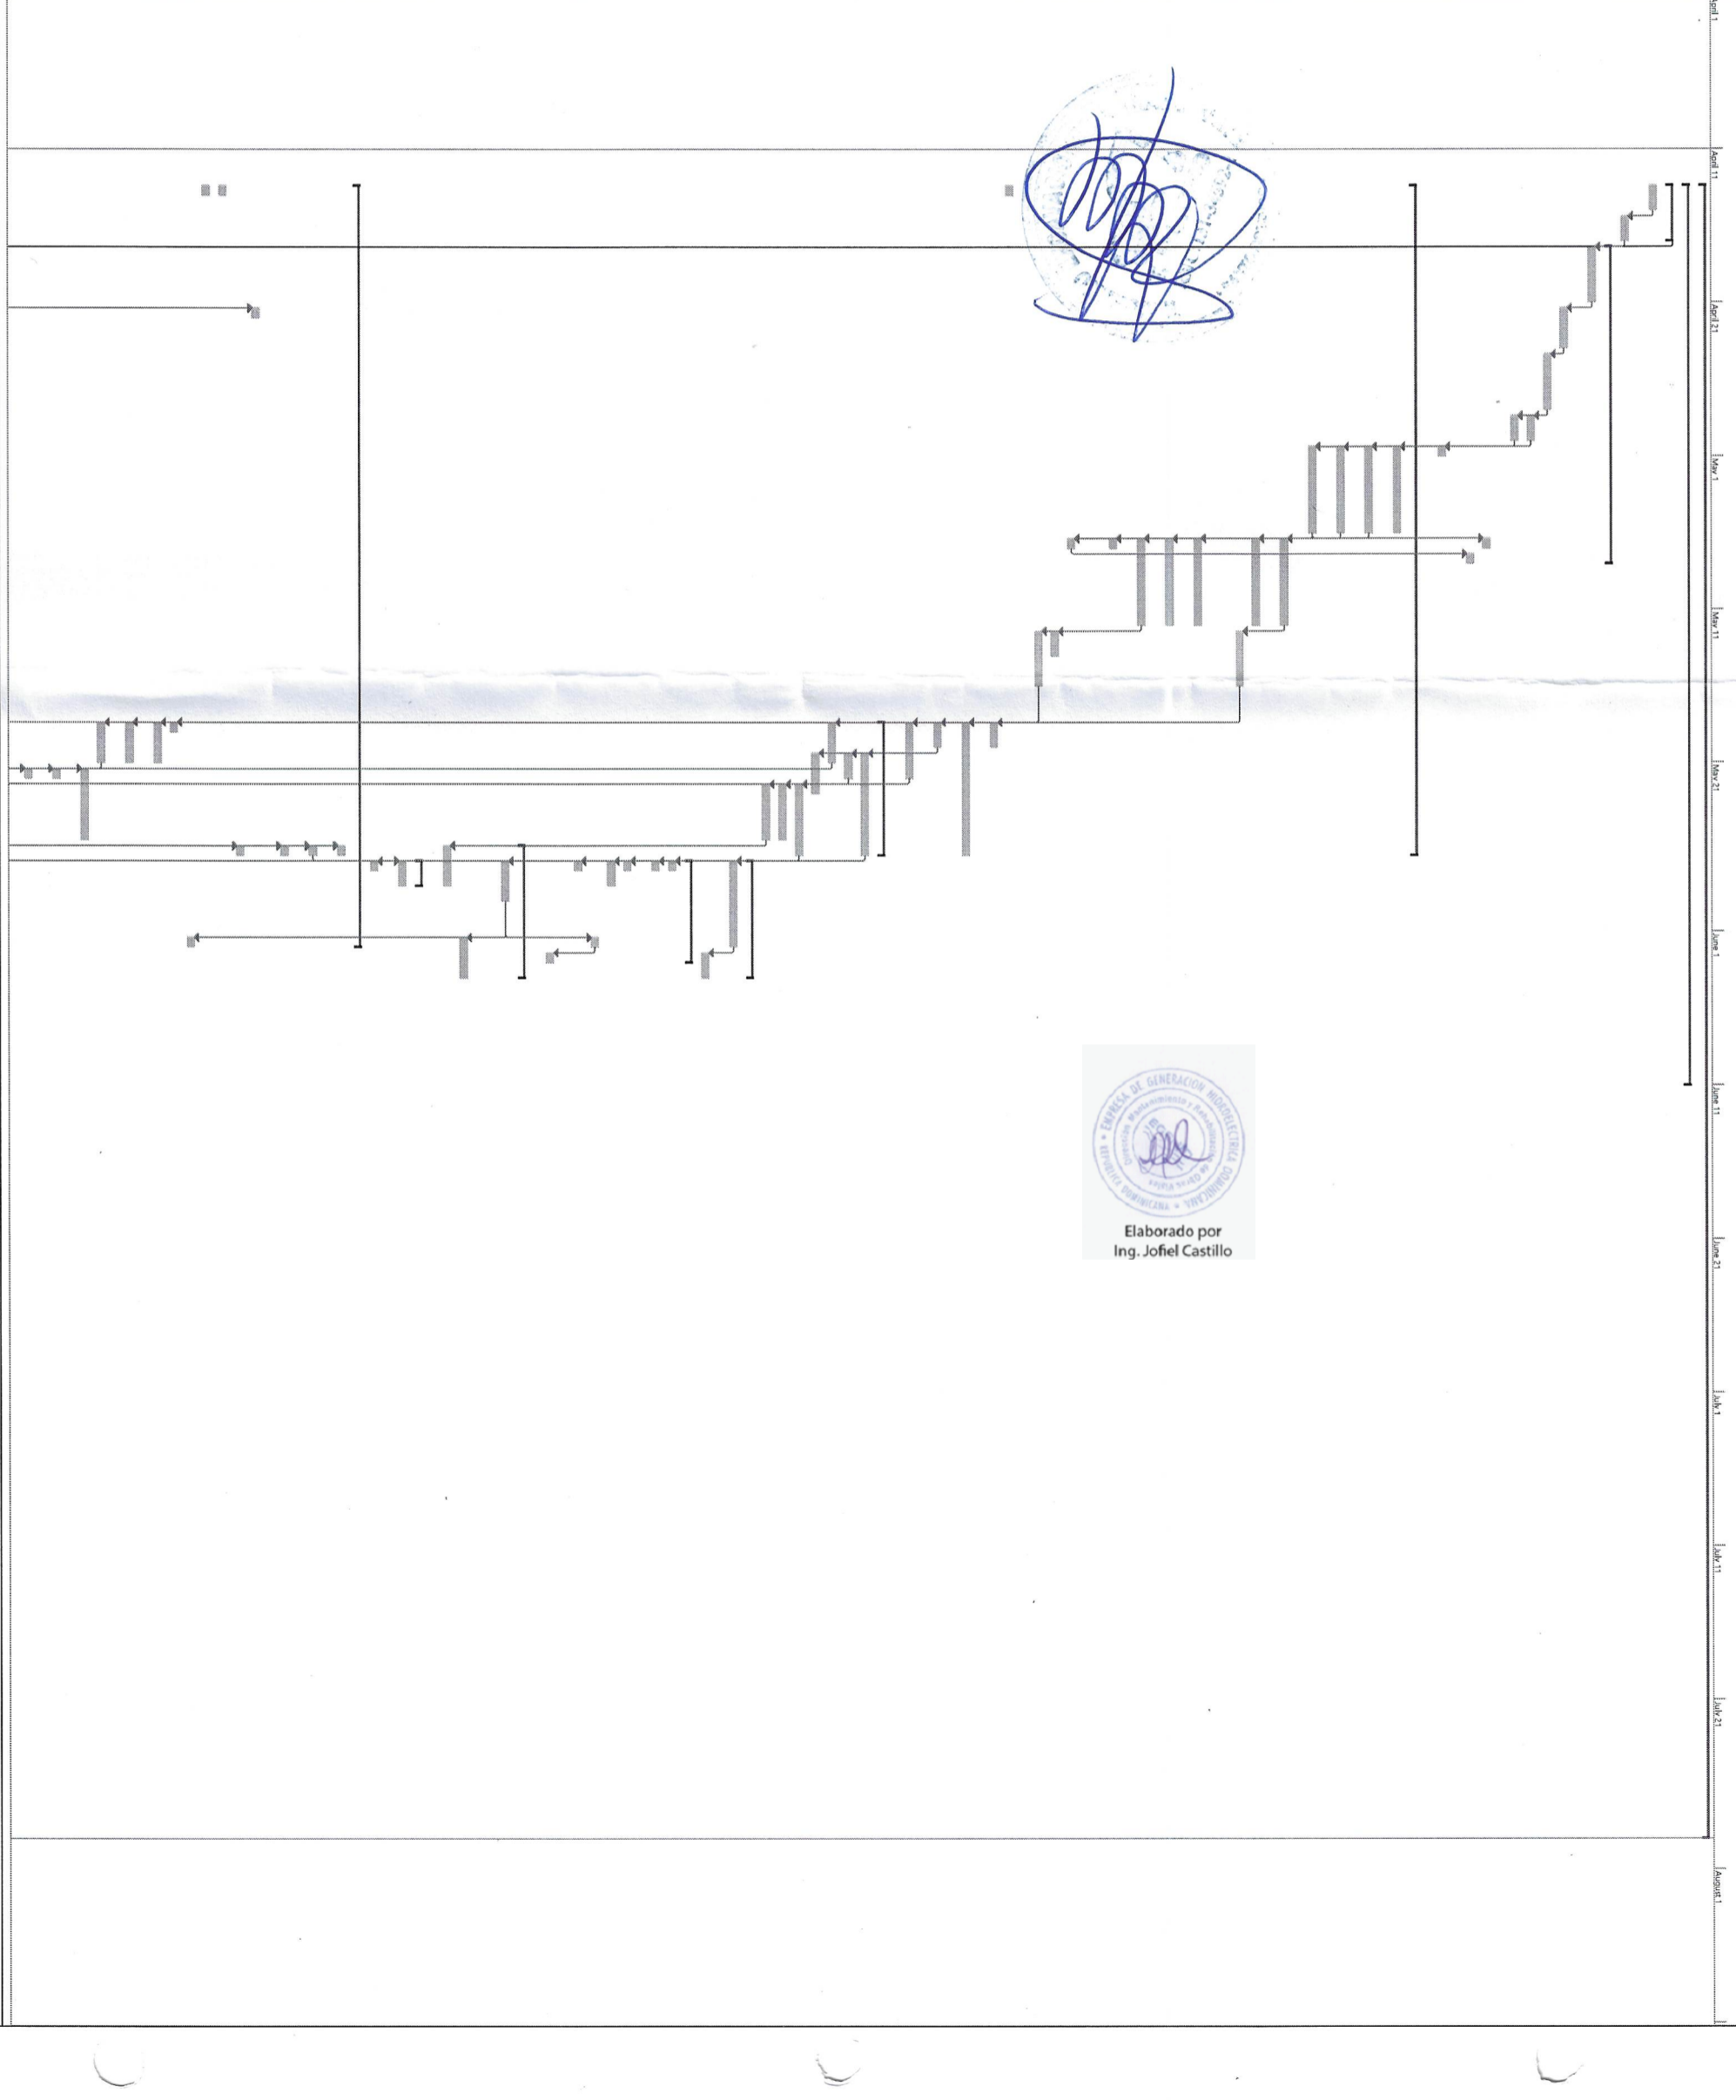
