

ID	Task	Mod	Start	Finish	Duration	Preced
1	IGLESIA SANTA LUCIA, N. ITAS DE FARFAN		Thu 1/8/19	Wed 19/12/20	174.5 days	
2	IGLESIA Y AREA: ADMINISTRATIVAS 134 days		Thu 1/8/19	Wed 18/12/19	134 days	
3	PARTES GENERALES		Thu 1/8/19	Sat 24/8/19	23 days	
4	DEMOLICIONES DE		Thu 1/8/19	Tue 6/8/19	5 days	
5	DEMOLICIONES DE MUROS EN EL GRAN SALON		Tue 6/8/19	Fri 9/8/19	3 days	
6	ROTE ESCOMBRO (1 CILINDRO DE 8 MB)		Fri 9/8/19	Sat 17/8/19	8 days	
7	LIMPIEZA		Sat 17/8/19	Thu 22/8/19	5 days	
8	REPLANTEO		Thu 22/8/19	Sat 24/8/19	2 days	
9	MOVIMIENTO DE TIERRA		Sat 24/8/19	Tue 10/9/19	16 days	
10	ENCUAVACION PARA MURO BLOCC DIVISORIO		Thu 10/9/19	Sat 14/9/19	4 days	
11	RELLENO DE REPO CON		Sat 14/9/19	Wed 28/8/19	10 days	
12	BOTE DE MATERIAL INSECTICIDA		Wed 28/8/19	Thu 5/9/19	4 days	
13	RELLENO COMPACTO CALICHE		Thu 5/9/19	Tue 10/9/19	5 days	
14	HORMICON ARMADO 14"		Tue 10/9/19	Fri 20/9/19	10 days	
15	ZAPATA DE MURO 1 DIVISORIO		Fri 20/9/19	Sat 14/9/19	4 days	
16	ZAPATA DE COLUMNA CT		Sat 14/9/19	Tue 17/9/19	3 days	
17	COLUMNAS PORTIC 3 B.N.P.		Tue 17/9/19	Fri 20/9/19	3 days	
18	HORMICON ARMADO 14" EN		Fri 20/9/19	Fri 27/9/19	7 days	
19	COLUMNAS PORTIC 3 B.N.P.		Fri 27/9/19	Wed 25/9/19	4 days	
20	VIGA DAPTEL (V)		Wed 25/9/19	Fri 27/9/19	3 days	
21	MUROS BLOQUES		Fri 27/9/19	Thu 1/10/19	48 days	
22	MUROS BLOQUES 14"		Thu 1/10/19	Thu 1/10/19	1 day	
23	BLOQUES DE 14" X 14" X 14"		Thu 1/10/19	Thu 1/10/19	1 day	
24	TERMINACION DE SUPERFICIE		Thu 1/10/19	Wed 25/9/19	5 days	
25	FRAGUACHE SOBRE HORMICON		Wed 25/9/19	Sat 19/10/19	24 days	
26	PANETES INTERIORES Y EXTERIORES EL 20%		Sat 19/10/19	Mon 30/9/19	5 days	
27	CANTOS		Mon 30/9/19	Tue 8/10/19	8 days	
28	CORNIZAS EXT. DE CEMENTO EN TODO EL PERIMETRO		Tue 8/10/19	Sat 12/10/19	4 days	
29	CORNIZAS INTERIORES DE YESO TODO PERIMETRO		Sat 12/10/19	Thu 17/10/19	5 days	
30	DIBUÑO DECORATIVO UN CORNIZA ARCO		Thu 17/10/19	Thu 14/11/19	27 days	
31	EN PARTE FRONTAL DEL EDIFICIO		Thu 14/11/19	Tue 22/10/19	4 days	
32	REVESTIMIENTO DE COLUMNAS EN MARMOL		Tue 22/10/19	Sat 26/10/19	5 days	
33	PREDESTALES EN COLUMNAS		Sat 26/10/19	Wed 30/10/19	3 days	
34	REVESTIMIENTO DE COLUMNAS EN PIEDRA		Wed 30/10/19	Fri 1/11/19	3 days	
35	GOTERO RAINWATER		Fri 1/11/19	Tue 5/11/19	3 days	
36	SUMINISTRO E INST. DE UN CRISTO EN BRONCE		Tue 5/11/19	Mon 11/11/19	5 days	
37	TRABAJOS ARTISTICO EN EL PRENTE DEL TEMPLO		Mon 11/11/19	Thu 14/11/19	4 days	
38	CONSTRUCCION Y TERMINACION DE DE TECHO:		Thu 14/11/19	Mon 25/11/19	10 days	
39	CONSTRUCCION CUBIERTA DEL TECHO		Mon 25/11/19	Mon 25/11/19	1 day	
40	EN TIJAS METALICAS		Mon 25/11/19	Thu 14/11/19	6 days	
41	FINO DE TECHO PLANO		Thu 14/11/19	Tue 19/11/19	4 days	
42	TERMINACION DE DE TECHO EN DUKON		Tue 19/11/19	Mon 25/11/19	6 days	
43	ZABALETAS		Mon 25/11/19	Wed 20/11/19	2 days	
44	APUNTEALIZANTES		Wed 20/11/19	Fri 22/11/19	2 days	
45	TERMINACION DE PISO:		Fri 22/11/19	Thu 19/11/19	18 days	
46	DE CERAMICA ESPANOLA DE 14" FONDO BLANCO		Thu 19/11/19	Wed 27/10/19	12 days	
47	ZOCALO DE CERAMICA FONDO BLANCO		Wed 27/10/19	Tue 8/10/19	6 days	
48	REVESTIMIENTO DE JARDINERAS EN LAORLOS		Tue 8/10/19	Wed 25/9/19	5 days	
49	LACILLOS DE ENTRADA PUERTA PRINCIPAL		Wed 25/9/19	Sat 28/9/19	4 days	
50	INSTALACIONES ELECTRICAS		Sat 28/9/19	Mon 25/11/19	22 days	
51	LUCES LAMPARA DECORATIVAS COLGANTES		Mon 25/11/19	Fri 28/12/19	5 days	
52	LUCES LAMPARA EN COLUMNAS		Fri 28/12/19	Sat 30/11/19	7 days	
53	LAMPARAS DECORATIVAS EN PRENTE DEL TEMP		Sat 30/11/19	Mon 9/12/19	2 days	
54	INTERRUPTORES DOBLES		Mon 9/12/19	Fri 13/12/19	4 days	
55	INTERRUPTORES SIMPLE		Fri 13/12/19	Wed 18/12/19	4 days	
56	TOMACORRIENTES		Wed 18/12/19	Tue 17/12/19	3 days	
57	TRABAJOS DE INSTALACION DE LAMPARAS DE AJES ACCIONADOS DE 1600 BTU INVERTER		Tue 17/12/19	Wed 25/11/19	3 days	
58	PANEL DE DISTRIBUCION 15 CIRCUITOS		Wed 25/11/19	Wed 27/11/19	2 days	
59	BAJO DE OBRA		Wed 27/11/19	Mon 25/11/19	5 days	

Elaborado por
Ing. Jofiel Castillo




Elaborado por
Ing. Jofiel Castillo

Legend:

- Task: Blue bar
- Milestone: Yellow diamond
- Summary: Blue bar with white text
- Project Summary: Blue bar with white text
- Progress: Blue bar with white text
- External Task: Blue bar with white text
- External Milestone: Yellow diamond
- Start only: Blue bar with white text
- Finish only: Blue bar with white text
- Duration only: Blue bar with white text
- Manual Summary: Blue bar with white text
- Manual Task: Blue bar with white text
- Manual Milestone: Yellow diamond
- Manual Project Summary: Blue bar with white text
- Manual Progress: Blue bar with white text

ID	Task Name	Duration	Start	Finish	Preced
60	PORTAL Y ESTANTES EN TODO CABAÑA Y METALICAS	67 days	Sat 28/8/19	Sat 7/12/19	
61	PASAMAROS BARRILAS EN MESA DE ALUMINIO DEL CAMPANARIO DE 11 Y 148 PULG	12 days	Sat 28/8/19	Fri 11/10/19	60
62	PASAMAROS DE 87 PULG PARA DIVIDIR EL ALTAR	10 days	Fri 11/10/19	Tue 22/10/19	61
63	SUMINISTRO E INSTALACION DE PUERTAS NUEVAS EN 7 CABAÑAS	7 days	Tue 22/10/19	Tue 29/10/19	62
64	REPARACION PUERTAS PRINCIPALES TEMPLO	6 days	Tue 22/10/19	Mon 28/10/19	63
65	REPARACION DE PUERTAS DE BARRILAS	6 days	Mon 28/10/19	Sat 27/11/19	64
66	REPARACION DE BARRILAS INCLUYE PINTURA	5 days	Mon 28/10/19	Fri 11/11/19	65
67	REPARACION DE UJUEGO DE COMEDOR	18 days	Sat 27/11/19	Wed 20/12/19	66
68	REPARACION DE AJUAROS GRANDES	7 days	Thu 28/11/19	Thu 28/11/19	67
69	REPARACION DE ESTANTES GRANDES	6 days	Wed 4/12/19	Wed 4/12/19	68
70	REPARACION DE ESTANTES GRANDES	3 days	Wed 4/12/19	Sat 7/12/19	69
71	REPARACION DE BARRILAS	3 days	Thu 28/11/19	Sat 30/11/19	70
72	REPARACION DE PANELES TRIANGULOS	12 days	Tue 22/10/19	Sat 27/11/19	71
73	REPARA VITRINA DE LA VIRGEN STA. LUCIA	4 days	Sat 28/9/19	Thu 3/10/19	72
74	REPARA VITRINA DE LA VIRGEN ALTA GRACIA	2 days	Thu 3/10/19	Fri 4/10/19	73
75	REPARACION VENTANILLAS DE AFRIMA EN EL TEMPLO	2 days	Sat 5/10/19	Mon 7/10/19	74
76	REPARACION ENTALLADO CON CRISTAL	2 days	Mon 7/10/19	Wed 9/10/19	75
77	CONSTRUCCION GABINETES Y DEFENSA EN COCINA	5 days	Sat 28/9/19	Fri 4/10/19	76
78	SUMINISTRO E INSTALACION DE PUERTAS METALICAS APARELLADAS	4 days	Sat 28/9/19	Thu 3/10/19	77
79	VENTANAS	6 days	Sat 12/10/19	Fri 18/10/19	78
80	VENTANAS REFORZADAS CORREDORES DE ALUMINIO Y VIDRIO EN TEMPLO	3 days	Sat 12/10/19	Tue 15/10/19	79
81	VENTANAS REFORZADAS CORREDORES DE ALUMINIO Y VIDRIO EN AREAS ADMINISTRATIVAS	3 days	Tue 15/10/19	Fri 18/10/19	80
82	PINTURAS	29 days	Sat 12/10/19	Mon 11/11/19	
83	RENOVACION DE PINTURA EXISTENTE	15 days	Sat 12/10/19	Mon 28/10/19	82
84	MAILLADO Y RELLENO DE SUPERFICIE ACRILOCA ESPECIAL EN TECHO	4 days	Mon 28/10/19	Sat 27/11/19	83
85	ACRILOCA ESPECIAL EN PAREDES EXTERIOR INTERIOR	8 days	Sat 27/11/19	Mon 11/12/19	84
86	UTILIZACION DE GOMOLLA	8 days	Sat 27/11/19	Mon 11/12/19	85
87	MANTENIMIENTO EN PUERTAS	3 days	Thu 7/11/19	Mon 11/11/19	86
88	VARIOS	50 days	Sat 28/9/19	Wed 20/11/19	87
89	ACERA PERIMETRAL	4 days	Sat 28/9/19	Thu 3/10/19	88
90	PROTECCION DE VENTANAS Y PUERTAS INTERIORES	6 days	Fri 18/10/19	Thu 24/10/19	89
91	CANALITA PARA DESAGUE DE TECHOS PVC	1 day	Tue 19/11/19	Wed 20/11/19	90
92	SEMIORA DE GRAMAS Y FLORES	3 days	Thu 3/10/19	Sat 5/10/19	91
93	LIMPIEZA Y PINTURA CAMPANARIO	3 days	Sat 5/10/19	Wed 9/10/19	92
94	LIMPIEZA FINAL	2 days	Wed 9/10/19	Fri 11/10/19	93
95	CONSTRUCCION AREA DE BAÑO EXTERIOR	118 days	Tue 6/8/19	Fri 6/12/19	
96	PAREDES GENERALES	11 days	Tue 6/8/19	Sat 17/8/19	95
97	DEMOLICIONES DE PISOS EN SALONES Y AREAS ADMINISTRATIVAS Y MUROS	3 days	Tue 6/8/19	Fri 9/8/19	96
98	BOITE ESCOMBRO	4 days	Fri 9/8/19	Tue 13/8/19	97
99	LIMPIEZA	4 days	Tue 13/8/19	Sat 17/8/19	98
100	MOVIMIENTO DE TIERRA	9 days	Sat 17/8/19	Tue 27/8/19	99
101	EXCAVACION PARA MURO BLOQUE CEMENTADO	2 days	Tue 27/8/19	Mon 19/8/19	100
102	RELLENO DE REPOSICION	2 days	Tue 27/8/19	Wed 21/8/19	101
103	BOITE DE MATERIAL INSERVIBLE	3 days	Wed 21/8/19	Sat 24/8/19	102
104	RELLENO COMPACTADO CALICHE	2 days	Sat 24/8/19	Tue 27/8/19	103
105	HORMICON ARMADO EN:	4 days	Tue 27/8/19	Fri 30/8/19	104
106	ZARZA DE COLUMNA C1	2 days	Tue 27/8/19	Wed 28/8/19	105
107	COLUMNA PORTICO B.A.P	2 days	Thu 29/8/19	Fri 30/8/19	106
108	HORMICON ARMADO SMP EN:	9 days	Fri 30/8/19	Mon 9/9/19	107
109	COLUMNA PORTICO S.A.P	2 days	Fri 30/8/19	Mon 2/9/19	108
110	VIGA DENTEL (VO)	2 days	Mon 2/9/19	Wed 4/9/19	109
111	VIGA DE CARGA	2 days	Mon 2/9/19	Wed 4/9/19	110
112	LOSAS Y VUELOS	5 days	Wed 4/9/19	Mon 9/9/19	111
113	MAROS BLOQUES	2 days	Tue 20/8/19	Wed 21/8/19	112
114	BLOQUES DE 6'x 6' @ SMP	2 days	Tue 20/8/19	Wed 21/8/19	113
115	TERMINACION DE SUPERFICIE FRAGUACHE SOBRE HORMICON	7 days	Wed 21/8/19	Wed 28/8/19	114
116		2 days	Wed 21/8/19	Wed 28/8/19	115
117		2 days	Wed 21/8/19	Wed 28/8/19	116

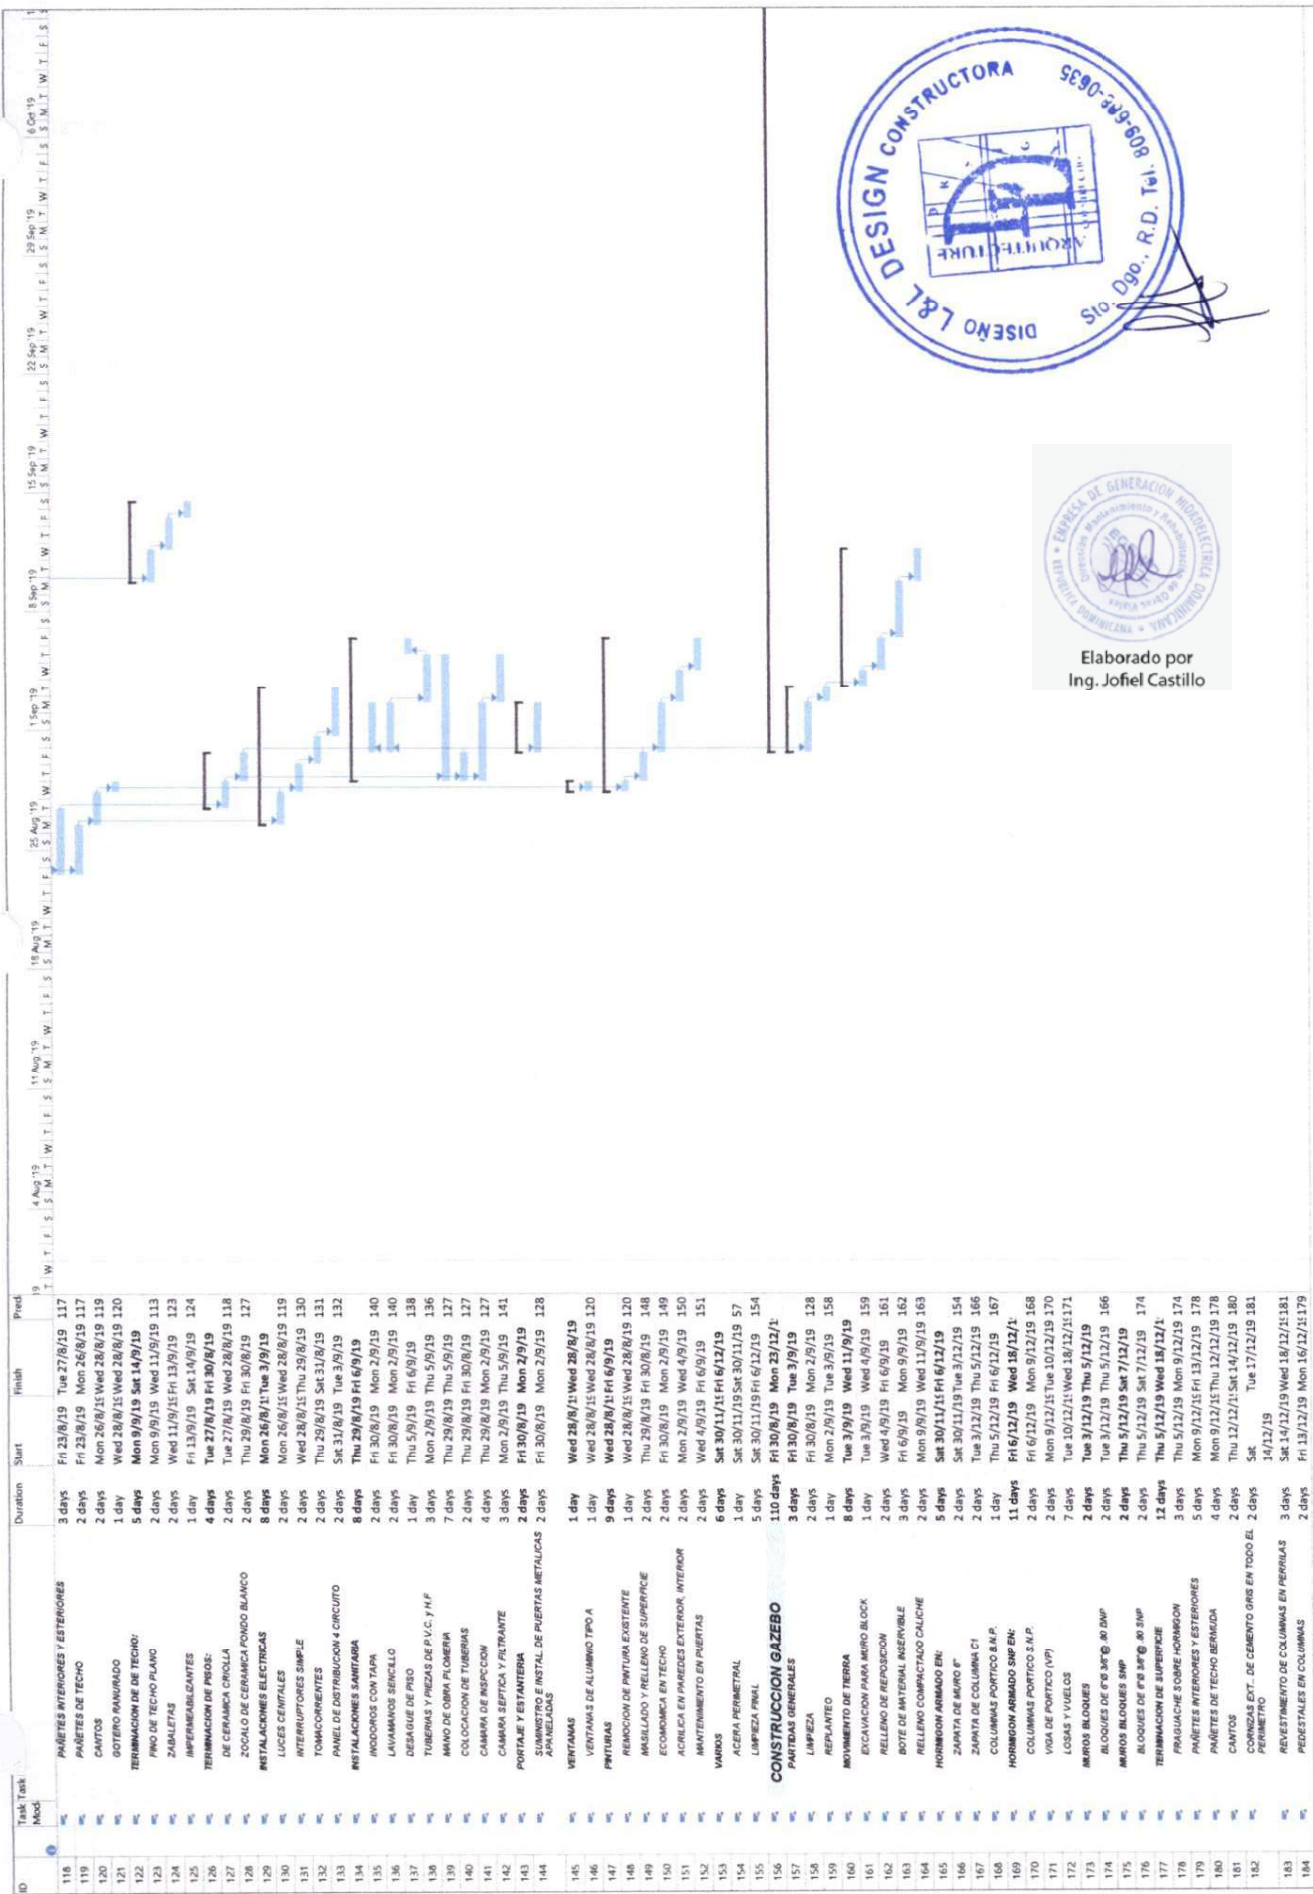

ID	Task	Mod	Duration	Start	Finish	Preld
250	Rego de Impresión 0.5 g/s/m2 con Gavilla		4 days	Sat 11/1/20	Thu 16/1/20	248
				T	W	T
				F	S	M
				T	F	S
				11 Aug 19	18 Aug 19	25 Aug 19
				S	M	T
				15 Aug 19	22 Aug 19	29 Aug 19
				T	F	S
				22 Aug 19	29 Aug 19	5 Sep 19
				S	M	T
				29 Aug 19	5 Sep 19	12 Sep 19
				T	F	S
				5 Sep 19	12 Sep 19	19 Sep 19
				S	M	T
				12 Sep 19	19 Sep 19	26 Sep 19
				T	F	S
				19 Sep 19	26 Sep 19	3 Oct 19
				S	M	T
				26 Sep 19	3 Oct 19	10 Oct 19
				T	F	S
				3 Oct 19	10 Oct 19	17 Oct 19
				S	M	T
				10 Oct 19	17 Oct 19	24 Oct 19
				T	F	S
				17 Oct 19	24 Oct 19	31 Oct 19
				S	M	T
				24 Oct 19	31 Oct 19	7 Nov 19
				T	F	S
				31 Oct 19	7 Nov 19	14 Nov 19
				S	M	T
				7 Nov 19	14 Nov 19	21 Nov 19
				T	F	S
				14 Nov 19	21 Nov 19	28 Nov 19
				S	M	T
				21 Nov 19	28 Nov 19	5 Dec 19
				T	F	S
				28 Nov 19	5 Dec 19	12 Dec 19
				S	M	T
				5 Dec 19	12 Dec 19	19 Dec 19
				T	F	S
				12 Dec 19	19 Dec 19	26 Dec 19
				S	M	T
				19 Dec 19	26 Dec 19	2 Jan 20
				T	F	S
				26 Dec 19	2 Jan 20	2 Jan 20



Project: croco-Santa Lucia
Date: Thu 30/5/19

Task: Split


Milestones: Summary, Inactive Milestone, Manual Summary, Manual Task, Duration only, Manual Summary (Setup), Manual Summary, Start only, Finish only, External Task, External Milestone, Duration, Manual Progress

Page 5



Elaborado por
Ing. Jofiel Castillo



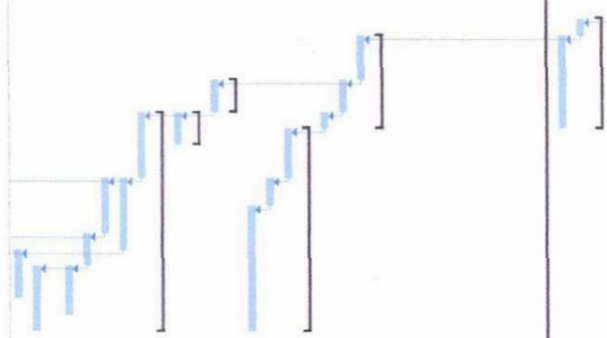

Project: crono-Santa Lucia
Date: Thu 30/5/15

Task
Spot

Page 6



13 Oct 19 20 Oct 19 27 Oct 19 3 Nov 19 10 Nov 19 17 Nov 19 24 Nov 19 1 Dec 19 8 Dec 19 15 Dec 19 22 Dec 19 29 Dec 19 5 Jan 20 12 Jan 20 19 Jan 20 26 Jan 20

Elaborado por
Ing. Jofiel Castillo

