


ID	Task	Nombre de tarea	Duration	Start	Finish	Predecessor Names
1	Modo	CUARTEL POLICIAL	78 days	Mon 4/13/20	Wed 7/29/20	
2		PRIMER NIVEL	43 days	Mon 4/13/20	Wed 6/10/20	
3		PARTIDAS GENERALES	4 days	Mon 4/13/20	Thu 4/15/20	
4		Limpieza y Replanteo	2 days	Mon 4/13/20	Mon 4/14/20	
5		Indicador de Materiales	2 days	Wed 4/15/20	Thu 4/16/20	
6		MOVIMIENTO DE TIERRA	15 days	Fri 4/17/20	Thu 5/7/20	
7		Demolicion de	2 days	Fri 4/17/20	Mon 4/20/20	
8		Estructuras de Hormigon	3 days	Tue 4/21/20	Thu 4/23/20	
9		Excavacion en Material C2	days	Fri 4/24/20	Mon 4/27/20	
10		Excavacion Zanja de M2	days	Tue 4/28/20	Wed 4/29/20	
11		Excavacion Zanja de C2	2 days	Tue 4/28/20	Wed 4/29/20	
12		Replanteo de Respaldon	1 day	Wed 5/6/20	Wed 5/6/20	
13		Replanteo de Edificacion	1 day	Thu 5/7/20	Thu 5/7/20	
14		Punto de Anclaje	1 day	Thu 4/30/20	Thu 4/30/20	
15		HORMIGON ARMADO Etc.	32 days	Mon 4/13/20	Tue 5/25/20	
16		Zapatas para Muros de	4 days	Thu 4/30/20	Tue 5/19/20	
17		Bloques 5.20x30x20	4 days	Thu 4/30/20	Tue 5/19/20	
18		Bloques 4.20x30x20	4 days	Thu 4/30/20	Tue 5/19/20	
19		Zanaja para Columnas	4 days	Thu 4/30/20	Tue 5/19/20	
20		C2 0.80M/0.80M	4 days	Thu 4/30/20	Tue 5/19/20	
21		Columnas de Amarré	4 days	Wed 5/6/20	Mon 5/11/20	
22		Columnas Circulares de 14	days	Wed 5/6/20	Mon 5/11/20	
23		Columnas Circulares de 14	days	Tue 5/12/20	Fri 5/15/20	
24		Visas de Amarré	4 days	Wed 5/6/20	Mon 5/11/20	
25		Visas de Amarré	4 days	Wed 5/6/20	Mon 5/11/20	
26		Visas de Amarré	4 days	Wed 5/6/20	Wed 5/6/20	
27		Dielat Puerta Frontal	1 day	Wed 5/6/20	Wed 5/6/20	
28		Relanzado Plancha 1'x 30"	days	Tue 5/12/20	Wed 5/13/20	
29		Loza de Techo en 0.14m	4 days	Tue 5/12/20	Fri 5/15/20	
30		MUROS DE BLOQUES	1 day	Mon 4/13/20	Mon 4/13/20	
31		Bloques Horm. 6" 0'12"	7 days	Mon 4/13/20	Tue 5/19/20	
32		Bloques Horm. 6" 0'12"	7 days	Mon 4/13/20	Tue 5/19/20	
33		Bloques Horm. 4" 0'12"	2 days	Mon 4/13/20	Tue 5/19/20	
34		Bloques Horm. 4" 0'12"	4 days	Mon 4/13/20	Thu 5/21/20	
35		TERMINACION DE SUPERFICIES	7 days	Mon 5/18/20	Tue 5/25/20	
36		Pavimento en Muros Interiores	5 days	Wed 5/20/20	Tue 5/25/20	
37		Pavimento en Muros Exteriores	2 days	Wed 5/20/20	Thu 5/21/20	
38		Replanteo en Loza de Techo	3 days	Mon 5/18/20	Wed 5/20/20	
39		Franqueo sobre superficie	3 days	Wed 5/20/20	Fri 5/22/20	
40		Cortes en general	3 days	Fri 5/22/20	Tue 5/25/20	
41		Enlase o alto relieve	2 days	Fri 5/22/20	Mon 5/25/20	
42		GOBIERNO REINTEGRADO	6 days	Wed 5/27/20	Wed 6/3/20	
43		Ventanas Cortadas de 4	days	Wed 5/27/20	Mon 6/1/20	
44		Aluminio y Crystal	2 days	Tue 6/2/20	Wed 6/3/20	
45		PUERTAS	5 days	Wed 5/27/20	Tue 6/2/20	
46		Puerta en Aluminio y Cristal	1 day	Wed 5/27/20	Wed 5/27/20	
47		Puerta Polimetal 0.80m	1 day	Wed 5/27/20	Wed 5/27/20	
48		Puerta de Hierro 0.80m x 2.10m	1 day	Wed 5/27/20	Wed 5/27/20	
49		Replanteo en Loza de Techo	2 days	Wed 5/27/20	Thu 5/28/20	
50		Gabinete de Piso en Placa	1 day	Wed 5/27/20	Wed 5/27/20	
51		Gabinete de Piso en Placa	1 day	Wed 5/27/20	Wed 5/27/20	
52		Tubo de Canal Natural	1 day	Tue 6/2/20	Tue 6/2/20	
53		TERMINACION DE PISOS	7 days	Tue 5/26/20	Wed 6/3/20	
54		Piso en Pórtico	3 days	Wed 5/27/20	Fri 5/29/20	
55		Indicador de Piso	3 days	Mon 6/1/20	Wed 6/3/20	
56		Acera Volada en	3 days	Tue 5/26/20	Thu 5/28/20	
57		REVESTIMIENTO EN PARED	days	Wed 5/27/20	Thu 5/28/20	
58		Cerámicas Impopables	2 days	Wed 5/27/20	Thu 5/28/20	
59		Instalaciones Sanitarias	days	Wed 5/27/20	Thu 5/28/20	
60		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
61		Instalaciones Sanitarias	days	Tue 5/26/20	Tue 5/26/20	
62		Instalaciones Sanitarias	days	Tue 5/26/20	Tue 5/26/20	
63		Instalaciones Sanitarias	days	Tue 5/26/20	Tue 5/26/20	
64		Instalaciones Sanitarias	days	Tue 5/26/20	Tue 5/26/20	
65		Instalaciones Sanitarias	days	Tue 5/26/20	Tue 5/26/20	
66		Instalaciones Sanitarias	days	Tue 5/26/20	Tue 5/26/20	
67		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
68		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
69		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
70		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
71		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
72		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
73		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
74		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
75		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	
76		Instalaciones Sanitarias	days	Mon 4/13/20	Mon 4/13/20	



Elaborado por  
Ing. Jofiel Castillo



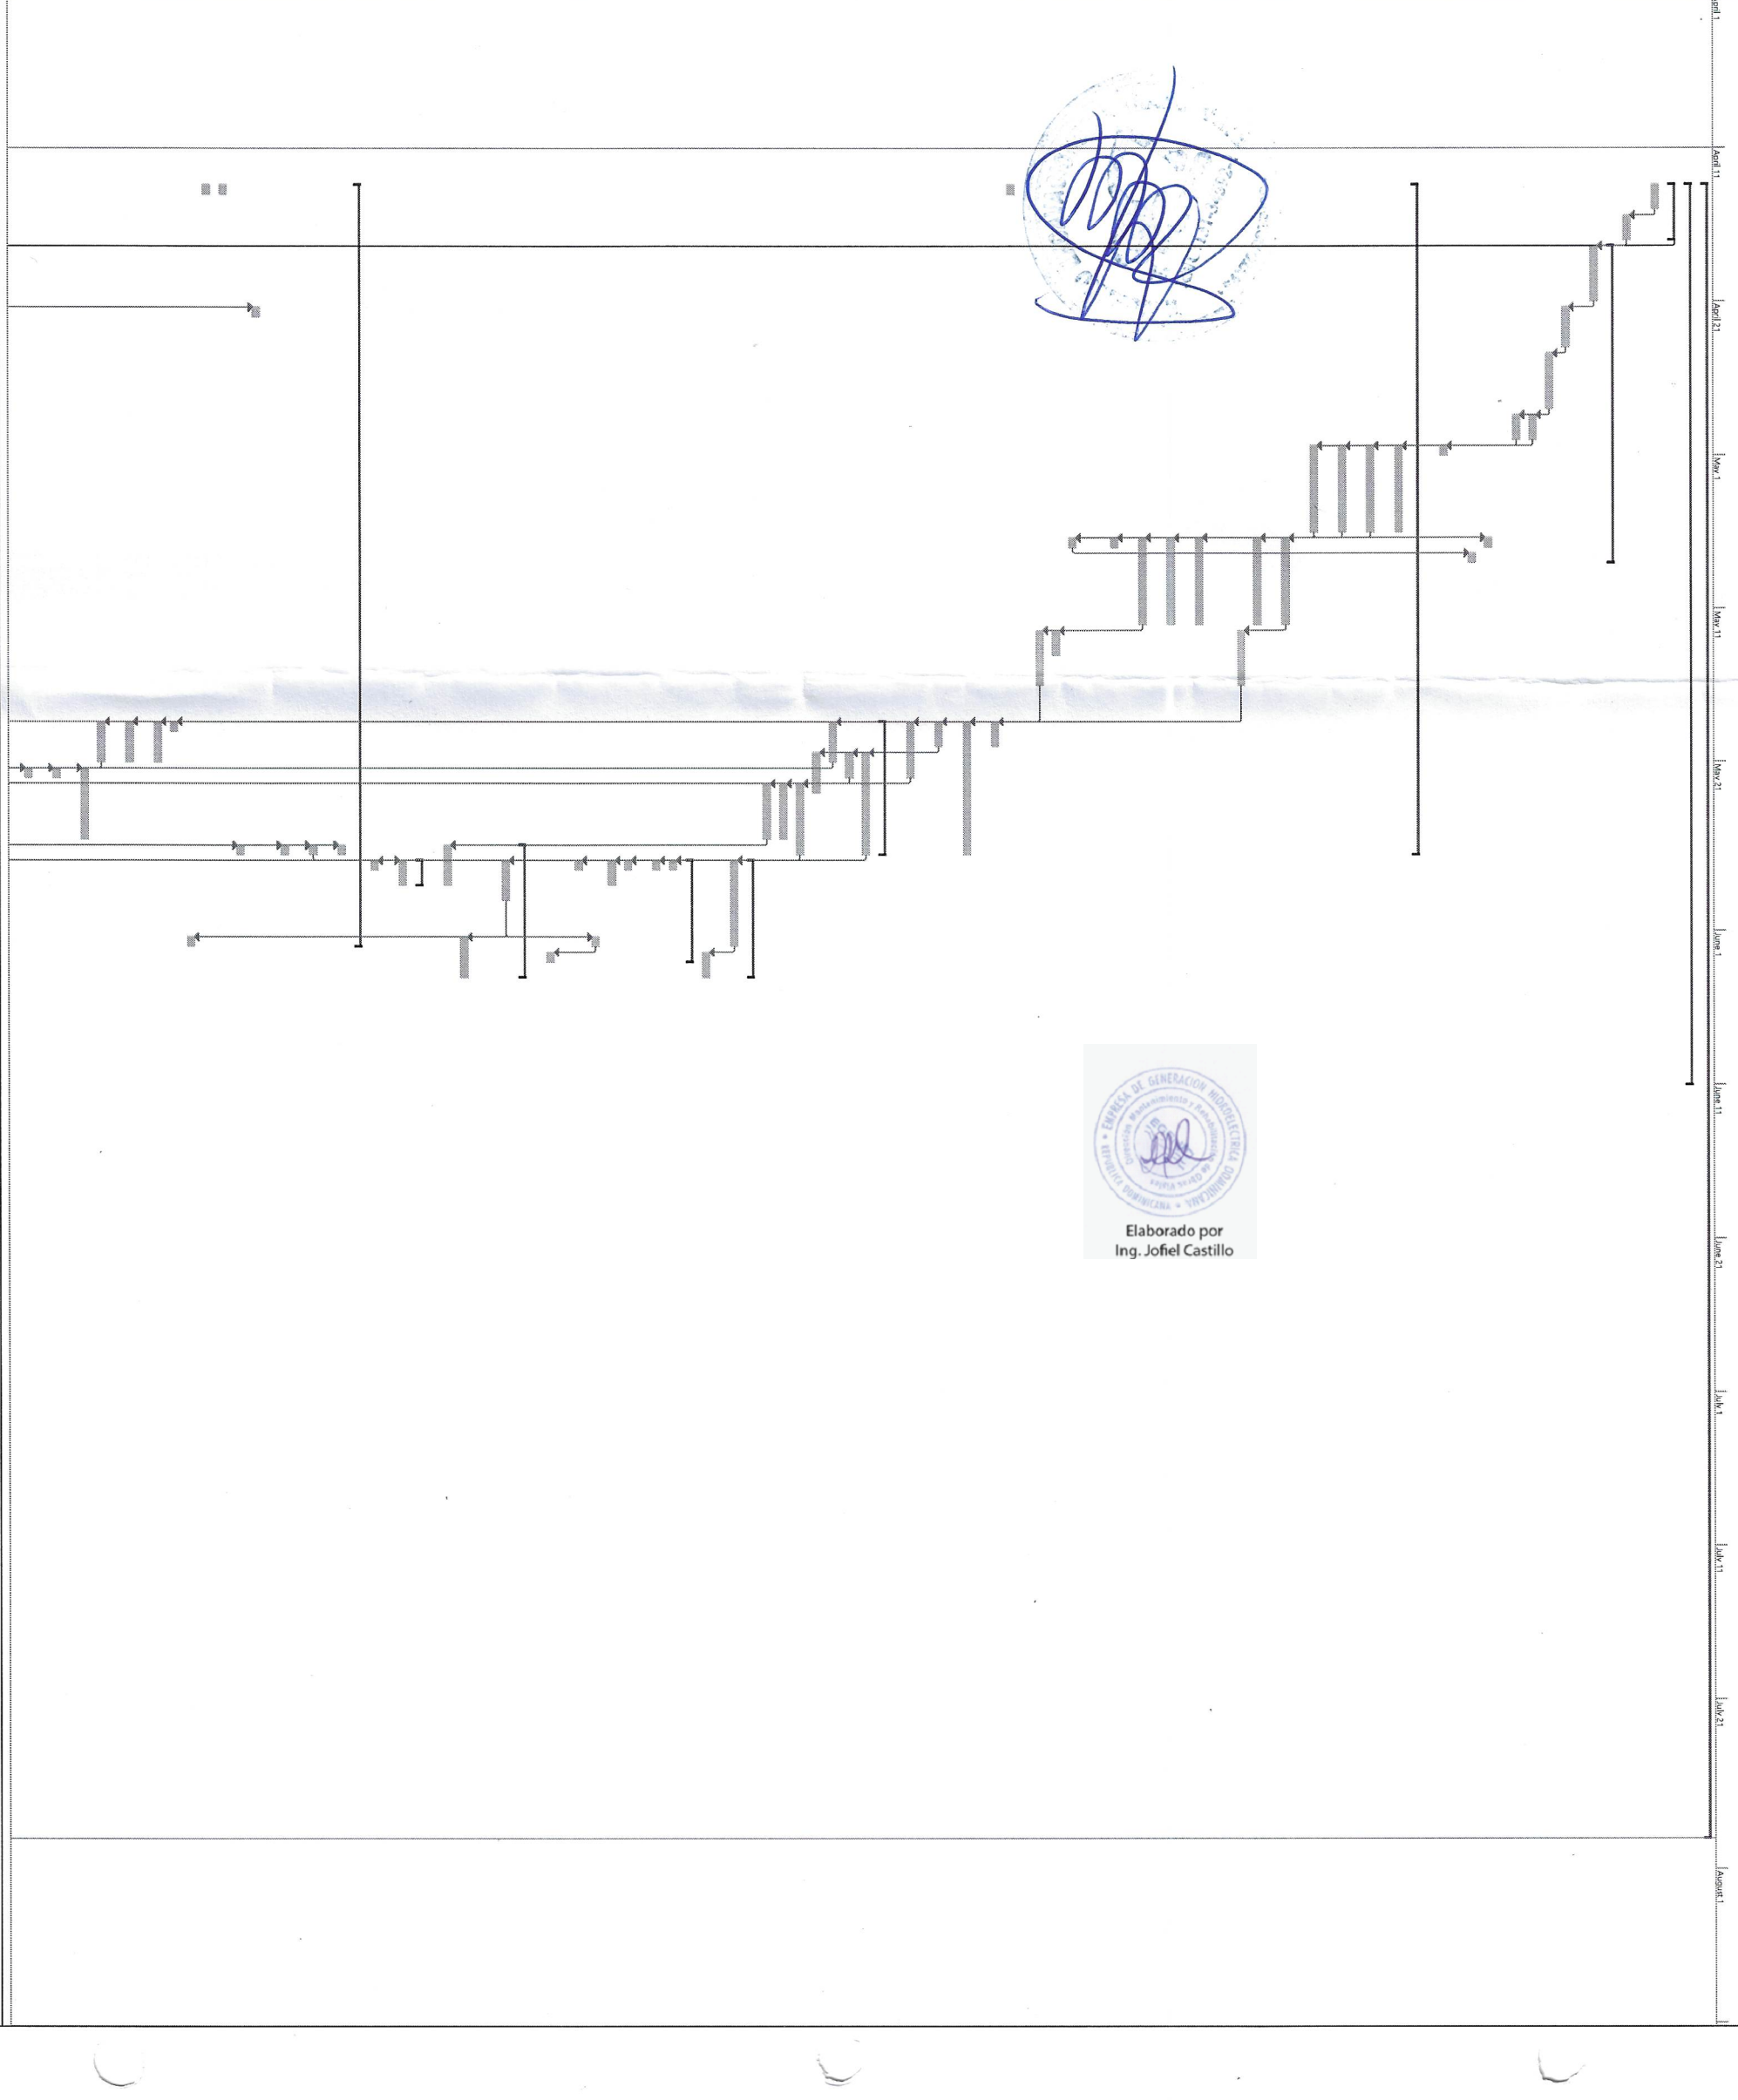
