


Id	Modo de tarea	Nombre de tarea	Duración	Comienzo	Fin	Predecesoras	S2	2022	S2	2023	S2
							S1	S1	S1		
1		CENTRO DE ATENCION PRIMARIO LAS PLACETAS	265.5 días	6/5/2022	4/5/2023						
2		INICIO	0 días	6/5/2022	6/5/2022						
3		TRABAJOS PRELIMINARES	11 días	6/6/2022	6/17/2022						
4		Limpieza y preparacion del	7 días	6/6/2022	6/13/2022						
5		Replanteo	4 días	6/13/2022	6/17/2022	4					
6		Caseta de mateirales (3m * 3m)	2 días	6/6/2022	6/7/2022	4CC					
7		Letrero en Obras	1 día	6/6/2022	6/6/2022	4CC					
8		MOVIMIENTO DE TIERRA	7 días	6/17/2022	6/25/2022	3					
9		Excavacion de zapara de muros y	3 días	6/17/2022	6/21/2022	5					
10		Relleno de reposicior	2 días	6/21/2022	6/23/2022	9					
11		Relleno compactad	2 días	6/23/2022	6/25/2022	10					
12		Bote de material	2 días	6/17/2022	6/20/2022	9CC					
13		HORMIGON ARMADO EN:	9 días	6/25/2022	7/6/2022	8					
14		Zapata de Columna Z1 210 kg/cm @3/8 a 2,20m AD Y doble	1 día	6/25/2022	6/27/2022	11					
15		Zapata de Columna CA 210 kg/cm @3/8 a 2,20m AD Y doble	1 día	6/27/2022	6/28/2022	14					
16		Zapata de Muros 210 kg/cm @3/8 a 2,20m AD Y doble	1 día	6/28/2022	6/29/2022	15					
17		Columnas C1 210kg/cm2 0.15x0.30	1 día	6/29/2022	6/30/2022	16					
18		Columnas CA 210kg/cm3 0.15x0.20	1 día	6/30/2022	7/1/2022	17					
19		Viga de amarre BNP y techo 0.15x0.20 210kg/cm2	1 día	7/1/2022	7/2/2022	18					
20		Losa h=0,12,	3 días	7/2/2022	7/6/2022	19					
21		MUROS DE BLOQUES	42 días	7/6/2022	8/23/2022						
22		BNP de 0,15 m	12 días	7/6/2022	7/20/2022	20					







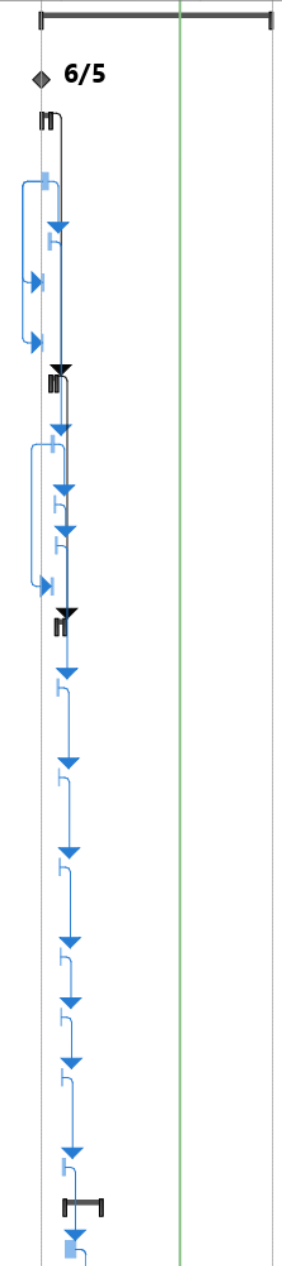



Id	Modo de tarea	Nombre de tarea	Duración	Comienzo	Fin	Predecesoras								
							S2	2022		2023		S2		
								S1		S2		S1		S2
23		BNP de 0,15 m	30 días	7/20/2022	8/23/2022	22								
24		TERMINACION DE SUPERFICIES	78 días	7/20/2022	10/17/2022									
25		Pañete muros, vigas y columnas	30 días	7/20/2022	8/23/2022	22								
26		Pañete de techo	15 días	8/23/2022	9/9/2022	25								
27		Cantos y mochetas general	15 días	9/9/2022	9/26/2022	26								
28		Fraguache	18 días	9/27/2022	10/17/2022	27								
29		TERMINACION DE TECHO	19 días	10/17/2022	11/8/2022									
30		Fino de techo plano	2 días	10/17/2022	10/19/2022	28								
31		Impermeabilizante Manto asfáltico granular	3 días	10/19/2022	10/22/2022	30								
32		Desague de techo de 3"	1 día	10/22/2022	10/24/2022	31								
33		Zabaleta	8 días	10/24/2022	11/2/2022	32								
34		Antepecho	5 días	11/2/2022	11/8/2022	33								
35		PORTAJE	40 días	11/8/2022	12/23/2022									
36		Puertas principales en pino tratado	2 días	11/8/2022	11/10/2022	34								
37		Puertas apaneladas Ever Door caoba	3 días	11/10/2022	11/14/2022	36								
38		Puertas apaneladas Ever Door Blanca	5 días	11/14/2022	11/19/2022	37								
39		Ventana corrediza de cristal P65	10 días	11/19/2022	11/30/2022	38								
40		Puerta en closet en pino tratado con division	4 días	11/30/2022	12/5/2022	39								
41		Gabinete en piso de pino tratado	4 días	12/5/2022	12/9/2022	40								
42		Gabinete en pared de pino tratado	4 días	12/9/2022	12/14/2022	41								
43		Meseta de granito natural	6 días	12/14/2022	12/21/2022	42								
44		Mueble en meseta pino tratado	2 días	12/21/2022	12/23/2022	43								
45		PINTURA	10.5 días	11/8/2022	11/19/2022									

Id	Modo de tarea	Nombre de tarea	Duración	Comienzo	Fin	Predecesoras	S2	2022	S2	2023	S2
								S1		S1	
46		Pintura de techo	3 días	11/8/2022	11/11/2022	34					
47		Pintura interior semiglos muros, vigas	5.5 días	11/11/2022	11/17/2022	46					
48		Pintura exterior acrilica muros, vigas	2 días	11/17/2022	11/19/2022	47					
49		INSTALACIONES SANITARIAS	28 días	11/19/2022	12/21/2022						
50		Inodoro azteca blanco c/tapa Sum.	2 días	11/19/2022	11/22/2022	48					
51		Lavamanos blanco Inc. Mezcladora	2 días	11/22/2022	11/24/2022	50					
52		Fregadero dos bocas	1 día	11/24/2022	11/25/2022	51					
53		Desague de piso	2 días	11/25/2022	11/28/2022	52					
54		Ventilacion 3"	1.5 días	11/28/2022	11/29/2022	53					
55		Acometida agua potable	1 día	11/29/2022	11/30/2022	54					
56		Trampa de Grasa	1 día	11/30/2022	12/1/2022	55					
57		Registro	4.5 días	12/1/2022	12/7/2022	56					
58		Septico	12 días	12/1/2022	12/15/2022	57CC					
59		Filtrante de 12" PVC	1 día	12/15/2022	12/16/2022	58					
60		Suministro e Instalacion de	2 días	12/16/2022	12/19/2022	59					
61		Sum. Y Col. Bomba de 1/2 HP pedrolo	2 días	12/19/2022	12/21/2022	60					
62		Botiquin	0.5 días	12/21/2022	12/21/2022	61					
63		Accesorios	0.5 días	12/21/2022	12/21/2022	62CC					
64		Tuberias y piezas especiales	1 día	12/19/2022	12/20/2022	61CC					
65		Mano de obra plome	12 días	11/19/2022	12/3/2022	50CC					
66		INSTALACIONES ELECTRICAS	23.5 días	11/22/2022	12/19/2022						
67		Salidas cenitales	5 días	11/22/2022	11/28/2022	50					
68		Salidas para telefono	1 día	11/28/2022	11/29/2022	67					
69		Interruptores sencillos	2 días	11/29/2022	12/1/2022	68					
70		Interruptores dobles	0.5 días	12/1/2022	12/1/2022	69					
71		Globo	4 días	12/1/2022	12/6/2022	70					



Id	Modo de tarea	Nombre de tarea	Duración	Comienzo	Fin	Predecesoras						
							S2	2022		2023		S2
								S1		S2	S1	S2
72	→	Tomacorriente 110	1 día	12/6/2022	12/7/2022	71						
73	→	Lampara exterior tipo secador	2 días	12/7/2022	12/9/2022	72						
74	→	Tuberías y piezas especiales	5 días	12/9/2022	12/15/2022	73						
75	→	Paneles de distribución 4 a 8	2 días	12/15/2022	12/17/2022	74						
76	→	Conexión a CDEEE	1 día	12/17/2022	12/19/2022	75						
77	→	PISOS Y CERAMICA	22 días	11/19/2022	12/15/2022							
78	→	torta de hormigon con malla	7 días	11/19/2022	11/28/2022	45						
79	→	Piso de porcelanato 0.5*0.5 importada	7 días	11/28/2022	12/6/2022	78						
80	→	Ceramica en pared de baños	3 días	12/6/2022	12/9/2022	79						
81	→	Ceramica en pared de cocina	2 días	12/9/2022	12/12/2022	80						
82	→	Zocalos	3 días	12/12/2022	12/15/2022	81						
83	→	VERJA DEBLOK Y MALLA CICLONICA	97 días	12/15/2022	4/5/2023	77						
84	→	TRABAJOS PRELIMINARES	1 día	12/15/2022	12/16/2022							
85	→	Limpieza y replant	1 día	12/15/2022	12/16/2022	77						
86	→	MOVIMIENTOS DE TIERRA	21 días	12/16/2022	1/9/2023	84						
87	→	Excavación de zapatas de muros	7 días	12/16/2022	12/23/2022	84						
88	→	Excavación de zapatas de columnas	7 días	12/24/2022	12/31/2022	87						
89	→	Relleno de reposi	7 días	12/31/2022	1/9/2023	88						
90	→	Bote de material producto de excavación	7 días	12/16/2022	12/23/2022	87CC						
91	→	HORMIGON ARMADO	3 días	1/9/2023	1/12/2023	86						
92	→	zapata de muro 180kg/cm2	1 día	1/9/2023	1/10/2023	87						
93	→	Zapata de columna C1	0.5 días	1/10/2023	1/11/2023	92						

Id	Modo de tarea	Nombre de tarea	Duración	Comienzo	Fin	Predecesoras	2022		2023		
							S2	S1	S2	S1	S2
94		Zapata de columna C2	0.5 días	1/11/2023	1/11/2023	93					
95		Columnas C1 0.20m*0.20m, 210kg/cm2	0.5 días	1/11/2023	1/12/2023	94					
96		Columnas C2 0.15m*0.20m, 210kg/cm2	0.5 días	1/12/2023	1/12/2023	95					
97		Coumnas de amarre 0.15m*0.20m,	0.5 días	1/11/2023	1/11/2023	93					
98		MUROS DE BLOQU	9 días	1/12/2023	1/23/2023	91					
99		Bloques de 6" B.N	2 días	1/12/2023	1/14/2023	97					
100		Bloques de 6" S.N	7 días	1/14/2023	1/23/2023	99					
101		TERMINACION DE SUPERFICIES	24 días	1/23/2023	2/18/2023	98					
102		Pañete en muros y columnas	7 días	1/23/2023	1/31/2023	99					
103		Cantos	14 días	1/31/2023	2/15/2023	102					
104		Fraguache	3 días	2/16/2023	2/18/2023	103					
105		PORTAJE	25 días	2/18/2023	3/20/2023						
106		Puerta corrediza perf. 2*4 (sum. E inst. Del tubo)	5 días	2/18/2023	2/24/2023	101					
107		Puerta peatonal tubo y malla.	5 días	2/24/2023	3/2/2023	106					
108		Malla ciclonica de 6' inc. palometas y alambre de	15 días	3/2/2023	3/20/2023	107					
109		PINTURA	0.5 días	3/20/2023	3/20/2023						
110		Pintura acrilica en paredes	0.5 días	3/20/2023	3/20/2023	105					
111		VARIOS	13.5 días	3/20/2023	4/5/2023						
112		Acera en entrada	2 días	3/20/2023	3/22/2023	109					
113		Cisterna de 4,000 galones	10 días	3/22/2023	4/3/2023	112					
114		Capitel y perrilla en columna	2 días	3/22/2023	3/24/2023	113CC					

Id	Modo de tarea	Nombre de tarea	Duración	Comienzo	Fin	Predecesoras	2022		2023	
							S2	S1	S2	S1
115		Rampa de hormigon con malla	1.5 días	3/24/2023	3/27/2023	114				
116		Construcción de jardinera	2 días	3/27/2023	3/29/2023	115				
117		Letrero frontal en bronce	1 día	3/29/2023	3/30/2023	116				
118		Grava s/c	0.5 días	3/30/2023	3/30/2023	117				
119		Plantas ornamentc	1 día	3/30/2023	3/31/2023	118CC				
120		Palmas manila princesa	1 día	3/31/2023	4/1/2023	119				
121		Limpieza final	3 días	4/1/2023	4/5/2023	120				
122		FIN	0 días	4/5/2023	4/5/2023	121				

