


| Id | Modo de tarea | Nombre de tarea | Duración | Comienzo | Fin | Predecesoras | 2022 | | | | | 2023 | | | | | | | |
|----|---------------|--|-------------------|------------------|------------------|--------------|------|----|----|----|----|------|----|----|----|--|--|--|--|
| | | | | | | | S2 | S1 | S2 | S1 | S2 | S1 | S2 | S1 | S2 | | | | |
| 1 | | CENTRO DE ATENCION PRIMARIO LAS PLACETAS | 265.5 días | 6/5/2022 | 4/5/2023 | | | | | | | | | | | | | | |
| 2 | | INICIO | 0 días | 6/5/2022 | 6/5/2022 | | | | | | | | | | | | | | |
| 3 | | TRABAJOS PRELIMINARES | 11 días | 6/6/2022 | 6/17/2022 | | | | | | | | | | | | | | |
| 4 | | Limpieza y preparacion del | 7 días | 6/6/2022 | 6/13/2022 | | | | | | | | | | | | | | |
| 5 | | Replanteo | 4 días | 6/13/2022 | 6/17/2022 | 4 | | | | | | | | | | | | | |
| 6 | | Caseta de mateirales (3m * 3m) | 2 días | 6/6/2022 | 6/7/2022 | 4CC | | | | | | | | | | | | | |
| 7 | | Letrero en Obras | 1 día | 6/6/2022 | 6/6/2022 | 4CC | | | | | | | | | | | | | |
| 8 | | MOVIMIENTO DE TIERRA | 7 días | 6/17/2022 | 6/25/2022 | 3 | | | | | | | | | | | | | |
| 9 | | Excavacion de zapara de muros y | 3 días | 6/17/2022 | 6/21/2022 | 5 | | | | | | | | | | | | | |
| 10 | | Relleno de reposicior | 2 días | 6/21/2022 | 6/23/2022 | 9 | | | | | | | | | | | | | |
| 11 | | Relleno compactad | 2 días | 6/23/2022 | 6/25/2022 | 10 | | | | | | | | | | | | | |
| 12 | | Bote de material | 2 días | 6/17/2022 | 6/20/2022 | 9CC | | | | | | | | | | | | | |
| 13 | | HORMIGON ARMADO EN: | 9 días | 6/25/2022 | 7/6/2022 | 8 | | | | | | | | | | | | | |
| 14 | | Zapata de Columna Z1 210 kg/cm @3/8 a 2,20m AD Y doble | 1 día | 6/25/2022 | 6/27/2022 | 11 | | | | | | | | | | | | | |
| 15 | | Zapata de Columna CA 210 kg/cm @3/8 a 2,20m AD Y doble | 1 día | 6/27/2022 | 6/28/2022 | 14 | | | | | | | | | | | | | |
| 16 | | Zapata de Muros 210 kg/cm @3/8 a 2,20m AD Y doble | 1 día | 6/28/2022 | 6/29/2022 | 15 | | | | | | | | | | | | | |
| 17 | | Columnas C1 210kg/cm2 0.15x0.30 | 1 día | 6/29/2022 | 6/30/2022 | 16 | | | | | | | | | | | | | |
| 18 | | Columnas CA 210kg/cm3 0.15x0.20 | 1 día | 6/30/2022 | 7/1/2022 | 17 | | | | | | | | | | | | | |
| 19 | | Viga de amarre BNP y techo 0.15x0.20 210kg/cm2 | 1 día | 7/1/2022 | 7/2/2022 | 18 | | | | | | | | | | | | | |
| 20 | | Losa h=0,12, | 3 días | 7/2/2022 | 7/6/2022 | 19 | | | | | | | | | | | | | |
| 21 | | MUROS DE BLOQUES | 42 días | 7/6/2022 | 8/23/2022 | | | | | | | | | | | | | | |
| 22 | | BNP de 0,15 m | 12 días | 7/6/2022 | 7/20/2022 | 20 | | | | | | | | | | | | | |







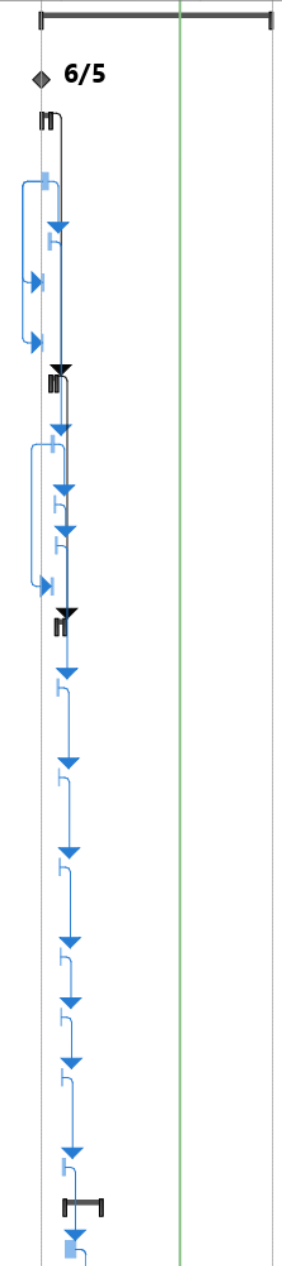



| Id | Modo de tarea | Nombre de tarea | Duración | Comienzo | Fin | Predecesoras | S2 | 2022 | S2 | 2023 | S2 |
|----|---------------|---|------------------|-------------------|-------------------|--------------|----|------|----|------|----|
| | | | | | | | | S1 | | S1 | |
| 23 | | BNP de 0,15 m | 30 días | 7/20/2022 | 8/23/2022 | 22 | | | | | |
| 24 | | TERMINACION DE SUPERFICIES | 78 días | 7/20/2022 | 10/17/2022 | | | | | | |
| 25 | | Pañete muros, vigas y columnas | 30 días | 7/20/2022 | 8/23/2022 | 22 | | | | | |
| 26 | | Pañete de techo | 15 días | 8/23/2022 | 9/9/2022 | 25 | | | | | |
| 27 | | Cantos y mochetas general | 15 días | 9/9/2022 | 9/26/2022 | 26 | | | | | |
| 28 | | Fraguache | 18 días | 9/27/2022 | 10/17/2022 | 27 | | | | | |
| 29 | | TERMINACION DE TECHO | 19 días | 10/17/2022 | 11/8/2022 | | | | | | |
| 30 | | Fino de techo plano | 2 días | 10/17/2022 | 10/19/2022 | 28 | | | | | |
| 31 | | Impermeabilizante Manto asfáltico granular | 3 días | 10/19/2022 | 10/22/2022 | 30 | | | | | |
| 32 | | Desague de techo de 3" | 1 día | 10/22/2022 | 10/24/2022 | 31 | | | | | |
| 33 | | Zabaleta | 8 días | 10/24/2022 | 11/2/2022 | 32 | | | | | |
| 34 | | Antepecho | 5 días | 11/2/2022 | 11/8/2022 | 33 | | | | | |
| 35 | | PORTAJE | 40 días | 11/8/2022 | 12/23/2022 | | | | | | |
| 36 | | Puertas principales en pino tratado | 2 días | 11/8/2022 | 11/10/2022 | 34 | | | | | |
| 37 | | Puertas apaneladas Ever Door caoba | 3 días | 11/10/2022 | 11/14/2022 | 36 | | | | | |
| 38 | | Puertas apaneladas Ever Door Blanca | 5 días | 11/14/2022 | 11/19/2022 | 37 | | | | | |
| 39 | | Ventana corrediza de cristal P65 | 10 días | 11/19/2022 | 11/30/2022 | 38 | | | | | |
| 40 | | Puerta en closet en pino tratado con division | 4 días | 11/30/2022 | 12/5/2022 | 39 | | | | | |
| 41 | | Gabinete en piso de pino tratado | 4 días | 12/5/2022 | 12/9/2022 | 40 | | | | | |
| 42 | | Gabinete en pared de pino tratado | 4 días | 12/9/2022 | 12/14/2022 | 41 | | | | | |
| 43 | | Meseta de granito natural | 6 días | 12/14/2022 | 12/21/2022 | 42 | | | | | |
| 44 | | Mueble en meseta pino tratado | 2 días | 12/21/2022 | 12/23/2022 | 43 | | | | | |
| 45 | | PINTURA | 10.5 días | 11/8/2022 | 11/19/2022 | | | | | | |

| Id | Modo de tarea | Nombre de tarea | Duración | Comienzo | Fin | Predecesoras | S2 | 2022 | S2 | 2023 | S2 |
|----|---------------|--|------------------|-------------------|-------------------|--------------|----|------|----|------|----|
| | | | | | | | | S1 | | S1 | |
| 46 | | Pintura de techo | 3 días | 11/8/2022 | 11/11/2022 | 34 | | | | | |
| 47 | | Pintura interior semiglos muros, vigas | 5.5 días | 11/11/2022 | 11/17/2022 | 46 | | | | | |
| 48 | | Pintura exterior acrilica muros, vigas | 2 días | 11/17/2022 | 11/19/2022 | 47 | | | | | |
| 49 | | INSTALACIONES SANITARIAS | 28 días | 11/19/2022 | 12/21/2022 | | | | | | |
| 50 | | Inodoro azteca blanco c/tapa Sum. | 2 días | 11/19/2022 | 11/22/2022 | 48 | | | | | |
| 51 | | Lavamanos blanco Inc. Mezcladora | 2 días | 11/22/2022 | 11/24/2022 | 50 | | | | | |
| 52 | | Fregadero dos bocas | 1 día | 11/24/2022 | 11/25/2022 | 51 | | | | | |
| 53 | | Desague de piso | 2 días | 11/25/2022 | 11/28/2022 | 52 | | | | | |
| 54 | | Ventilacion 3" | 1.5 días | 11/28/2022 | 11/29/2022 | 53 | | | | | |
| 55 | | Acometida agua potable | 1 día | 11/29/2022 | 11/30/2022 | 54 | | | | | |
| 56 | | Trampa de Grasa | 1 día | 11/30/2022 | 12/1/2022 | 55 | | | | | |
| 57 | | Registro | 4.5 días | 12/1/2022 | 12/7/2022 | 56 | | | | | |
| 58 | | Septico | 12 días | 12/1/2022 | 12/15/2022 | 57CC | | | | | |
| 59 | | Filtrante de 12" PVC | 1 día | 12/15/2022 | 12/16/2022 | 58 | | | | | |
| 60 | | Suministro e Instalacion de | 2 días | 12/16/2022 | 12/19/2022 | 59 | | | | | |
| 61 | | Sum. Y Col. Bomba de 1/2 HP pedrolo | 2 días | 12/19/2022 | 12/21/2022 | 60 | | | | | |
| 62 | | Botiquin | 0.5 días | 12/21/2022 | 12/21/2022 | 61 | | | | | |
| 63 | | Accesorios | 0.5 días | 12/21/2022 | 12/21/2022 | 62CC | | | | | |
| 64 | | Tuberias y piezas especiales | 1 día | 12/19/2022 | 12/20/2022 | 61CC | | | | | |
| 65 | | Mano de obra plome | 12 días | 11/19/2022 | 12/3/2022 | 50CC | | | | | |
| 66 | | INSTALACIONES ELECTRICAS | 23.5 días | 11/22/2022 | 12/19/2022 | | | | | | |
| 67 | | Salidas cenitales | 5 días | 11/22/2022 | 11/28/2022 | 50 | | | | | |
| 68 | | Salidas para telefono | 1 día | 11/28/2022 | 11/29/2022 | 67 | | | | | |
| 69 | | Interruptores sencillos | 2 días | 11/29/2022 | 12/1/2022 | 68 | | | | | |
| 70 | | Interruptores dobles | 0.5 días | 12/1/2022 | 12/1/2022 | 69 | | | | | |
| 71 | | Globo | 4 días | 12/1/2022 | 12/6/2022 | 70 | | | | | |



| Id | Modo de tarea | Nombre de tarea | Duración | Comienzo | Fin | Predecesoras | | | | | | |
|----|---------------|---|----------------|-------------------|-------------------|--------------|----|------|--|------|----|----|
| | | | | | | | S2 | 2022 | | 2023 | | S2 |
| | | | | | | | | S1 | | S2 | S1 | S2 |
| 72 | → | Tomacorriente 110 | 1 día | 12/6/2022 | 12/7/2022 | 71 | | | | | | |
| 73 | → | Lampara exterior tipo secador | 2 días | 12/7/2022 | 12/9/2022 | 72 | | | | | | |
| 74 | → | Tuberías y piezas especiales | 5 días | 12/9/2022 | 12/15/2022 | 73 | | | | | | |
| 75 | → | Paneles de distribución 4 a 8 | 2 días | 12/15/2022 | 12/17/2022 | 74 | | | | | | |
| 76 | → | Conexión a CDEEE | 1 día | 12/17/2022 | 12/19/2022 | 75 | | | | | | |
| 77 | → | PISOS Y CERAMICA | 22 días | 11/19/2022 | 12/15/2022 | | | | | | | |
| 78 | → | torta de hormigon con malla | 7 días | 11/19/2022 | 11/28/2022 | 45 | | | | | | |
| 79 | → | Piso de porcelanato 0.5*0.5 importada | 7 días | 11/28/2022 | 12/6/2022 | 78 | | | | | | |
| 80 | → | Ceramica en pared de baños | 3 días | 12/6/2022 | 12/9/2022 | 79 | | | | | | |
| 81 | → | Ceramica en pared de cocina | 2 días | 12/9/2022 | 12/12/2022 | 80 | | | | | | |
| 82 | → | Zocalos | 3 días | 12/12/2022 | 12/15/2022 | 81 | | | | | | |
| 83 | → | VERJA DEBLOK Y MALLA CICLONICA | 97 días | 12/15/2022 | 4/5/2023 | 77 | | | | | | |
| 84 | → | TRABAJOS PRELIMINARES | 1 día | 12/15/2022 | 12/16/2022 | | | | | | | |
| 85 | → | Limpieza y replant | 1 día | 12/15/2022 | 12/16/2022 | 77 | | | | | | |
| 86 | → | MOVIMIENTOS DE TIERRA | 21 días | 12/16/2022 | 1/9/2023 | 84 | | | | | | |
| 87 | → | Excavación de zapatas de muros | 7 días | 12/16/2022 | 12/23/2022 | 84 | | | | | | |
| 88 | → | Excavación de zapatas de columnas | 7 días | 12/24/2022 | 12/31/2022 | 87 | | | | | | |
| 89 | → | Relleno de reposi | 7 días | 12/31/2022 | 1/9/2023 | 88 | | | | | | |
| 90 | → | Bote de material producto de excavación | 7 días | 12/16/2022 | 12/23/2022 | 87CC | | | | | | |
| 91 | → | HORMIGON ARMADO | 3 días | 1/9/2023 | 1/12/2023 | 86 | | | | | | |
| 92 | → | zapata de muro 180kg/cm2 | 1 día | 1/9/2023 | 1/10/2023 | 87 | | | | | | |
| 93 | → | Zapata de columna C1 | 0.5 días | 1/10/2023 | 1/11/2023 | 92 | | | | | | |

| Id | Modo de tarea | Nombre de tarea | Duración | Comienzo | Fin | Predecesoras | 2022 | | 2023 | | |
|-----|---------------|--|------------------|------------------|------------------|--------------|------|----|------|----|----|
| | | | | | | | S2 | S1 | S2 | S1 | S2 |
| 94 | | Zapata de columna C2 | 0.5 días | 1/11/2023 | 1/11/2023 | 93 | | | | | |
| 95 | | Columnas C1 0.20m*0.20m, 210kg/cm2 | 0.5 días | 1/11/2023 | 1/12/2023 | 94 | | | | | |
| 96 | | Columnas C2 0.15m*0.20m, 210kg/cm2 | 0.5 días | 1/12/2023 | 1/12/2023 | 95 | | | | | |
| 97 | | Coumnas de amarre 0.15m*0.20m, | 0.5 días | 1/11/2023 | 1/11/2023 | 93 | | | | | |
| 98 | | MUROS DE BLOQU | 9 días | 1/12/2023 | 1/23/2023 | 91 | | | | | |
| 99 | | Bloques de 6" B.N | 2 días | 1/12/2023 | 1/14/2023 | 97 | | | | | |
| 100 | | Bloques de 6" S.N | 7 días | 1/14/2023 | 1/23/2023 | 99 | | | | | |
| 101 | | TERMINACION DE SUPERFICIES | 24 días | 1/23/2023 | 2/18/2023 | 98 | | | | | |
| 102 | | Pañete en muros y columnas | 7 días | 1/23/2023 | 1/31/2023 | 99 | | | | | |
| 103 | | Cantos | 14 días | 1/31/2023 | 2/15/2023 | 102 | | | | | |
| 104 | | Fraguache | 3 días | 2/16/2023 | 2/18/2023 | 103 | | | | | |
| 105 | | PORTAJE | 25 días | 2/18/2023 | 3/20/2023 | | | | | | |
| 106 | | Puerta corrediza perf. 2*4 (sum. E inst. Del tubo) | 5 días | 2/18/2023 | 2/24/2023 | 101 | | | | | |
| 107 | | Puerta peatonal tubo y malla. | 5 días | 2/24/2023 | 3/2/2023 | 106 | | | | | |
| 108 | | Malla ciclonica de 6' inc. palometas y alambre de | 15 días | 3/2/2023 | 3/20/2023 | 107 | | | | | |
| 109 | | PINTURA | 0.5 días | 3/20/2023 | 3/20/2023 | | | | | | |
| 110 | | Pintura acrilica en paredes | 0.5 días | 3/20/2023 | 3/20/2023 | 105 | | | | | |
| 111 | | VARIOS | 13.5 días | 3/20/2023 | 4/5/2023 | | | | | | |
| 112 | | Acera en entrada | 2 días | 3/20/2023 | 3/22/2023 | 109 | | | | | |
| 113 | | Cisterna de 4,000 galones | 10 días | 3/22/2023 | 4/3/2023 | 112 | | | | | |
| 114 | | Capitel y perrilla en columna | 2 días | 3/22/2023 | 3/24/2023 | 113CC | | | | | |

| Id | Modo de tarea | Nombre de tarea | Duración | Comienzo | Fin | Predecesoras | 2022 | | 2023 | |
|-----|---|-----------------------------|----------|-----------|-----------|--------------|------|----|------|----|
| | | | | | | | S2 | S1 | S2 | S1 |
| 115 |  | Rampa de hormigon con malla | 1.5 días | 3/24/2023 | 3/27/2023 | 114 | | | | |
| 116 |  | Construcción de jardinera | 2 días | 3/27/2023 | 3/29/2023 | 115 | | | | |
| 117 |  | Letrero frontal en bronce | 1 día | 3/29/2023 | 3/30/2023 | 116 | | | | |
| 118 |  | Grava s/c | 0.5 días | 3/30/2023 | 3/30/2023 | 117 | | | | |
| 119 |  | Plantas ornamentales | 1 día | 3/30/2023 | 3/31/2023 | 118CC | | | | |
| 120 |  | Palmas manila princesa | 1 día | 3/31/2023 | 4/1/2023 | 119 | | | | |
| 121 |  | Limpieza final | 3 días | 4/1/2023 | 4/5/2023 | 120 | | | | |
| 122 |  | FIN | 0 días | 4/5/2023 | 4/5/2023 | 121 | | | | |

