


ID	Task Mode	Task Name	Duration	Start	Finish	February 2023																
						24	27	30	2	5	8	11	14	17	20	23						
1		Destacamento Policial de Santana	119 days?	Wed 1/2/23	Tue 18/7/23																	
2		Primer Nivel	82 days?	Wed 1/2/23	Fri 26/5/23																	
3		inicio	0 days	Wed 1/2/23	Wed 1/2/23																	
4		Movimiento de tierra	1 day?	Wed 1/2/23	Thu 2/2/23																	
5		Hormigon Armado	37 days	Thu 2/2/23	Mon 27/3/23																	
6		Hormigon Armado Zapatas	5 days	Thu 2/2/23	Thu 9/2/23																	
7		Hormigon Armado Columnas	4 days	Tue 7/3/23	Mon 13/3/23																	
8		Hormigon Armado Vigas y losa	10 days	Mon 13/3/23	Mon 27/3/23																	
9		Muro de Bloques	18 days	Thu 9/2/23	Tue 7/3/23																	
10		Terminacion de superficies	21 days	Mon 27/3/23	Tue 25/4/23																	
11		Ventanas y Puertas	15 days	Tue 2/5/23	Tue 23/5/23																	
12		Terminacion de Pisos y Paredes	5 days	Tue 25/4/23	Tue 2/5/23																	
13		Instalaciones Electricas	58 days	Tue 7/3/23	Fri 26/5/23																	
14		Canalizacion	5 days	Tue 7/3/23	Tue 14/3/23																	
15		Alambrado	3 days	Tue 23/5/23	Fri 26/5/23																	
16		S/C de Accesorios	2 days	Mon 15/5/23	Wed 17/5/23																	
17		Instalaciones Sanitarias	21 days	Tue 7/3/23	Wed 5/4/23																	
18		Acabados y pintura	8 days	Wed 3/5/23	Mon 15/5/23																	
19		Miscelaneos	10 days	Tue 7/3/23	Tue 21/3/23																	
20		Segundo Nivel	74 days	Tue 7/3/23	Mon 19/6/23																	
21		Hormigon Armado	12 days	Fri 31/3/23	Tue 18/4/23																	
22		Hormigon Armado Columnas	4 days	Fri 31/3/23	Thu 6/4/23																	
23		Hormigon Armado Vigas y losa	8 days	Thu 6/4/23	Tue 18/4/23																	

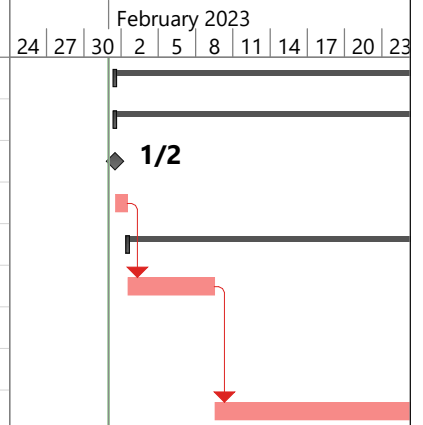


Project: Cronograma Santana a
Date: Mon 23/1/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	February 2023																	
						24	27	30	2	5	8	11	14	17	20	23							
24		Muro de Bloques	18 days	Tue 7/3/23	Fri 31/3/23																		
25		Terminacion de superficies	21 days	Tue 18/4/23	Wed 17/5/23																		
26		Ventanas y Puertas	15 days	Wed 24/5/23	Wed 14/6/23																		
27		Terminacion de Pisos y Paredes	5 days	Wed 17/5/23	Wed 24/5/23																		
28		Instalaciones Electricas	56 days	Fri 31/3/23	Mon 19/6/23																		
29		Canalizacion	5 days	Fri 31/3/23	Fri 7/4/23																		
30		Alambrado	3 days	Wed 14/6/23	Mon 19/6/23																		
31		S/C de Accesorios	2 days	Tue 6/6/23	Thu 8/6/23																		
32		Instalaciones Sanitarias	21 days	Tue 7/3/23	Wed 5/4/23																		
33		Acabados y pintura	7 days	Fri 26/5/23	Tue 6/6/23																		
34		Exterior	30 days	Tue 6/6/23	Tue 18/7/23																		
35		Miscelaneos Exteriore	30 days	Tue 6/6/23	Tue 18/7/23																		
36		Fin del proyecto	0 days	Tue 18/7/23	Tue 18/7/23																		


Project: Cronograma Santana a
Date: Mon 23/1/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

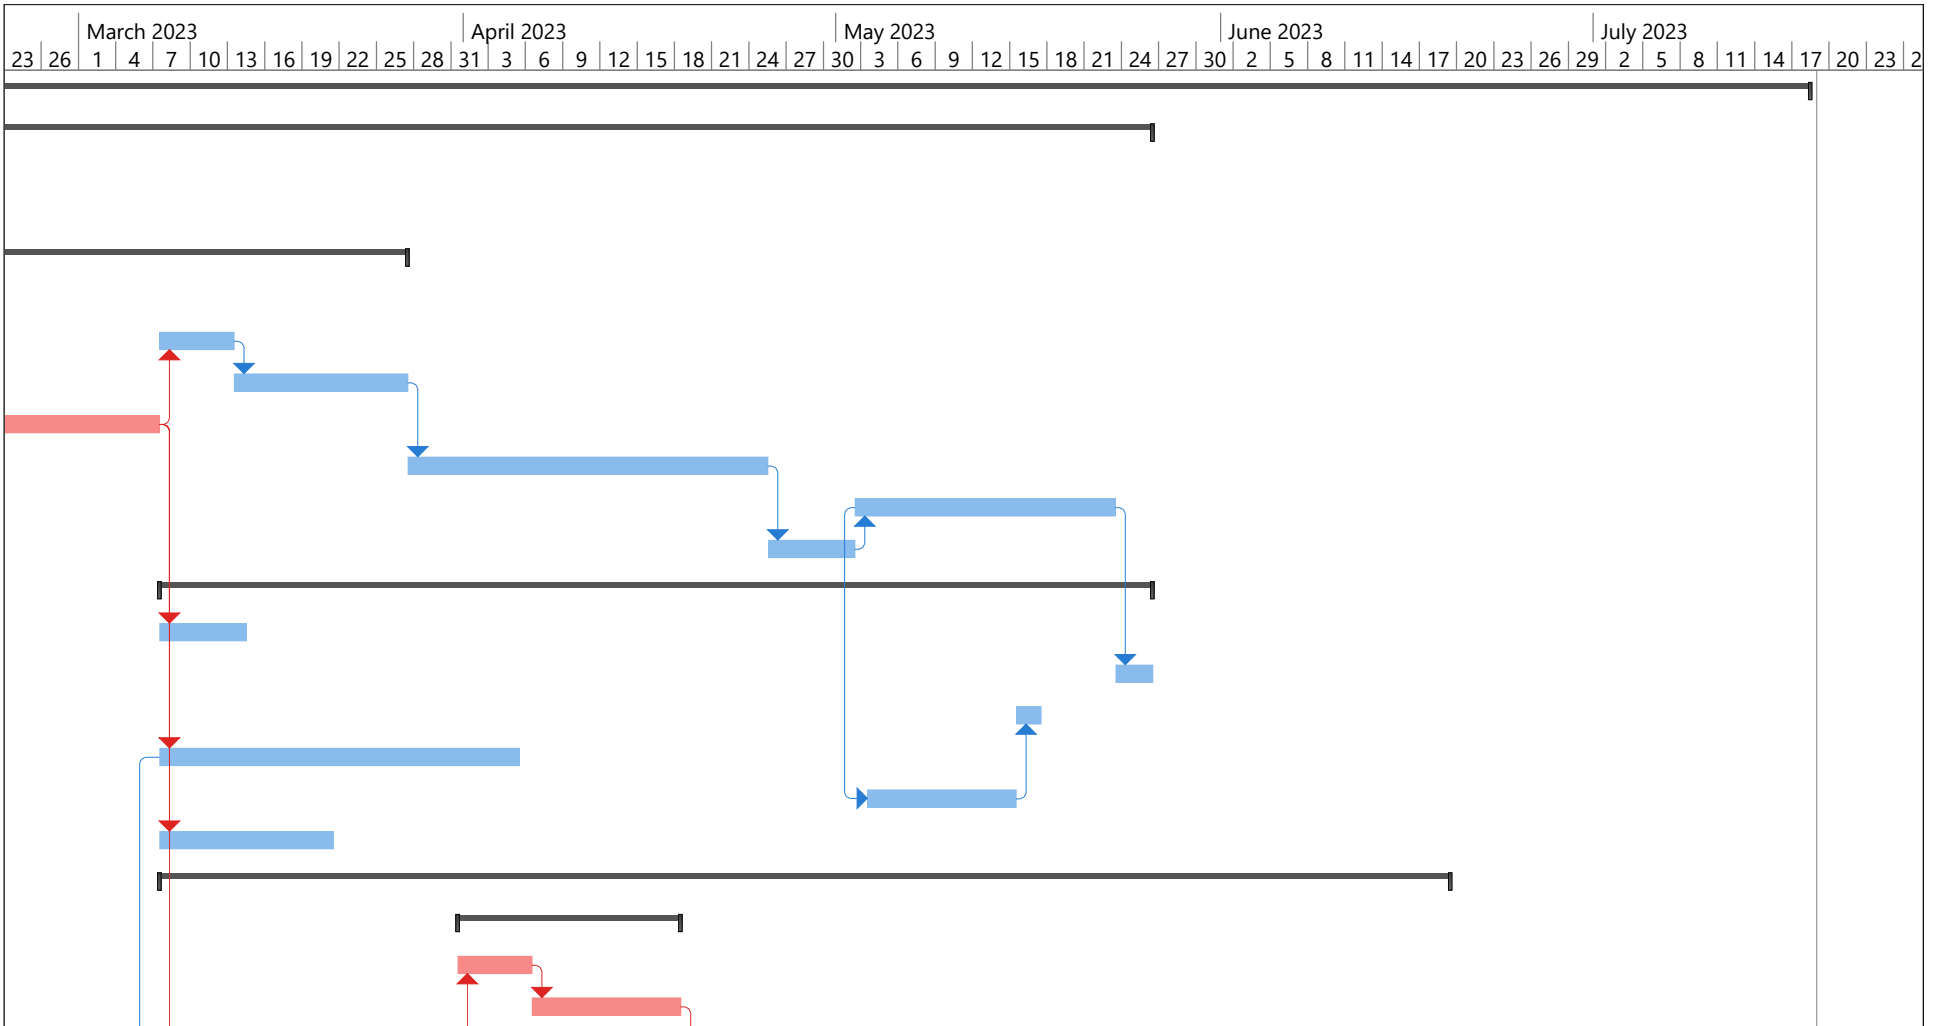

Project: Cronograma Santana a
Date: Mon 23/1/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

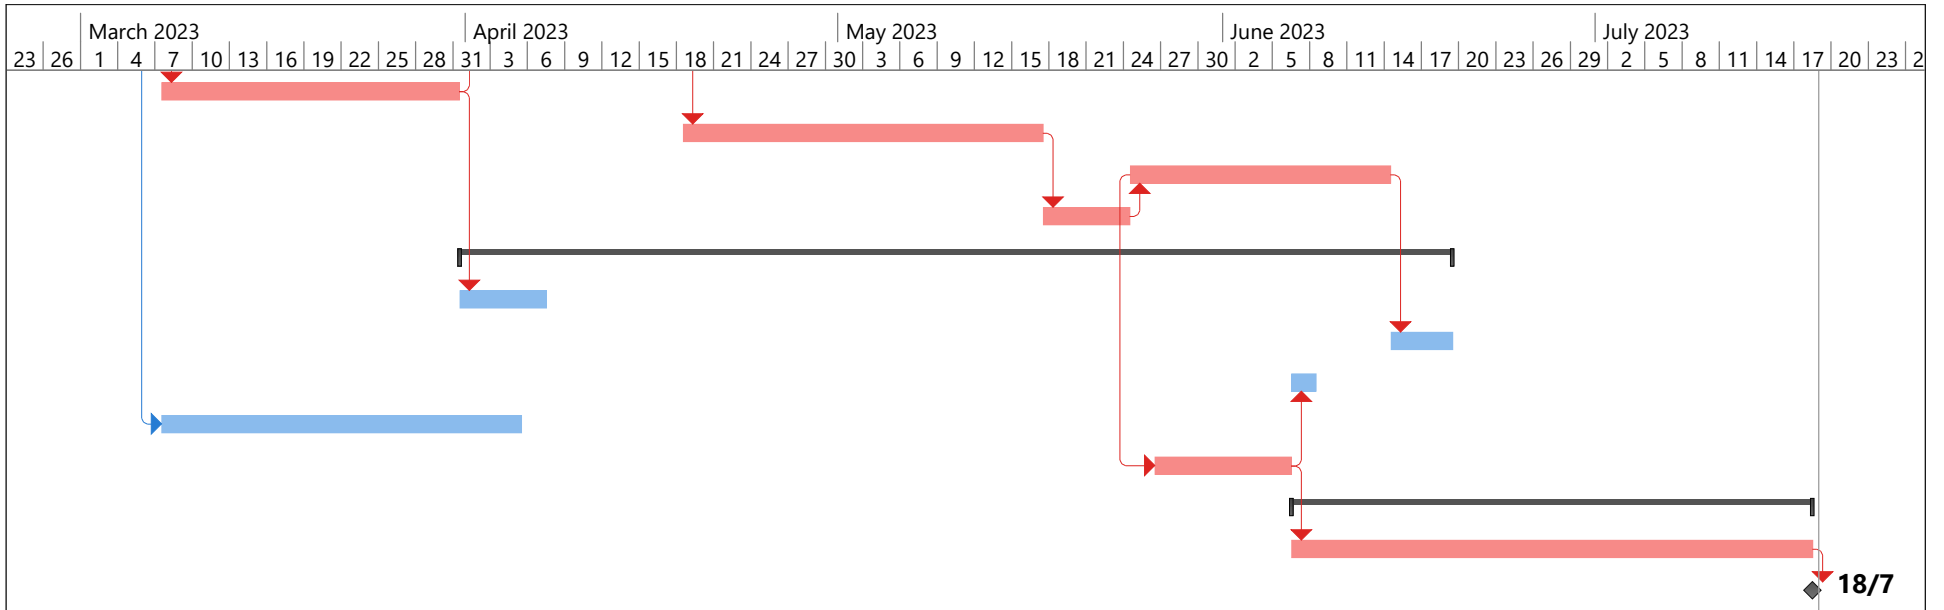

Project: Cronograma Santana a Date: Mon 23/1/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
